

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 8

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

1. WELL NAME
Dobby 1236-5MVH

2. TYPE OF WELL
Gas Well

3. TYPE OF WORK
DRILL NEW ☒ REENTER P&A ☐ DEEPEN ☐ RECOMP ☐

4. API NUMBER
4304757298

5. NAME OF OPERATOR
Middle Fork Energy Uinta, LLC

6. OPERATOR PHONE
435-828-2730

7. FIELD NAME
UNDESIGNATED

8. ADDRESS OF OPERATOR
1401 Wynkoop Street, Suite 300, Denver, CO, 80202

9. OPERATOR E-MAIL
jillj@kodaresh.com

10. UNIT NAME
KJ2

11. MINERAL LEASE NUMBER
MULTIPLE LEASES

12. MINERAL OWNERSHIP
FEDERAL

13. SURFACE OWNERSHIP
FEDERAL

14. COUNTY
UINTAH

15. DATE SPUDDED (SPUD RIG)
06/30/2024

16. DATE SPUDDED (ROTARY RIG)
06/30/2024

17. DATE TOTAL DEPTH REACHED
08/27/2024

18. DATE COMPLETED/ABANDONED
09/21/2024

19. DATE OF FIRST PROD. / INJ.
PROD:09/27/2024 INJ:

20. DEPTH REFERENCE
GROUND LEVEL ☐ KELLY BUSHING ☒ DERRICK FLOOR ☐

21. DEPTH REFERENCE ELEVATION
5373 (US Feet)

22. GRADED GROUND LEVEL ELEVATION
5347 (US Feet)

23. WELLBORE DEVIATION PROFILE
VERTICAL ☐ DIRECTIONAL ☐ HORIZONTAL ☒

24. TOTAL DEPTH
MD 18215 TVD 11984

25. PLUGGED BACK TOTAL DEPTH
MD 18215 TVD 11984

26. CURRENT WELL STATUS
Producing

27. LOCATION OF WELL									
WELL POSITION	FOOTAGES		QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN	UTM EASTING	UTM NORTHING
Surface	2402 FSL	2627 FWL	NESW	12	7.0 S	22.0 E	S	637118	4454010
Producing Interval Top	2265 FNL	2522 FWL	SEnw	12	7.0 S	22.0 E	S		
Producing Interval Bottom	2026 FNL	2371 FWL	LOT6	1	7.0 S	22.0 E	S		
Total Depth	2007 FNL	2417 FWL	LOT6	1	7.0 S	22.0 E	S		

28. HOLE, CASING AND CEMENT INFORMATION																
STRING	HOLE SIZE	CASING O.D.	WEIGHT	GRADE	THREAD	TOP (MD)	BOTTOM (MD)	DV TOOL DEPTH	LEAD TAIL	CEMENT TYPE	SACKS	YIELD	WEIGHT	CEMENT TOP	BASIS FOR TOP	
COND	24.0	16.0	42.05	X-52	LTC	0	146		L	Class G Cement	282	1.16	15.8	0		
SURF	12.25	9.625	40.0	L-80	LTC	0	4019		L	Class G Cement	780	2.89	11.5	0		
									T	Class G Cement	240	1.16	15.8			
INT	8.75	7.0	29.0	HCP-110	LTC	0	11765		L	Class G Cement	340	2.47	12.0	0		
									T	Class G Cement	110	1.15	15.8			
									L	Class G Cement	800	2.46	12.0	5468		
									T	Class G Cement	200	1.56	13.5			
PROD	6.125	4.5	15.1	P-110	BTC	11020	18212		L	Class G Cement	660	1.31	14.0	11020		

29. TUBING RECORD			
TUBING SIZE	TOP (MD)	BOT (MD)	PACKER DEPTH

30. RETRIEVABLE / TEMPORARY PLUGS		
PLUG	DEPTH (MD)	TYPE

31. PERMANENT / ABANDONMENT PLUGS		
PLUG	TOP (MD)	BOTTOM (MD)

32. FORMATION DETAILS and STRATIGRAPHIC MARKERS				
FR	FORMATION NAME	TOP (MD)	TOP (TVD)	DESCRIPTION, CONTENTS, ETC.
1	GREEN RIVER	3150	3150	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
2	BIRDS NEST	3354	3353	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
3	MAHOGANY	3990	3989	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
4	WASATCH	6624	6623	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
5	MESA VERDE	9556	9545	
	OIL SHOW? ☒ GAS SHOW? ☒ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☒ COMMINGLED? ☐			

33. COMPLETED and TESTED INTERVALS (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)
--

FR	TOP (MD)	BOTTOM (MD)	TOP (TVD)	BOTTOM (TVD)	STIMULATION TREATMENT	INTERVAL STATUS
5	11761	18142	11637	11983	Fracture Stimulated	PRODUCING

34A. PRODUCTION INFORMATION (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)									
FR	TOP (MD)	BOTTOM (MD)	DATE FIRST PROD.	TEST DATE	HRS. TESTED	TBG. PRESSURE	CSG. PRESSURE	PROD. METHOD	
5	11761	18142	09/27/2024	10/15/2024	24		529	Flowing	
	TEST PRODUCTION VOLUMES			24-HOUR PRODUCTION RATES			GAS-OIL RATIO	OIL API	GAS BTU
	OIL (BBL)	GAS (MSCF)	WATER (BBL)	OIL (BBL)	GAS (MSCF)	WATER (BBL)	175759	0.0	
	29	5097	1630	29	5097	1630			

35. WELL TREATMENTS (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)						
FR	TREATMENT TYPE	TOP (MD)	BOTTOM (MD)	START DATE	END DATE	AMOUNT AND TYPE OF MATERIAL
5	Fracture Stimulation	11761	18142	09/14/2024	09/21/2024	199,493 BBLs FRESH WATER - 6,413,290 LBS PROPPANT - 32 STAGES

36. LOGS, SURVEYS, AND REPORTS (PDF file of each and LAS file of logs if available are to be submitted.)								
REPORTS AND OTHER INFORMATION.								
Dx Survey ☒ DST Report ☐ Core Analysis ☐ DOGM Form 7 ☐ Geologic Report ☐ Wellbore Diagram ☐ Other ☐								
SUBMITTED PDF LOGS					SUBMITTED LAS LOGS			
MEASURED WHILE DRILLING, CEMENT BOND								

OGM Official Use Only

37. I hereby certify that the foregoing and attached information is complete as determined from all available records.		
NAME Karlyn Linarte	TITLE Permitting Tech - Uintah Group Permitting	DATE 11/07/2024
SIGNATURE N/A	PHONE 435-789-1017	EMAIL klinarte@uintahgroup.com



Middle Fork Daily Completion Activity Report

Well Name: DOBBY 1236-5MVH

API/UWI 4304757298	Surface Legal Location S12-T7S-R22E	Field Name UNDESIGNATED	License # UTU-011226	State/Province UTAH	Well Configuration Type HORIZONTAL
Ground Elevation (ft) 5,347.40	Casing Flange Elevation (ft) 5,345.32	KB-Ground Distance (ft) 26.00	KB-Casing Flange Distance (ft) 28.08	Surface Spud Date 6/30/2024 04:30	Rig Release Date 8/30/2024 18:00

Job Category COMPLETION			
Rpt #	Start Date	End Date	Summary
3.0	9/3/2024	9/4/2024	install Tubing Head
4.0	9/5/2024	9/6/2024	MIRU W/L RIH W/GR/JB
5.0	9/6/2024	9/7/2024	MIRU W/L RIH W/ CBL Log
6.0	9/7/2024	9/8/2024	MIRU Delsco Rig
7.0	9/8/2024	9/9/2024	NU BOPE/Test/Polish PBR/LD tubing
8.0	9/9/2024	9/10/2024	POOH/RDMOSU/
9.0	9/11/2024	9/12/2024	MIRUSU/NU BOPE/Test BOPE
10.0	9/12/2024	9/13/2024	TIH w/4 1/2" frac string
11.0	9/13/2024	9/14/2024	RDMOSU, N/U Frac Stack & Zipper Manifold.
12.0	9/14/2024	9/15/2024	MIRU Cal Frac, TWG & Straightline. Set 2 RBP Test & Chart Casing. Pull 2 RBP. Perf Stage 1 & Perform Defit.
13.0	9/15/2024	9/16/2024	Rig Up.
14.0	9/16/2024	9/17/2024	Frac stages 1-4, and begin stage-5 frac Perf stages 2-5
15.0	9/17/2024	9/18/2024	Frac Stages 5-10 Perf Stages 6-10
16.0	9/18/2024	9/19/2024	Frac Stages 11-15, Perf stages 11-16
17.0	9/19/2024	9/20/2024	Frac stages 16-21, Perf stages 17-21
18.0	9/20/2024	9/21/2024	Frac Stages 22-26 Begin Stage-27 Frac, Perf stages 22-27
19.0	9/21/2024	9/22/2024	Frac stages 27-32, Perf stages 28-32, and set Kill Plug.
20.0	9/22/2024	9/23/2024	RDMO all vendors.
21.0	9/23/2024	9/24/2024	Spot D/O Tanks & R/U 3" D/O pkg. R/U Prod Equip.
22.0	9/24/2024	9/25/2024	Swing reel onto CTU. Spot in coil equip.
23.0	9/25/2024	9/26/2024	Wait on hot spool to be delivered. N/D Wellhead. N/U hot spool & D/O assembly.
24.0	9/26/2024	9/27/2024	Pressure Test Hot Spool & D/O Tree. Finishing R/U Coil. D/O Plugs. Clean out to PBTD. Start Pooh W/BHA #1.
25.0	9/27/2024	9/28/2024	Continue Pooh W/BHA #1. Install Production Tree. Turn well over to production team.
26.0	9/29/2024	9/30/2024	Drain up all working tanks and release all rental equip.



UT Well Completion Report and Log

Well Name: DOBBY 1236-5MVH

Fluid Type GAS		Well Subtype NEW DRILL		Operator MIDDLE FORK ENERGY UINTA		Lease				
Surface Legal Location S12-T7S-R22E			North/South Distance (ft) 2,402.0		N/S Ref FSL	East/West Distance (ft) 2,627.0		E/W Ref FWL	Target Formation NESLEN UPPER	
Ground Elevation (ft) 5,347.40		KB-Ground Distance (ft) 26.00		Total Depth (All) (ftKB) ORIGINAL HOLE - 18,215.0		Total Depth All (TVD) (ftKB) ORIGINAL HOLE - 11,984.2			Well Name DOBBY 1236-5MVH	
Conductor Spud Date 6/11/2024			Surface Spud Date 6/30/2024			Rig Release Date 8/30/2024			API/UWI 4304757298	
									Field Name UNDESIGNATED	
TD Date		Frac Start Date		Completed Date		Initial Production Date				
End Date 8/27/2024		Date 9/14/2024		Date 9/21/2024		On Production Date				

Wellbores

Profile Type Horizontal	Actual Deviation Survey Table Deviation Survey
----------------------------	---

Casing Strings

Csg Des	Hole Size (in)	Casing OD (in)	Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
Conductor	24	16	X-52	42.05	29.4	146.0
Surface	12 1/4	9 5/8	HCL-80	40.00	29.4	4,019.0
Intermediate	8 3/4	7	HCP-110	29.00	29.4	11,765.0
Production Liner	6 1/8	4 1/2	P-110HP	15.10	11,020.0	18,212.0

Casing Components

Csg Des	Item Des	Top (ftKB)	Btm (ftKB)
Intermediate	Stage Tool	3,976.2	3,978.5

Cement Fluids

Casing Description	Stg #	Fluid Type	Class	Amount (sacks)	Yield (ft³/sack)	Density (lb/gal)	Final Top
Surface	1	Lead	G	780	2.89	11.50	29.4
Surface	1	Tail	G	240	1.16	15.80	3,533.0
Intermediate	1	Lead	G	800	2.46	12.00	5,468.0
Intermediate	1	Tail	G	200	1.56	13.50	9,700.0
Intermediate	2	Lead	G	340	2.47	12.00	29.4
Intermediate	2	Tail	G	110	1.15	15.80	3,200.0
Production Liner	1	Tail	G	660	1.31	14.00	11,020.0

Tubing Record:

String Max Nominal OD (in)	Tubing Set Depth (ftKB)	Tubing Land Date
----------------------------	-------------------------	------------------

Perforations

Formation	Top (ftKB)	Btm (ftKB)	Top (TVD) (ftKB)	Btm (TVD) (ftKB)	Est Hole Dia (in)	Shot Dens (shots/ft)	Sum of Calculated Shot Total	Current Status
NESLEN	11,761.0	11,942.0	11,636.9	11,689.7		3.0	30	Open - Flowing (11,761.0 - 11,762.0 ftKB)
NESLEN	11,961.0	12,142.0	11,692.1	11,705.2		3.0	30	Open - Flowing (11,961.0 - 11,962.0 ftKB)
NESLEN	12,161.0	12,342.0	11,706.0	11,719.7		3.0	30	Open - Flowing (12,301.0 - 12,302.0 ftKB)
NESLEN	12,361.0	12,542.0	11,721.2	11,732.1		3.0	30	Open - Flowing (12,361.0 - 12,362.0 ftKB)
NESLEN	12,561.0	12,742.0	11,733.0	11,749.5		3.0	30	Open - Flowing (12,561.0 - 12,562.0 ftKB)
NESLEN	12,761.0	12,942.0	11,751.4	11,760.7		3.0	30	Open - Flowing (12,761.0 - 12,762.0 ftKB)
NESLEN	12,961.0	13,142.0	11,761.3	11,769.4		3.0	30	Open - Flowing (12,961.0 - 12,962.0 ftKB)
NESLEN	13,161.0	13,342.0	11,769.7	11,774.8		3.0	30	Open - Flowing (13,161.0 - 13,162.0 ftKB)
NESLEN	13,361.0	13,542.0	11,775.6	11,783.2		3.0	30	Open - Flowing (13,361.0 - 13,362.0 ftKB)
NESLEN	13,561.0	13,742.0	11,784.1	11,793.3		3.0	30	Open - Flowing (13,561.0 - 13,562.0 ftKB)
NESLEN	13,761.0	13,942.0	11,794.2	11,803.3		3.0	30	Open - Flowing (13,761.0 - 13,762.0 ftKB)
NESLEN	13,961.0	14,142.0	11,804.0	11,810.4		3.0	30	Open - Flowing (13,961.0 - 13,962.0 ftKB)
NESLEN	14,161.0	14,344.0	11,810.6	11,817.3		3.0	30	Open - Flowing (14,161.0 - 14,162.0 ftKB)
NESLEN	14,361.0	14,542.0	11,818.0	11,826.0		3.0	30	Open - Flowing (14,361.0 - 14,362.0 ftKB)
NESLEN	14,561.0	14,742.0	11,826.6	11,831.1		3.0	30	Open - Flowing (14,561.0 - 14,562.0 ftKB)
NESLEN	14,761.0	14,942.0	11,831.8	11,839.3		3.0	30	Open - Flowing (14,761.0 - 14,762.0 ftKB)
NESLEN	14,961.0	15,142.0	11,840.3	11,855.6		3.0	30	Open - Flowing (14,961.0 - 14,962.0 ftKB)
NESLEN	15,159.0	15,342.0	11,857.1	11,870.2		3.0	30	Open - Flowing (15,159.0 - 15,160.0 ftKB)
NESLEN	15,361.0	15,542.0	11,871.3	11,877.6		3.0	30	Open - Flowing (15,361.0 - 15,362.0 ftKB)
NESLEN	15,561.0	15,742.0	11,878.4	11,887.0		3.0	30	Open - Flowing (15,561.0 - 15,562.0 ftKB)
NESLEN	15,761.0	15,942.0	11,887.6	11,894.0		3.0	30	Open - Flowing (15,761.0 - 15,762.0 ftKB)
NESLEN	15,961.0	16,142.0	11,894.9	11,908.8		3.0	30	Open - Flowing (15,961.0 - 15,962.0 ftKB)



UT Well Completion Report and Log

Well Name: DOBBY 1236-5MVH

Fluid Type GAS		Well Subtype NEW DRILL		Operator MIDDLE FORK ENERGY UINTA		Lease	
Surface Legal Location S12-T7S-R22E		North/South Distance (ft) 2,402.0		N/S Ref FSL		East/West Distance (ft) 2,627.0	
E/W Ref FWL		Target Formation NESLEN UPPER		Well Name DOBBY 1236-5MVH		API/UWI 4304757298	
Ground Elevation (ft) 5,347.40		KB-Ground Distance (ft) 26.00		Total Depth (All) (ftKB) ORIGINAL HOLE - 18,215.0		Total Depth (TVD) (ftKB) ORIGINAL HOLE - 11,984.2	
Conductor Spud Date 6/11/2024		Surface Spud Date 6/30/2024		Rig Release Date 8/30/2024		Field Name UNDESIGNATED	
TD Date End Date 8/27/2024		Frac Start Date Date 9/14/2024		Completed Date Date 9/21/2024		Initial Production Date On Production Date	

Perforations

Formation	Top (ftKB)	Btm (ftKB)	Top (TVD) (ftKB)	Btm (TVD) (ftKB)	Est Hole Dia (in)	Shot Dens (shots/ft)	Sum of Calculated Shot Total	Current Status
NESLEN	16,161.0	16,342.0	11,910.4	11,924.6		3.0	30	Open - Flowing (16,161.0 - 16,162.0 ftKB)
NESLEN	16,361.0	16,542.0	11,925.9	11,939.4		3.0	30	Open - Flowing (16,361.0 - 16,362.0 ftKB)
NESLEN	16,559.0	16,742.0	11,940.8	11,952.2		3.0	30	Open - Flowing (15,559.0 - 15,560.0 ftKB)
NESLEN	16,761.0	16,942.0	11,953.0	11,959.9		3.0	30	Open - Flowing (16,761.0 - 16,762.0 ftKB)
NESLEN	16,961.0	17,142.0	11,960.4	11,967.2		3.0	30	Open - Flowing (16,961.0 - 16,962.0 ftKB)
NESLEN	17,161.0	17,342.0	11,968.0	11,972.7		3.0	30	Open - Flowing (17,161.0 - 17,162.0 ftKB)
NESLEN	17,361.0	17,542.0	11,973.0	11,973.8		3.0	30	Open - Flowing (17,361.0 - 17,362.0 ftKB)
NESLEN	17,561.0	17,742.0	11,973.7	11,975.7		3.0	30	Open - Flowing (17,561.0 - 17,562.0 ftKB)
NESLEN	17,761.0	17,942.0	11,976.1	11,978.1		3.0	30	Open - Flowing (17,761.0 - 17,762.0 ftKB)
NESLEN	17,961.0	18,142.0	11,978.3	11,982.9		3.0	30	Open - Flowing (17,961.0 - 17,962.0 ftKB)
Total							960	

Producing Intervals & Perforation Record:

Minimum of Top Depth (ftKB) 11,761.0	Maximum of Bottom Depth (ftKB) 18,142.0
---	--

Acid, Fracture, Treatment, Cement Squeeze, Etc.:

Type Hydraulic Frac	Number of Treatment Intervals 32	Volume Clean Total (bbl) 199,492.54	Proppant Total (lb) 6,413,290.0
Type	Sand Size		

Fluid Name
Slickwater

Plug Back Total Depths

Depth (ftKB)	Depth (TVD) (ftKB)
--------------	--------------------

Zones

Zone Name	Top (ftKB)	Btm (ftKB)	Final Top (ftKB)
Neslen Lower			
Neslen Upper	11,705.0		
Neslen Lower	11,761.0	18,142.0	

Formations

Formation Name	Final Top MD (ftKB)
GREEN RIVER	3,150.0
BIRDS NEST	3,354.0
MAHOGANY	3,990.0
WASATCH	6,624.0
MESAVERDE	9,556.0
NESLEN	11,704.0



Survey Certification

7327 West Barton Road
Casper, WY 82604
(307)-472-6621

Operator	<u>Middle Fork Energy Partners</u>
Well Name & No.	<u>Dobby 1236-5MVH</u>
County & State	<u>Uintah, UT</u>
SDI Job #	<u>OP.045066</u>
Rig	<u>Cyclone 34</u>
Survey Date	<u>6/30/2024 to 8/27/2024</u>
GL & KB Elevation	<u>GL 5347.4' & KB 26' = 5373.4'</u>

I, Janie Collins, having personal knowledge of all the facts, hereby
certify that the attached directional survey run from a measured depth of 213 feet to a
measured depth of 18,215 feet is true and correct as determined from all available records.

A handwritten signature in blue ink, appearing to read 'Janie Collins', written over a horizontal line.

Signature

30-Aug-2024

Date

Janie Collins


Rockies Region Well Planner
Scientific Drilling - Rocky Mountain District



WELL DETAILS: Dobby 1236-5MVH



		GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)	5347.40
+N/-S	+E/-W	Northing	Easting
0.00	0.00	7257751.79	2229966.29
		Latitude	Longitude
		40.2253018	-109.3883747

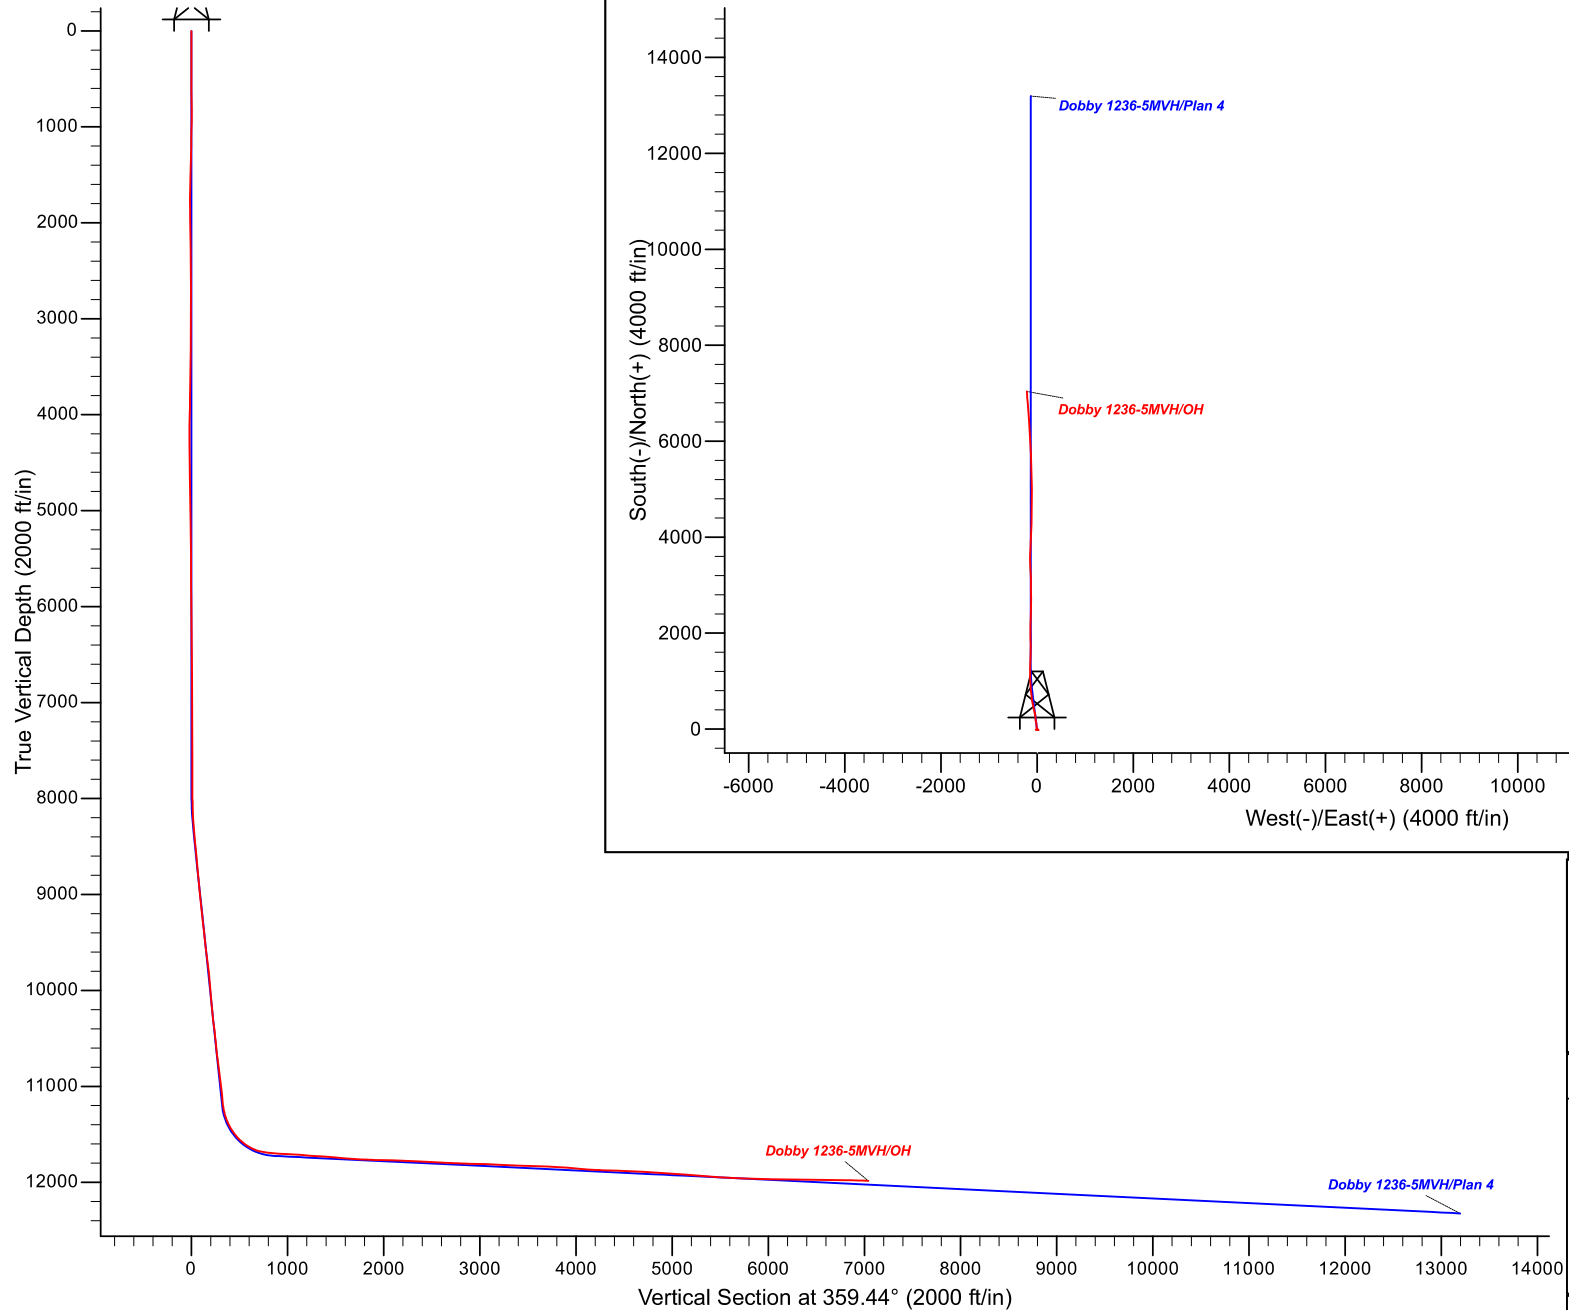

Company Name: Middle Fork Energy Uinta, LLC
Project: Uintah County, UT
Site: Dobby 33-12-722 Pad
Well: Dobby 1236-5MVH
Wellbore: OH

PROJECT DETAILS: Uintah County, UT

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: Utah Central Zone

System Datum: Mean Sea Level
Local North: True

Created By: Janie Collins Date: 10:03, August 30 2024



Middle Fork Energy Uinta, LLC

Uintah County, UT
Dobby 33-12-722 Pad
Dobby 1236-5MVH

OH

Design: OH

Standard Survey Report

30 August, 2024



www.scientificdrilling.com



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-5MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-5MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Project	Uintah County, UT		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	Utah Central Zone		

Site		Dobby 33-12-722 Pad			
Site Position:		Northing:	7,257,751.79 usft	Latitude:	40.2253018
From:	Map	Easting:	2,229,966.29 usft	Longitude:	-109.3883747
Position Uncertainty:	0.00 ft	Slot Radius:	13.200 in	Grid Convergence:	1.35 °

Well		Dobby 1236-5MVH				
Well Position	+N/-S	0.00 ft	Northing:	7,257,751.79 usft	Latitude:	40.2253018
	+E/-W	0.00 ft	Easting:	2,229,966.29 usft	Longitude:	-109.3883747
Position Uncertainty		0.00 ft	Wellhead Elevation:	ft	Ground Level:	5,347.40 ft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM2024	6/25/2024	9.70	65.82	50,881.70000000
	HDGM2024	8/15/2024	9.68	65.82	50,862.90000000

Design	OH				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)	
	0.00	0.00	0.00		359.44

Survey Program		Date	8/30/2024		
From (ft)	To (ft)	Survey (Wellbore)	Tool Name	Description	
26.00	3,964.00	Survey #1 - Surface (OH)	MWD+HDGM	OWSG MWD + HDGM	
4,104.00	11,113.00	Survey #2 - Intermediate (OH)	MWD+HDGM	OWSG MWD + HDGM	
11,149.00	11,984.00	Survey #3 - Curve (OH)	MWD+HDGM	OWSG MWD + HDGM	
12,078.00	18,215.00	Survey #4 - Lateral (OH)	MWD+HDGM	OWSG MWD + HDGM	

Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
26.00	0.00	0.00	26.00	0.00	0.00	0.00	0.00	0.00	0.00
213.00	1.35	254.08	212.98	-0.60	-2.12	-0.58	0.72	0.72	0.00
304.00	1.36	271.33	303.96	-0.87	-4.23	-0.83	0.45	0.01	18.96
395.00	1.40	271.53	394.93	-0.82	-6.42	-0.76	0.04	0.04	0.22
485.00	1.41	267.76	484.90	-0.83	-8.63	-0.75	0.10	0.01	-4.19
575.00	1.38	284.87	574.88	-0.60	-10.78	-0.49	0.46	-0.03	19.01



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-5MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-5MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
665.00	1.29	290.71	664.85	0.04	-12.77	0.16	0.18	-0.10	6.49
756.00	1.39	281.14	755.83	0.61	-14.82	0.76	0.27	0.11	-10.52
846.00	1.36	280.48	845.80	1.02	-16.94	1.18	0.04	-0.03	-0.73
936.00	0.58	204.85	935.79	0.80	-18.18	0.98	1.49	-0.87	-84.03
1,027.00	0.95	162.89	1,026.78	-0.34	-18.15	-0.16	0.71	0.41	-46.11
1,118.00	1.21	169.01	1,117.77	-2.00	-17.74	-1.83	0.31	0.29	6.73
1,212.00	1.03	175.72	1,211.75	-3.82	-17.49	-3.65	0.24	-0.19	7.14
1,303.00	1.44	159.19	1,302.73	-5.70	-17.03	-5.54	0.59	0.45	-18.16
1,394.00	1.42	166.02	1,393.70	-7.87	-16.35	-7.71	0.19	-0.02	7.51
1,484.00	1.63	161.51	1,483.67	-10.16	-15.67	-10.01	0.27	0.23	-5.01
1,576.00	1.43	161.86	1,575.64	-12.49	-14.90	-12.35	0.22	-0.22	0.38
1,671.00	1.45	163.36	1,670.61	-14.77	-14.19	-14.63	0.04	0.02	1.58
1,765.00	0.41	148.78	1,764.59	-16.20	-13.67	-16.07	1.13	-1.11	-15.51
1,859.00	0.94	29.82	1,858.59	-15.82	-13.11	-15.69	1.27	0.56	-126.55
1,953.00	1.17	32.06	1,952.57	-14.34	-12.22	-14.22	0.25	0.24	2.38
2,048.00	1.11	25.30	2,047.55	-12.68	-11.31	-12.57	0.15	-0.06	-7.12
2,143.00	0.96	21.50	2,142.54	-11.11	-10.63	-11.01	0.17	-0.16	-4.00
2,238.00	0.81	32.60	2,237.53	-9.80	-9.97	-9.71	0.24	-0.16	11.68
2,332.00	0.79	49.72	2,331.52	-8.83	-9.12	-8.74	0.25	-0.02	18.21
2,427.00	0.82	55.96	2,426.51	-8.02	-8.06	-7.94	0.10	0.03	6.57
2,522.00	1.08	74.85	2,521.50	-7.41	-6.63	-7.34	0.42	0.27	19.88
2,616.00	0.89	79.94	2,615.48	-7.05	-5.06	-7.00	0.22	-0.20	5.41
2,709.00	0.89	72.11	2,708.47	-6.70	-3.66	-6.66	0.13	0.00	-8.42
2,804.00	0.90	71.21	2,803.46	-6.23	-2.25	-6.21	0.02	0.01	-0.95
2,899.00	0.85	78.38	2,898.45	-5.85	-0.85	-5.84	0.13	-0.05	7.55
2,994.00	0.80	102.26	2,993.44	-5.85	0.48	-5.85	0.36	-0.05	25.14
3,085.00	1.04	114.58	3,084.43	-6.33	1.86	-6.35	0.34	0.26	13.54
3,178.00	1.31	107.36	3,177.41	-7.00	3.64	-7.03	0.33	0.29	-7.76
3,273.00	1.25	119.16	3,272.38	-7.83	5.58	-7.88	0.28	-0.06	12.42
3,367.00	1.49	111.83	3,366.36	-8.78	7.61	-8.85	0.32	0.26	-7.80
3,462.00	1.74	113.85	3,461.32	-9.82	10.08	-9.92	0.27	0.26	2.13
3,557.00	1.82	116.88	3,556.27	-11.09	12.74	-11.21	0.13	0.08	3.19
3,652.00	1.94	116.29	3,651.22	-12.48	15.53	-12.63	0.13	0.13	-0.62
3,746.00	1.96	121.41	3,745.17	-14.02	18.33	-14.20	0.19	0.02	5.45
3,840.00	1.93	121.97	3,839.11	-15.70	21.04	-15.90	0.04	-0.03	0.60
3,935.00	1.86	117.63	3,934.06	-17.26	23.76	-17.49	0.17	-0.07	-4.57
3,964.00	1.82	119.66	3,963.05	-17.71	24.58	-17.95	0.26	-0.14	7.00
4,104.00	1.62	119.14	4,102.98	-19.77	28.24	-20.05	0.14	-0.14	-0.37
4,197.00	0.41	311.51	4,195.97	-20.19	29.14	-20.47	2.17	-1.30	-180.25
4,290.00	0.18	18.80	4,288.97	-19.83	28.94	-20.11	0.41	-0.25	72.35
4,384.00	0.20	315.46	4,382.97	-19.58	28.87	-19.86	0.21	0.02	-67.38
4,479.00	0.50	225.55	4,477.97	-19.75	28.46	-20.02	0.57	0.32	-94.64
4,574.00	1.10	305.35	4,572.96	-19.51	27.42	-19.78	1.18	0.63	84.00



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-5MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-5MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
4,667.00	2.46	307.96	4,665.92	-17.77	25.12	-18.01	1.46	1.46	2.81
4,759.00	2.26	305.51	4,757.84	-15.50	22.08	-15.71	0.24	-0.22	-2.66
4,852.00	2.10	299.57	4,850.77	-13.59	19.11	-13.78	0.30	-0.17	-6.39
4,947.00	1.91	304.00	4,945.71	-11.85	16.28	-12.01	0.26	-0.20	4.66
5,041.00	1.73	299.02	5,039.66	-10.28	13.74	-10.42	0.25	-0.19	-5.30
5,136.00	1.61	298.15	5,134.62	-8.96	11.31	-9.07	0.13	-0.13	-0.92
5,230.00	1.07	299.00	5,228.60	-7.91	9.38	-8.00	0.57	-0.57	0.90
5,324.00	0.78	287.51	5,322.59	-7.29	8.00	-7.37	0.36	-0.31	-12.22
5,419.00	0.40	271.31	5,417.58	-7.09	7.05	-7.16	0.43	-0.40	-17.05
5,514.00	0.58	318.10	5,512.58	-6.72	6.40	-6.79	0.44	0.19	49.25
5,609.00	0.81	326.52	5,607.57	-5.81	5.71	-5.86	0.26	0.24	8.86
5,703.00	0.53	343.98	5,701.56	-4.83	5.22	-4.88	0.37	-0.30	18.57
5,797.00	0.48	348.55	5,795.56	-4.03	5.03	-4.08	0.07	-0.05	4.86
5,891.00	0.55	4.24	5,889.56	-3.19	4.98	-3.24	0.17	0.07	16.69
5,986.00	0.71	345.58	5,984.55	-2.17	4.87	-2.22	0.27	0.17	-19.64
6,081.00	0.59	315.51	6,079.55	-1.25	4.38	-1.29	0.38	-0.13	-31.65
6,176.00	0.77	307.04	6,174.54	-0.52	3.53	-0.55	0.22	0.19	-8.92
6,269.00	0.81	320.14	6,267.53	0.36	2.61	0.34	0.20	0.04	14.09
6,362.00	0.62	314.28	6,360.52	1.22	1.82	1.20	0.22	-0.20	-6.30
6,456.00	0.75	324.69	6,454.52	2.08	1.11	2.07	0.19	0.14	11.07
6,551.00	0.51	321.89	6,549.51	2.92	0.48	2.91	0.25	-0.25	-2.95
6,645.00	0.77	359.70	6,643.50	3.88	0.22	3.88	0.51	0.28	40.22
6,740.00	0.29	352.05	6,738.50	4.75	0.19	4.75	0.51	-0.51	-8.05
6,835.00	0.34	351.94	6,833.50	5.27	0.11	5.27	0.05	0.05	-0.12
6,930.00	0.37	36.59	6,928.50	5.80	0.26	5.79	0.29	0.03	47.00
7,025.00	0.45	35.22	7,023.49	6.35	0.66	6.34	0.08	0.08	-1.44
7,119.00	0.61	27.67	7,117.49	7.09	1.10	7.08	0.19	0.17	-8.03
7,214.00	0.39	39.87	7,212.49	7.79	1.54	7.77	0.26	-0.23	12.84
7,308.00	0.40	48.90	7,306.48	8.25	1.99	8.23	0.07	0.01	9.61
7,403.00	0.27	53.36	7,401.48	8.60	2.42	8.58	0.14	-0.14	4.69
7,498.00	0.34	335.69	7,496.48	8.99	2.49	8.97	0.41	0.07	-81.76
7,592.00	0.28	301.83	7,590.48	9.37	2.18	9.35	0.20	-0.06	-36.02
7,618.00	0.12	280.34	7,616.48	9.41	2.10	9.38	0.67	-0.62	-82.65
7,712.00	0.24	233.78	7,710.48	9.31	1.84	9.29	0.19	0.13	-49.53
7,806.00	0.38	72.13	7,804.48	9.29	1.98	9.27	0.65	0.15	-171.97
7,901.00	0.34	93.82	7,899.48	9.36	2.56	9.34	0.15	-0.04	22.83
7,995.00	0.58	3.16	7,993.48	9.82	2.87	9.79	0.72	0.26	-96.45
8,090.00	1.95	335.71	8,088.45	11.77	2.23	11.75	1.54	1.44	-28.89
8,185.00	3.02	327.27	8,183.36	15.35	0.21	15.35	1.19	1.13	-8.88
8,276.00	4.44	341.76	8,274.17	20.71	-2.19	20.74	1.86	1.56	15.92
8,371.00	5.43	342.66	8,368.81	28.50	-4.68	28.54	1.05	1.04	0.95
8,465.00	5.66	349.17	8,462.38	37.30	-6.88	37.36	0.71	0.24	6.93
8,559.00	5.79	356.07	8,555.91	46.58	-8.07	46.66	0.74	0.14	7.34
8,654.00	4.96	0.54	8,650.49	55.47	-8.36	55.55	0.98	-0.87	4.71



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-5MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-5MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
8,749.00	4.89	359.76	8,745.14	63.62	-8.34	63.70	0.10	-0.07	-0.82
8,844.00	5.07	359.40	8,839.78	71.87	-8.40	71.95	0.19	0.19	-0.38
8,939.00	5.43	352.56	8,934.38	80.52	-9.03	80.61	0.76	0.38	-7.20
9,033.00	6.02	347.33	9,027.91	89.74	-10.69	89.84	0.84	0.63	-5.56
9,125.00	5.68	347.11	9,119.43	98.89	-12.76	99.01	0.37	-0.37	-0.24
9,220.00	5.94	352.40	9,213.95	108.34	-14.46	108.48	0.63	0.27	5.57
9,315.00	7.27	350.64	9,308.31	119.15	-16.09	119.30	1.42	1.40	-1.85
9,409.00	6.68	352.60	9,401.62	130.44	-17.76	130.60	0.68	-0.63	2.09
9,502.00	5.56	353.06	9,494.09	140.27	-19.00	140.45	1.21	-1.20	0.49
9,597.00	7.60	347.50	9,588.46	150.98	-20.91	151.17	2.25	2.15	-5.85
9,692.00	7.98	346.27	9,682.58	163.52	-23.84	163.74	0.44	0.40	-1.29
9,786.00	6.92	340.95	9,775.79	175.21	-27.24	175.47	1.34	-1.13	-5.66
9,881.00	5.17	356.67	9,870.26	184.89	-29.35	185.17	2.52	-1.84	16.55
9,976.00	4.62	357.82	9,964.91	192.99	-29.75	193.27	0.59	-0.58	1.21
10,071.00	4.36	356.12	10,059.62	200.41	-30.14	200.70	0.31	-0.27	-1.79
10,166.00	5.01	356.24	10,154.30	208.16	-30.65	208.45	0.68	0.68	0.13
10,261.00	5.82	354.42	10,248.88	217.09	-31.39	217.39	0.87	0.85	-1.92
10,355.00	7.77	357.04	10,342.22	228.18	-32.19	228.48	2.10	2.07	2.79
10,450.00	6.67	357.29	10,436.46	240.10	-32.78	240.41	1.16	-1.16	0.26
10,545.00	5.64	356.76	10,530.91	250.28	-33.30	250.59	1.09	-1.08	-0.56
10,640.00	5.81	353.45	10,625.44	259.71	-34.12	260.04	0.39	0.18	-3.48
10,734.00	7.82	348.50	10,718.77	270.71	-35.93	271.05	2.23	2.14	-5.27
10,829.00	7.85	350.52	10,812.88	283.44	-38.29	283.80	0.29	0.03	2.13
10,924.00	7.40	350.25	10,907.04	295.87	-40.39	296.25	0.48	-0.47	-0.28
11,019.00	6.43	351.92	11,001.35	307.17	-42.18	307.56	1.04	-1.02	1.76
11,113.00	5.44	352.27	11,094.85	316.79	-43.52	317.20	1.05	-1.05	0.37
11,149.00	5.35	351.47	11,130.69	320.14	-44.00	320.56	0.33	-0.25	-2.22
11,217.00	6.97	350.27	11,198.29	327.35	-45.16	327.77	2.39	2.38	-1.76
11,311.00	15.39	346.66	11,290.43	345.14	-49.01	345.60	8.98	8.96	-3.84
11,404.00	24.80	347.57	11,377.67	376.26	-56.07	376.79	10.12	10.12	0.98
11,499.00	33.94	346.10	11,460.37	421.56	-66.76	422.19	9.65	9.62	-1.55
11,591.00	42.49	348.57	11,532.59	477.05	-79.11	477.80	9.44	9.29	2.68
11,684.00	52.74	348.59	11,595.20	544.29	-92.69	545.17	11.02	11.02	0.02
11,723.00	57.47	349.58	11,617.50	575.69	-98.74	576.63	12.31	12.13	2.54
11,797.00	64.50	352.84	11,653.38	639.60	-108.56	640.63	10.25	9.50	4.41
11,828.00	69.73	354.13	11,665.43	667.97	-111.79	669.03	17.30	16.87	4.16
11,859.00	74.91	354.58	11,674.85	697.35	-114.69	698.44	16.77	16.71	1.45
11,890.00	79.09	353.57	11,681.82	727.39	-117.81	728.51	13.85	13.48	-3.26
11,922.00	81.98	352.79	11,687.08	758.73	-121.56	759.88	9.35	9.03	-2.44
11,984.00	84.14	354.26	11,694.57	819.87	-128.50	821.09	4.20	3.48	2.37
12,078.00	86.74	356.74	11,702.04	913.27	-135.84	914.56	3.82	2.77	2.64
12,172.00	87.98	358.15	11,706.37	1,007.08	-140.03	1,008.40	2.00	1.32	1.50
12,265.00	84.25	359.53	11,712.67	1,099.82	-141.91	1,101.16	4.28	-4.01	1.48



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-5MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-5MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
12,359.00	85.49	359.98	11,721.08	1,193.44	-142.31	1,194.78	1.40	1.32	0.48
12,454.00	86.61	1.69	11,727.62	1,288.20	-140.93	1,289.52	2.15	1.18	1.80
12,547.00	87.61	1.56	11,732.31	1,381.05	-138.29	1,382.33	1.08	1.08	-0.14
12,641.00	84.25	1.12	11,738.98	1,474.77	-136.10	1,476.03	3.60	-3.57	-0.47
12,734.00	83.78	1.01	11,748.68	1,567.25	-134.38	1,568.49	0.52	-0.51	-0.12
12,828.00	86.21	359.34	11,756.88	1,660.88	-134.10	1,662.11	3.13	2.59	-1.78
12,921.00	89.46	358.91	11,760.39	1,753.79	-135.52	1,755.03	3.53	3.49	-0.46
13,015.00	86.11	359.11	11,764.03	1,847.69	-137.14	1,848.94	3.57	-3.56	0.21
13,034.00	85.90	358.43	11,765.35	1,866.64	-137.55	1,867.89	3.74	-1.11	-3.58
13,129.00	89.36	0.12	11,769.28	1,961.53	-138.75	1,962.80	4.05	3.64	1.78
13,223.00	88.72	359.88	11,770.85	2,055.52	-138.75	2,056.78	0.73	-0.68	-0.26
13,316.00	87.68	1.20	11,773.77	2,148.47	-137.87	2,149.71	1.81	-1.12	1.42
13,410.00	87.78	2.43	11,777.50	2,242.34	-134.90	2,243.55	1.31	0.11	1.31
13,505.00	87.45	3.30	11,781.45	2,337.14	-130.15	2,338.30	0.98	-0.35	0.92
13,598.00	86.94	2.37	11,786.00	2,429.91	-125.56	2,431.03	1.14	-0.55	-1.00
13,692.00	87.11	0.77	11,790.88	2,523.75	-122.99	2,524.83	1.71	0.18	-1.70
13,786.00	87.45	0.70	11,795.34	2,617.64	-121.78	2,618.70	0.37	0.36	-0.07
13,880.00	86.61	358.74	11,800.21	2,711.50	-122.24	2,712.57	2.27	-0.89	-2.09
13,974.00	88.26	0.06	11,804.42	2,805.40	-123.22	2,806.47	2.25	1.76	1.40
14,068.00	87.31	358.87	11,808.05	2,899.32	-124.10	2,900.40	1.62	-1.01	-1.27
14,161.00	89.56	359.88	11,810.59	2,992.27	-125.11	2,993.35	2.65	2.42	1.09
14,255.00	87.25	358.69	11,813.21	3,086.22	-126.28	3,087.31	2.76	-2.46	-1.27
14,350.00	87.52	358.39	11,817.54	3,181.09	-128.70	3,182.20	0.42	0.28	-0.32
14,443.00	87.15	356.20	11,821.87	3,273.88	-133.09	3,275.03	2.39	-0.40	-2.35
14,537.00	88.02	356.70	11,825.83	3,367.62	-138.90	3,368.81	1.07	0.93	0.53
14,630.00	89.13	358.54	11,828.14	3,460.50	-142.76	3,461.73	2.31	1.19	1.98
14,723.00	88.09	1.16	11,830.40	3,553.47	-143.00	3,554.69	3.03	-1.12	2.82
14,817.00	87.01	1.60	11,834.42	3,647.35	-140.74	3,648.55	1.24	-1.15	0.47
14,910.00	88.42	2.05	11,838.12	3,740.23	-137.78	3,741.40	1.59	1.52	0.48
15,004.00	85.32	3.12	11,843.26	3,833.98	-133.55	3,835.10	3.49	-3.30	1.14
15,098.00	84.52	2.05	11,851.58	3,927.51	-129.33	3,928.59	1.42	-0.85	-1.14
15,193.00	85.37	2.49	11,859.95	4,022.07	-125.58	4,023.10	1.01	0.89	0.46
15,287.00	86.24	2.12	11,866.83	4,115.74	-121.81	4,116.73	1.01	0.93	-0.39
15,381.00	86.94	1.39	11,872.42	4,209.53	-118.94	4,210.49	1.07	0.74	-0.78
15,475.00	88.99	1.54	11,875.76	4,303.43	-116.54	4,304.37	2.19	2.18	0.16
15,569.00	87.32	1.35	11,878.78	4,397.35	-114.17	4,398.26	1.79	-1.78	-0.20
15,663.00	86.88	0.54	11,883.54	4,491.22	-112.62	4,492.10	0.98	-0.47	-0.86
15,757.00	88.32	1.07	11,887.47	4,585.12	-111.30	4,585.99	1.63	1.53	0.56
15,852.00	88.02	1.12	11,890.51	4,680.06	-109.48	4,680.90	0.32	-0.32	0.05
15,946.00	87.52	0.67	11,894.17	4,773.97	-108.02	4,774.80	0.72	-0.53	-0.48
16,039.00	85.35	0.52	11,899.95	4,866.78	-107.05	4,867.60	2.34	-2.33	-0.16
16,133.00	84.88	0.26	11,907.95	4,960.44	-106.41	4,961.24	0.57	-0.50	-0.28
16,226.00	85.19	359.62	11,916.00	5,053.09	-106.51	5,053.89	0.76	0.33	-0.69



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-5MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-5MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
16,321.00	86.13	359.49	11,923.19	5,147.81	-107.25	5,148.61	1.00	0.99	-0.14
16,415.00	86.27	359.02	11,929.42	5,241.60	-108.47	5,242.41	0.52	0.15	-0.50
16,508.00	84.97	357.72	11,936.52	5,334.28	-111.10	5,335.11	1.97	-1.40	-1.40
16,670.00	86.57	357.14	11,948.47	5,495.67	-118.35	5,496.57	1.05	0.99	-0.36
16,763.00	87.72	357.80	11,953.10	5,588.47	-122.45	5,589.40	1.43	1.24	0.71
16,857.00	87.68	358.58	11,956.88	5,682.34	-125.42	5,683.30	0.83	-0.04	0.83
16,952.00	88.36	357.98	11,960.16	5,777.24	-128.26	5,778.22	0.95	0.72	-0.63
17,045.00	87.98	357.47	11,963.13	5,870.12	-131.95	5,871.13	0.68	-0.41	-0.55
17,139.00	87.28	356.33	11,967.02	5,963.90	-137.03	5,964.96	1.42	-0.74	-1.21
17,232.00	88.39	356.20	11,970.53	6,056.64	-143.09	6,057.75	1.20	1.19	-0.14
17,325.00	89.19	355.98	11,972.49	6,149.40	-149.43	6,150.56	0.89	0.86	-0.24
17,419.00	89.26	355.52	11,973.76	6,243.13	-156.39	6,244.36	0.49	0.07	-0.49
17,513.00	90.40	356.24	11,974.04	6,336.89	-163.15	6,338.18	1.43	1.21	0.77
17,607.00	90.54	357.06	11,973.27	6,430.72	-168.64	6,432.06	0.88	0.15	0.87
17,701.00	88.05	356.28	11,974.43	6,524.55	-174.10	6,525.94	2.78	-2.65	-0.83
17,795.00	89.16	355.81	11,976.72	6,618.29	-180.58	6,619.74	1.28	1.18	-0.50
17,890.00	89.70	356.73	11,977.66	6,713.09	-186.76	6,714.59	1.12	0.57	0.97
17,984.00	89.06	355.76	11,978.68	6,806.88	-192.91	6,808.44	1.24	-0.68	-1.03
18,078.00	87.95	355.19	11,981.13	6,900.55	-200.33	6,902.18	1.33	-1.18	-0.61
18,155.00	88.99	354.64	11,983.19	6,977.22	-207.15	6,978.91	1.53	1.35	-0.71
18,215.00	88.99	354.64	11,984.25	7,036.95	-212.75	7,038.69	0.00	0.00	0.00

Checked By: _____ Approved By: _____ Date: _____
