

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS AND MINING								FORM 8	
WELL COMPLETION OR RECOMPLETION REPORT AND LOG								1. WELL NAME Dobby 1236-7MVH	
2. TYPE OF WELL Gas Well			3. TYPE OF WORK DRILL NEW ☒ REENTER P&A ☐ DEEPEN ☐ RECOMP ☐					4. API NUMBER 4304757304	
5. NAME OF OPERATOR Middle Fork Energy Uinta, LLC					6. OPERATOR PHONE 435-789-1017			7. FIELD NAME UNDESIGNATED	
8. ADDRESS OF OPERATOR 1401 Wynkoop Street, Suite 300, Denver, CO, 80202					9. OPERATOR E-MAIL jillj@uintahgroup.com			10. UNIT NAME KJ2	
11. MINERAL LEASE NUMBER MULTIPLE LEASES			12. MINERAL OWNERSHIP FEDERAL			13. SURFACE OWNERSHIP FEDERAL		14. COUNTY UINTAH	
15. DATE SPUDDED (SPUD RIG) 06/27/2024		16. DATE SPUDDED (ROTARY RIG) 06/27/2024		17. DATE TOTAL DEPTH REACHED 08/15/2024		18. DATE COMPLETED/ABANDONED 09/22/2024		19. DATE OF FIRST PROD. / INJ. PROD:09/28/2024 INJ:	
20. DEPTH REFERENCE GROUND LEVEL ☐ KELLY BUSHING ☒ DERRICK FLOOR ☐					21. DEPTH REFERENCE ELEVATION 5373 (US Feet)			22. GRADED GROUND LEVEL ELEVATION 5347 (US Feet)	
23. WELLBORE DEVIATION PROFILE VERTICAL ☐ DIRECTIONAL ☐ HORIZONTAL ☒					24. TOTAL DEPTH MD 19025 TVD 12072			25. PLUGGED BACK TOTAL DEPTH MD 19025 TVD 12072	
26. CURRENT WELL STATUS Producing									

27. LOCATION OF WELL									
WELL POSITION	FOOTAGES		QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN	UTM EASTING	UTM NORTHING
Surface	2451 FSL	2578 FEL	NWSE	12	7.0 S	22.0 E	S	637140	4454025
Producing Interval Top	2420 FNL	2076 FEL	SWNE	12	7.0 S	22.0 E	S		
Producing Interval Bottom	2521 FNL	747 FEL	SENE	1	7.0 S	22.0 E	S		
Total Depth	2000 FNL	749 FEL	LOT8	1	7.0 S	22.0 E	S		

28. HOLE, CASING AND CEMENT INFORMATION															
STRING	HOLE SIZE	CASING O.D.	WEIGHT	GRADE	THREAD	TOP (MD)	BOTTOM (MD)	DV TOOL DEPTH	LEAD TAIL	CEMENT TYPE	SACKS	YIELD	WEIGHT	CEMENT TOP	BASIS FOR TOP
COND	24.0	16.0	42.05	X-52	LTC	0	146		L	Class G Cement	282	1.16	15.8	0	
SURF	12.25	9.625	40.0	L-80	LTC	0	4008		L	Class G Cement	780	2.89	11.5	0	
									T	Class G Cement	240	1.16	15.8		
INT	8.75	7.0	29.0	HCP-110	LTC	0	11942		L	Class G Cement	340	2.47	12.0	0	
									T	Class G Cement	110	1.15	15.8		
									L	Class G Cement	830	2.46	12.0	3987	
									T	Class G Cement	200	1.56	13.5		
PROD	6.125	4.5	15.1	P-110	BTC	11121	19022		L	Class G Cement	710	1.31	14.0	11120	

29. TUBING RECORD			
TUBING SIZE	TOP (MD)	BOT (MD)	PACKER DEPTH

30. RETRIEVABLE / TEMPORARY PLUGS		
PLUG	DEPTH (MD)	TYPE

31. PERMANENT / ABANDONMENT PLUGS		
PLUG	TOP (MD)	BOTTOM (MD)

32. FORMATION DETAILS and STRATIGRAPHIC MARKERS				
FR	FORMATION NAME	TOP (MD)	TOP (TVD)	DESCRIPTION, CONTENTS, ETC.
1	GREEN RIVER	3146	3145	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
2	BIRDS NEST	3559	3558	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
3	MAHOGANY	3988	3986	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
4	WASATCH	6626	6624	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
5	MESA VERDE	9539	9529	
	OIL SHOW? ☒ GAS SHOW? ☒ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☒ COMMINGLED? ☐			

33. COMPLETED and TESTED INTERVALS (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)
--

FR	TOP (MD)	BOTTOM (MD)	TOP (TVD)	BOTTOM (TVD)	STIMULATION TREATMENT	INTERVAL STATUS
5	11971	18952	11818	12074	Fracture Stimulated	PRODUCING

34A. PRODUCTION INFORMATION (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)									
FR	TOP (MD)	BOTTOM (MD)	DATE FIRST PROD.	TEST DATE	HRS. TESTED	TBG. PRESSURE	CSG. PRESSURE	PROD. METHOD	
5	11971	18952	09/28/2024	10/17/2024	24		536	Flowing	
	TEST PRODUCTION VOLUMES			24-HOUR PRODUCTION RATES			GAS-OIL RATIO	OIL API	GAS BTU
	OIL (BBL)	GAS (MSCF)	WATER (BBL)	OIL (BBL)	GAS (MSCF)	WATER (BBL)	71662	0.0	
	65	4658	1738	65	4658	1738			

35. WELL TREATMENTS (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)						
FR	TREATMENT TYPE	TOP (MD)	BOTTOM (MD)	START DATE	END DATE	AMOUNT AND TYPE OF MATERIAL
5	Fracture Stimulation	11971	18952	09/13/2024	09/22/2024	218,948 BBLs FRESH WATER - 6,991,661 LBS PROPPANT - 35 STAGES

36. LOGS, SURVEYS, AND REPORTS (PDF file of each and LAS file of logs if available are to be submitted.)						
REPORTS AND OTHER INFORMATION.						
Dx Survey ☒ DST Report ☐ Core Analysis ☐ DOGM Form 7 ☐ Geologic Report ☐ Wellbore Diagram ☐ Other ☐						
SUBMITTED PDF LOGS			SUBMITTED LAS LOGS			
MEASURED WHILE DRILLING, CEMENT BOND						

OGM Official Use Only

37. I hereby certify that the foregoing and attached information is complete as determined from all available records.		
NAME Karlyn Linarte	TITLE Permitting Tech - Uintah Group Permitting	DATE 11/07/2024
SIGNATURE N/A	PHONE 435-789-1017	EMAIL klinarte@uintahgroup.com



Middle Fork Daily Completion Activity Report

Well Name: DOBBY 1236-7MVH

API/UWI 4304757304	Surface Legal Location S12-T7S-R22E	Field Name UNDESIGNATED	License # UTU-011226	State/Province UTAH	Well Configuration Type HORIZONTAL
Ground Elevation (ft) 5,347.40	Casing Flange Elevation (ft) 5,345.32	KB-Ground Distance (ft) 26.00	KB-Casing Flange Distance (ft) 28.08	Surface Spud Date 6/27/2024 20:00	Rig Release Date 8/16/2024 16:30

Job Category COMPLETION			
Rpt #	Start Date	End Date	Summary
3.0	9/3/2024	9/4/2024	In stall Tubing Head
4.0	9/5/2024	9/6/2024	MIRU W/L RIH W/GR/JB
5.0	9/6/2024	9/7/2024	MIRU W/L RIH W/ CBL Log
6.0	9/9/2024	9/10/2024	MIRUSU/NU test bope/TIH w/Polish mill
7.0	9/10/2024	9/11/2024	LD Tubing/RIH w/ frac string
8.0	9/11/2024	9/12/2024	RIH/w Frac String/Land/RDMOSU. Start N/U Frac Tree & Zipper Manifold.
9.0	9/12/2024	9/13/2024	MIRU Cal Frac, TWG & Straightline. Set 2 RBP Test & Chart Casing. Pull 2 RBP.
10.0	9/13/2024	9/14/2024	Perf stage-1, and perform D-fit. Continue to prep loc for frac ops.
11.0	9/14/2024	9/15/2024	Continue Frac Prep.
12.0	9/15/2024	9/16/2024	Rig Up, begin Frac stage-1
13.0	9/16/2024	9/17/2024	Frac stage 1-5, Perf stages 2-6
14.0	9/17/2024	9/18/2024	Frac stages 6-10, Perf stages 7-11
15.0	9/18/2024	9/19/2024	Frac stages 11-16, Perf stages 12-16
16.0	9/19/2024	9/20/2024	Frac stages 17-21, Perf stages 17-21
17.0	9/20/2024	9/21/2024	Frac Stages 22-27, Perf stages 22-27, POOH perf stage-28
18.0	9/21/2024	9/22/2024	Frac stages 28-33, and begin stage-34 frac Perf stages 29-34
19.0	9/22/2024	9/23/2024	Frac stages 34-35, Perf stage 35, set kill plug
20.0	9/23/2024	9/24/2024	Spot D/O Tanks & R/U Prod Equip.
21.0	9/24/2024	9/25/2024	Swing reel onto CTU. Spot in coil equip.
22.0	9/25/2024	9/26/2024	Wait on hot spool to be delivered.
23.0	9/26/2024	9/27/2024	N/D Wellhead. N/U hot spool & D/O assembly.
24.0	9/27/2024	9/28/2024	Spot in Crane & Core CTU. R/U Coil Spread. Pressure test surface equip to 6,500 psi. Drill Plugs KP/#35-#1. Clean out to PBTD. Pump sweeps as per procedure. Start Pooh W/BHA #1
25.0	9/28/2024	9/29/2024	Continue Pooh W/BHA #1. Install Production Tree. RDMO all coil vendors. Turn well over to production team.
26.0	9/29/2024	9/30/2024	Drain up all working tanks and release all rental equip.



UT Well Completion Report and Log

Well Name: DOBBY 1236-7MVH

Fluid Type GAS		Well Subtype NEW DRILL		Operator MIDDLE FORK ENERGY UINTA		Lease			
Surface Legal Location S12-T7S-R22E		North/South Distance (ft) 2,451.0		N/S Ref FSL	East/West Distance (ft) 2,578.0		E/W Ref FEL	Target Formation NESLEN LOWER	
Ground Elevation (ft) 5,347.40	KB-Ground Distance (ft) 26.00	Total Depth (All) (ftKB) ORIGINAL HOLE - 19,025.0			Total Depth All (TVD) (ftKB) ORIGINAL HOLE - 12,072.1			Well Name DOBBY 1236-7MVH	
Conductor Spud Date 6/12/2024		Surface Spud Date 6/27/2024			Rig Release Date 8/16/2024			API/UWI 4304757304	
								Field Name UNDESIGNATED	
TD Date		Frac Start Date		Completed Date		Initial Production Date			
End Date 8/15/2024		Date 9/13/2024		Date 9/22/2024		On Production Date			

Wellbores

Profile Type Horizontal	Actual Deviation Survey Table Deviation Survey
----------------------------	---

Casing Strings

Csg Des	Hole Size (in)	Casing OD (in)	Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
Conductor	24	16	X-52	42.05	29.4	146.0
Surface	12 1/4	9 5/8	HCL-80	40.00	29.4	4,008.0
Intermediate	8 3/4	7	HCP-110	29.00	29.4	11,942.0
Production Liner	6 1/8	4 1/2	P-110HP	15.10	11,120.6	19,022.0

Casing Components

Csg Des	Item Des	Top (ftKB)	Btm (ftKB)
Intermediate	Stage Tool	3,988.8	3,991.2

Cement Fluids

Casing Description	Stg #	Fluid Type	Class	Amount (sacks)	Yield (ft³/sack)	Density (lb/gal)	Final Top
Surface	1	Lead	G	780	2.89	11.50	29.4
Surface	1	Tail	G	240	1.16	15.80	3,533.0
Intermediate	1	Lead	G	830	2.46	12.00	3,987.0
Intermediate	1	Tail	G	200	1.56	13.50	10,689.0
Intermediate	2	Lead	G	340	2.47	12.00	29.4
Intermediate	2	Tail	G	110	1.15	15.80	3,488.0
Production Liner	1	Tail	G	710	1.31	14.00	11,120.0

Tubing Record:

String Max Nominal OD (in)	Tubing Set Depth (ftKB)	Tubing Land Date
----------------------------	-------------------------	------------------

Perforations

Formation	Top (ftKB)	Btm (ftKB)	Top (TVD) (ftKB)	Btm (TVD) (ftKB)	Est Hole Dia (in)	Shot Dens (shots/ft)	Sum of Calculated Shot Total	Current Status
NESLEN	11,971.0	12,152.0	11,817.6	11,872.0		3.0	30	Open - Flowing (11,971.0 - 11,972.0 ftKB)
NESLEN	12,171.0	12,354.0	11,875.4	11,893.3		3.0	30	Open - Flowing (12,171.0 - 12,172.0 ftKB)
NESLEN	12,371.0	12,552.0	11,895.0	11,907.0		3.0	30	Open - Flowing (12,371.0 - 12,372.0 ftKB)
NESLEN	12,573.0	12,752.0	11,907.9	11,916.1		3.0	30	Open - Flowing (12,573.0 - 12,574.0 ftKB)
NESLEN	12,771.0	12,952.0	11,917.3	11,921.6		3.0	30	Open - Flowing (12,771.0 - 12,772.0 ftKB)
NESLEN	12,970.0	13,152.0	11,921.7	11,924.5		3.0	30	Open - Flowing (12,970.0 - 12,971.0 ftKB)
NESLEN	13,171.0	13,352.0	11,925.2	11,933.9		3.0	30	Open - Flowing (13,171.0 - 13,172.0 ftKB)
NESLEN	13,371.0	13,552.0	11,935.5	11,951.6		3.0	30	Open - Flowing (13,371.0 - 13,372.0 ftKB)
NESLEN	13,571.0	13,752.0	11,953.2	11,965.7		3.0	30	Open - Flowing (13,571.0 - 13,572.0 ftKB)
NESLEN	13,771.0	13,952.0	11,965.8	11,967.9		3.0	30	Open - Flowing (13,771.0 - 13,772.0 ftKB)
NESLEN	13,971.0	14,152.0	11,968.8	11,978.9		3.0	30	Open - Flowing (13,971.0 - 13,972.0 ftKB)
NESLEN	14,171.0	14,352.0	11,980.0	11,989.7		3.0	30	Open - Flowing (14,171.0 - 14,172.0 ftKB)
NESLEN	14,371.0	14,552.0	11,990.2	11,993.8		3.0	30	Open - Flowing (14,371.0 - 14,372.0 ftKB)
NESLEN	14,571.0	14,752.0	11,994.8	12,011.4		3.0	30	Open - Flowing (14,571.0 - 14,572.0 ftKB)
NESLEN	14,771.0	14,952.0	12,013.0	12,023.2		3.0	30	Open - Flowing (14,771.0 - 14,772.0 ftKB)
NESLEN	14,971.0	15,152.0	12,023.8	12,037.7		3.0	30	Open - Flowing (14,971.0 - 14,972.0 ftKB)
NESLEN	15,171.0	15,352.0	12,039.2	12,044.9		3.0	30	Open - Flowing (15,171.0 - 15,172.0 ftKB)
NESLEN	15,371.0	15,552.0	12,045.1	12,046.0		3.0	30	Open - Flowing (15,371.0 - 15,372.0 ftKB)
NESLEN	15,571.0	15,752.0	12,046.2	12,048.0		3.0	30	Open - Flowing (15,571.0 - 15,572.0 ftKB)
NESLEN	15,771.0	15,952.0	12,047.9	12,048.1		3.0	30	Open - Flowing (15,771.0 - 15,772.0 ftKB)
NESLEN	15,971.0	16,152.0	12,048.0	12,051.5		3.0	30	Open - Flowing (15,971.0 - 15,972.0 ftKB)
NESLEN	16,171.0	16,352.0	12,051.9	12,055.1		3.0	30	Open - Flowing (16,171.0 - 16,172.0 ftKB)



UT Well Completion Report and Log

Well Name: DOBBY 1236-7MVH

Fluid Type GAS	Well Subtype NEW DRILL	Operator MIDDLE FORK ENERGY UINTA				Lease
Surface Legal Location S12-T7S-R22E	North/South Distance (ft) 2,451.0	N/S Ref FSL	East/West Distance (ft) 2,578.0	E/W Ref FEL	Target Formation NESLEN LOWER	
Ground Elevation (ft) 5,347.40	KB-Ground Distance (ft) 26.00	Total Depth (All) (ftKB) ORIGINAL HOLE - 19,025.0		Total Depth (TVD) (ftKB) ORIGINAL HOLE - 12,072.1		Well Name DOBBY 1236-7MVH
Conductor Spud Date 6/12/2024	Surface Spud Date 6/27/2024	Rig Release Date 8/16/2024		API/UWI 4304757304		Field Name UNDESIGNATED
TD Date End Date 8/15/2024		Frac Start Date Date 9/13/2024		Completed Date Date 9/22/2024		Initial Production Date On Production Date

Perforations

Formation	Top (ftKB)	Btm (ftKB)	Top (TVD) (ftKB)	Btm (TVD) (ftKB)	Est Hole Dia (in)	Shot Dens (shots/ft)	Sum of Calculated Shot Total	Current Status
NESLEN	16,371.0	16,552.0	12,056.3	12,064.1		3.0	30	Open - Flowing (16,371.0 - 16,372.0 ftKB)
NESLEN	16,571.0	16,752.0	12,064.0	12,063.1		3.0	30	Open - Flowing (16,571.0 - 16,572.0 ftKB)
NESLEN	16,771.0	16,950.0	12,062.9	12,064.0		3.0	30	Open - Flowing (16,771.0 - 16,772.0 ftKB)
NESLEN	16,971.0	17,152.0	12,064.1	12,066.1		3.0	30	Open - Flowing (16,971.0 - 16,972.0 ftKB)
NESLEN	17,172.0	17,352.0	12,066.4	12,066.7		3.0	30	Open - Flowing (17,172.0 - 17,173.0 ftKB)
NESLEN	17,371.0	17,552.0	12,066.6	12,066.3		3.0	30	Open - Flowing (17,371.0 - 17,372.0 ftKB)
NESLEN	17,571.0	17,752.0	12,066.2	12,066.2		3.0	30	Open - Flowing (17,571.0 - 17,572.0 ftKB)
NESLEN	17,769.0	17,952.0	12,066.3	12,069.6		3.0	30	Open - Flowing (17,769.0 - 17,770.0 ftKB)
NESLEN	17,971.0	18,152.0	12,070.7	12,077.3		3.0	30	vwvperforationstatus 2E07F4439F344A04AA93613D9295 (17,971.0 - 17,972.0 ftKB)
NESLEN	18,173.0	18,352.0	12,077.7	12,083.2		3.0	30	Open - Flowing (18,173.0 - 18,174.0 ftKB)
NESLEN	18,371.0	18,552.0	12,083.6	12,082.0		3.0	30	Open - Flowing (18,371.0 - 18,372.0 ftKB)
NESLEN	18,571.0	18,752.0	12,081.6	12,079.2		3.0	30	Open - Flowing (18,571.0 - 18,572.0 ftKB)
NESLEN	18,771.0	18,952.0	12,078.9	12,074.2		3.0	30	Open - Flowing (18,771.0 - 18,772.0 ftKB)
Total							1,050	

Producing Intervals & Perforation Record:

Minimum of Top Depth (ftKB) 11,971.0	Maximum of Bottom Depth (ftKB) 18,952.0
---	--

Acid, Fracture, Treatment, Cement Squeeze, Etc.:

Type Hydraulic Frac	Number of Treatment Intervals 35	Volume Clean Total (bbl) 218,948.33	Proppant Total (lb) 6,991,661.0
Type	Sand Size		

Fluid Name Slickwater

Plug Back Total Depths

Depth (ftKB)	Depth (TVD) (ftKB)
--------------	--------------------

Zones

Zone Name	Top (ftKB)	Btm (ftKB)	Final Top (ftKB)
Neslen Upper	11,605.0		
Neslen Lower	11,971.0	18,952.0	
Neslen Lower	12,229.9		

Formations

Formation Name	Final Top MD (ftKB)
GREEN RIVER	3,146.0
BIRDS NEST	3,559.0
MAHOGANY	3,988.0
WASATCH	6,625.7
MESAVERDE	9,539.0
NESLEN	11,605.0



Survey Certification

7327 West Barton Road
Casper, WY 82604
(307)-472-6621

Operator	Middle Fork Energy Partners
Well Name & No.	Dobby 1236-7MVH
County & State	Uintah, UT
SDI Job #	OP.045024
Rig	Cyclone 34
Survey Date	6/17/2024 to 8/13/2024
GL & KB Elevation	GL 5347.4' & KB 26' = 5373.4'

I, Janie Collins, having personal knowledge of all the facts, hereby
certify that the attached directional survey run from a measured depth of 213 feet to a
measured depth of 19,025 feet is true and correct as determined from all available records.

A handwritten signature in blue ink, appearing to read 'Janie Collins', written over a horizontal line.

Signature

26-Aug-2024

Date



Janie Collins

Rockies Region Well Planner
Scientific Drilling - Rocky Mountain District



WELL DETAILS: Dobby 1236-7MVH

			GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)	5347.40		
+N/-S	+E/-W	Northing	Easting	Latitude	Longitude	
0.00	0.00	7257802.31	2230040.73	40.2254356	-109.3881039	

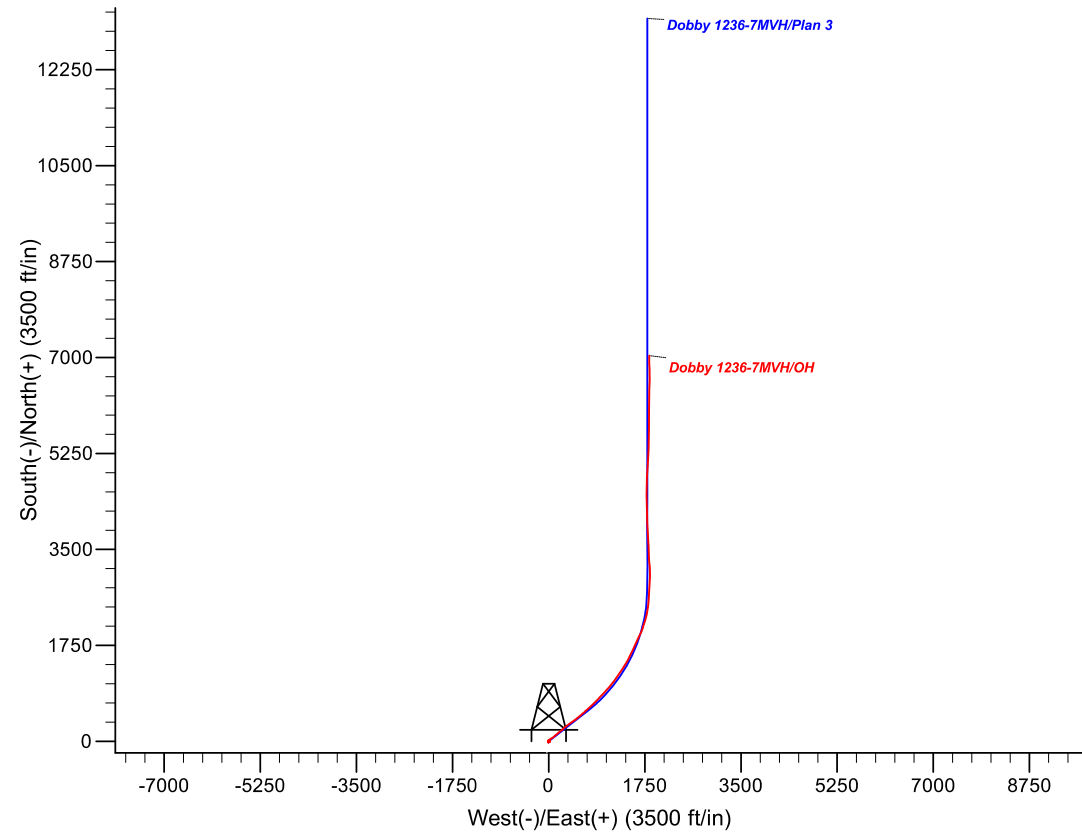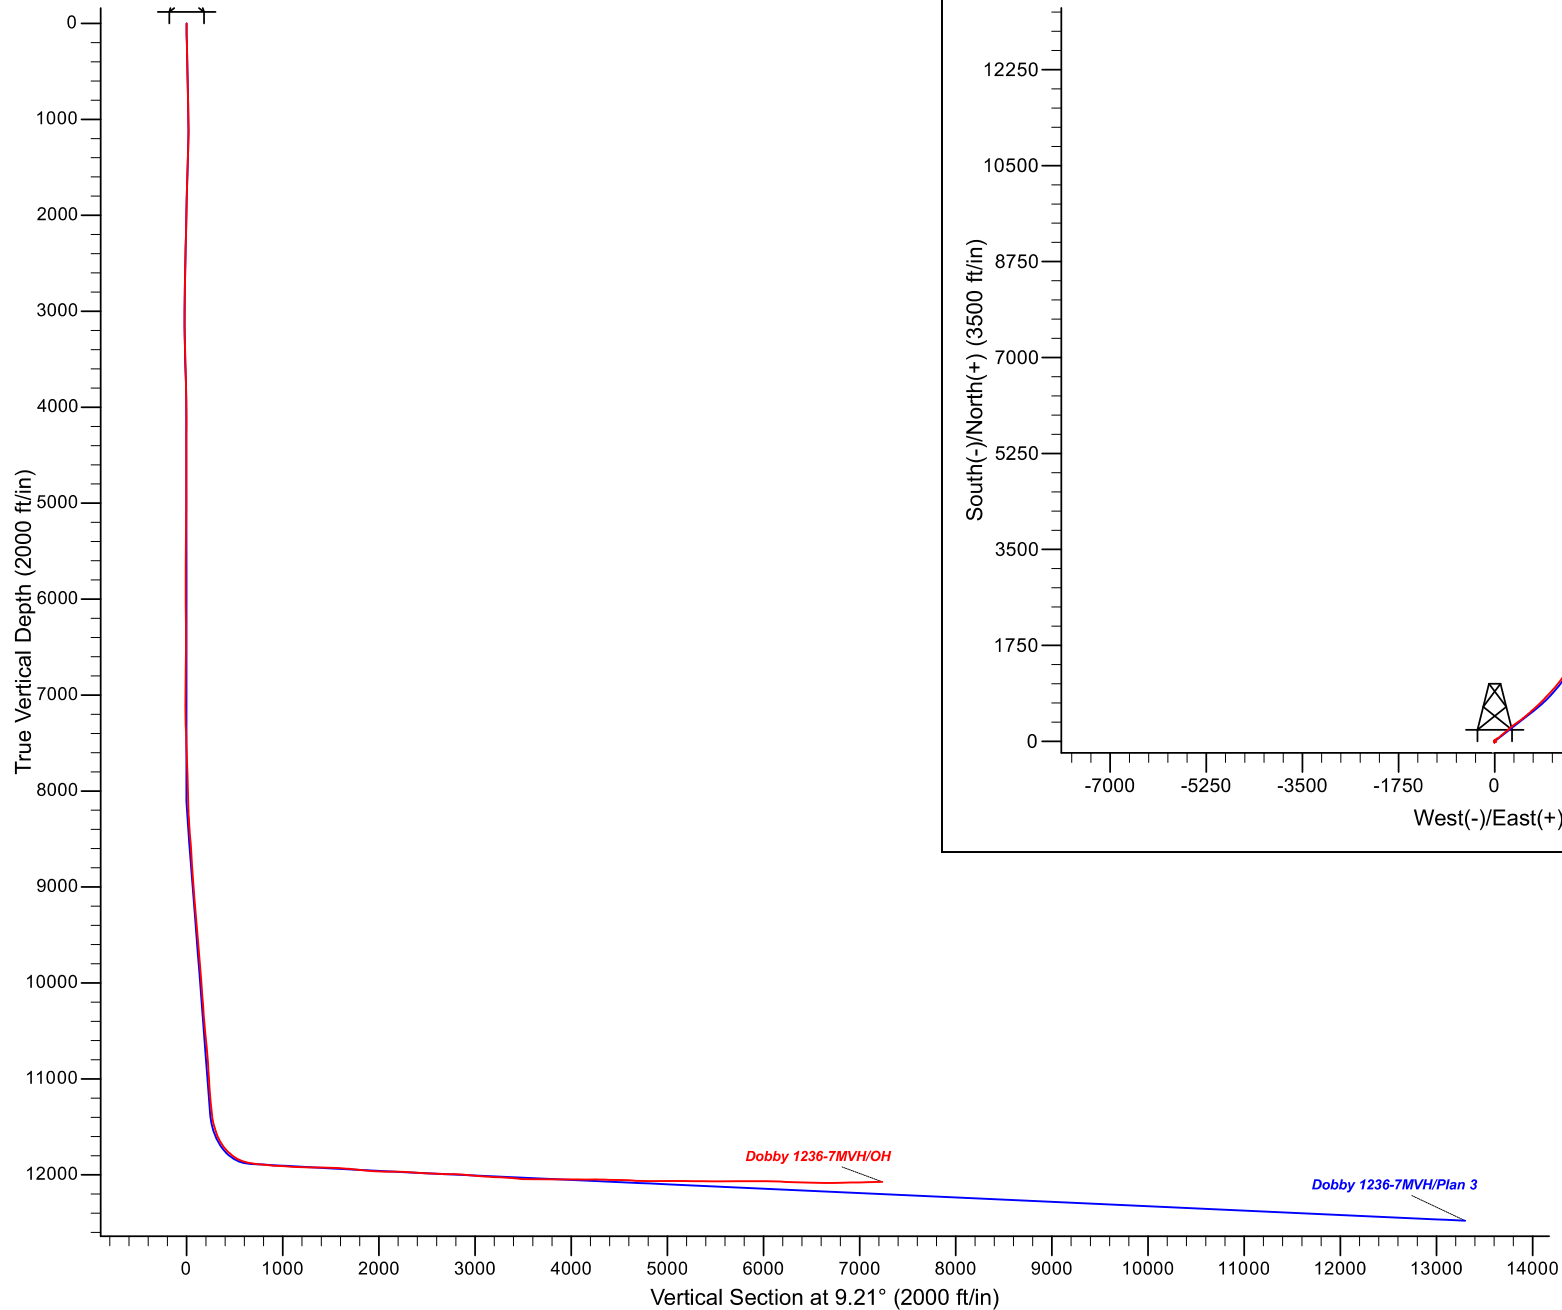

Company Name: Middle Fork Energy Uinta, LLC
Project: Uintah County, UT
Site: Dobby 33-12-722 Pad
Well: Dobby 1236-7MVH
Wellbore: OH

PROJECT DETAILS: Uintah County, UT

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: Utah Central Zone

System Datum: Mean Sea Level
Local North: True

Created By: Janie Collins Date: 9:11, August 26 2024



Middle Fork Energy Uinta, LLC

Uintah County, UT
Dobby 33-12-722 Pad
Dobby 1236-7MVH

OH

Design: OH

Standard Survey Report

26 August, 2024



www.scientificdrilling.com



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-7MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-7MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Project	Uintah County, UT		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	Utah Central Zone		

Site		Dobby 33-12-722 Pad				
Site Position:		Northing:	7,257,751.79	usft	Latitude:	40.2253018
From:	Map	Easting:	2,229,966.29	usft	Longitude:	-109.3883747
Position Uncertainty:		0.00	ft	Slot Radius:	13.200	in
					Grid Convergence:	1.35 °

Well	Dobby 1236-7MVH					
Well Position	+N/-S	0.00 ft	Northing:	7,257,802.31 usft	Latitude:	40.2254357
	+E/-W	0.00 ft	Easting:	2,230,040.73 usft	Longitude:	-109.3881039
Position Uncertainty		0.00 ft	Wellhead Elevation:	ft	Ground Level:	5,347.40 ft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM2024	6/25/2024	9.70	65.82	50,881.70000000

Design	OH				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)	
	0.00	0.00	0.00	9.21	

Survey Program	Date	8/15/2024			
From (ft)	To (ft)	Survey (Wellbore)	Tool Name	Description	
26.00	3,953.00	Survey #1 - Surface (OH)	MWD+HDGM	OWSG MWD + HDGM	
4,105.00	11,333.00	Survey #2 - Intermediate (OH)	MWD+HDGM	OWSG MWD + HDGM	
11,404.00	12,348.00	Survey #3 - Curve (OH)	MWD+HDGM	OWSG MWD + HDGM	
12,442.00	19,025.00	Survey #4 - Lateral (OH)	MWD+HDGM	OWSG MWD + HDGM	

Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
26.00	0.00	0.00	26.00	0.00	0.00	0.00	0.00	0.00	0.00	
213.00	1.61	31.96	212.98	2.23	1.39	2.42	0.86	0.86	0.00	
304.00	1.71	25.30	303.94	4.54	2.65	4.91	0.24	0.11	-7.32	
395.00	1.77	30.86	394.90	6.97	3.95	7.52	0.20	0.07	6.11	
485.00	0.94	43.95	484.87	8.70	5.17	9.42	0.98	-0.92	14.54	
575.00	1.25	42.68	574.85	9.95	6.35	10.84	0.35	0.34	-1.41	
665.00	1.13	42.42	664.83	11.33	7.62	12.40	0.13	-0.13	-0.29	



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-7MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-7MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
756.00	0.93	36.94	755.82	12.58	8.67	13.81	0.24	-0.22	-6.02
846.00	1.20	26.94	845.80	14.01	9.53	15.35	0.36	0.30	-11.11
936.00	1.17	29.11	935.78	15.65	10.40	17.11	0.06	-0.03	2.41
1,027.00	1.34	45.97	1,026.76	17.20	11.62	18.84	0.44	0.19	18.53
1,118.00	0.43	114.88	1,117.75	17.80	12.70	19.60	1.38	-1.00	75.73
1,212.00	1.60	212.90	1,211.74	16.55	12.30	18.30	1.82	1.24	104.28
1,303.00	1.73	215.05	1,302.70	14.35	10.83	15.90	0.16	0.14	2.36
1,394.00	1.50	207.07	1,393.67	12.17	9.49	13.53	0.35	-0.25	-8.77
1,484.00	1.72	211.48	1,483.63	9.97	8.25	11.16	0.28	0.24	4.90
1,576.00	1.81	215.56	1,575.59	7.61	6.69	8.58	0.17	0.10	4.43
1,671.00	1.83	218.86	1,670.54	5.21	4.86	5.92	0.11	0.02	3.47
1,765.00	1.67	216.31	1,764.49	2.94	3.11	3.40	0.19	-0.17	-2.71
1,859.00	1.61	207.79	1,858.46	0.66	1.68	0.92	0.27	-0.06	-9.06
1,953.00	1.49	193.00	1,952.42	-1.70	0.79	-1.55	0.44	-0.13	-15.73
2,048.00	1.26	197.15	2,047.39	-3.90	0.21	-3.81	0.26	-0.24	4.37
2,143.00	1.41	205.64	2,142.37	-5.95	-0.61	-5.97	0.26	0.16	8.94
2,238.00	1.26	208.61	2,237.34	-7.92	-1.61	-8.08	0.17	-0.16	3.13
2,332.00	1.12	211.89	2,331.32	-9.61	-2.59	-9.90	0.17	-0.15	3.49
2,427.00	1.33	193.48	2,426.30	-11.47	-3.34	-11.85	0.47	0.22	-19.38
2,522.00	1.28	191.94	2,521.28	-13.58	-3.82	-14.01	0.06	-0.05	-1.62
2,616.00	0.81	187.81	2,615.26	-15.26	-4.12	-15.73	0.51	-0.50	-4.39
2,709.00	1.06	181.35	2,708.25	-16.77	-4.23	-17.24	0.29	0.27	-6.95
2,804.00	0.99	188.53	2,803.23	-18.46	-4.38	-18.93	0.15	-0.07	7.56
2,899.00	0.85	169.61	2,898.22	-19.97	-4.37	-20.41	0.35	-0.15	-19.92
2,994.00	0.81	197.48	2,993.21	-21.30	-4.45	-21.74	0.42	-0.04	29.34
3,085.00	0.45	310.89	3,084.21	-21.68	-4.91	-22.19	1.18	-0.40	124.63
3,178.00	1.34	349.37	3,177.20	-20.37	-5.39	-20.97	1.10	0.96	41.38
3,273.00	1.28	347.13	3,272.17	-18.25	-5.83	-18.95	0.08	-0.06	-2.36
3,367.00	1.40	355.23	3,366.15	-16.08	-6.16	-16.86	0.24	0.13	8.62
3,462.00	1.51	7.29	3,461.12	-13.68	-6.09	-14.48	0.34	0.12	12.69
3,557.00	1.42	9.92	3,556.08	-11.28	-5.73	-12.05	0.12	-0.09	2.77
3,652.00	1.32	3.41	3,651.06	-9.03	-5.46	-9.79	0.19	-0.11	-6.85
3,746.00	1.25	358.98	3,745.03	-6.92	-5.42	-7.70	0.13	-0.07	-4.71
3,840.00	1.21	8.67	3,839.01	-4.92	-5.29	-5.70	0.23	-0.04	10.31
3,935.00	1.01	29.32	3,934.00	-3.20	-4.73	-3.91	0.47	-0.21	21.74
3,953.00	0.90	32.80	3,951.99	-2.94	-4.57	-3.63	0.69	-0.61	19.33
4,105.00	0.38	83.97	4,103.98	-1.88	-3.42	-2.41	0.48	-0.34	33.66
4,197.00	0.42	106.63	4,195.98	-1.95	-2.80	-2.37	0.18	0.04	24.63
4,291.00	0.34	125.12	4,289.98	-2.21	-2.24	-2.54	0.15	-0.09	19.67
4,385.00	0.44	121.94	4,383.98	-2.56	-1.70	-2.80	0.11	0.11	-3.38
4,480.00	0.64	138.95	4,478.97	-3.15	-1.05	-3.28	0.27	0.21	17.91
4,574.00	0.54	136.73	4,572.97	-3.87	-0.40	-3.88	0.11	-0.11	-2.36
4,667.00	0.48	124.42	4,665.96	-4.41	0.22	-4.32	0.13	-0.06	-13.24



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-7MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-7MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
4,759.00	0.38	114.33	4,757.96	-4.75	0.82	-4.56	0.14	-0.11	-10.97
4,852.00	0.42	131.42	4,850.96	-5.10	1.36	-4.82	0.13	0.04	18.38
4,947.00	0.53	119.94	4,945.96	-5.55	2.00	-5.16	0.15	0.12	-12.08
5,041.00	0.68	112.86	5,039.95	-5.99	2.89	-5.45	0.18	0.16	-7.53
5,136.00	1.01	114.57	5,134.94	-6.55	4.17	-5.80	0.35	0.35	1.80
5,230.00	1.13	106.35	5,228.92	-7.16	5.81	-6.14	0.21	0.13	-8.74
5,324.00	1.30	109.59	5,322.90	-7.78	7.71	-6.44	0.19	0.18	3.45
5,420.00	1.16	103.66	5,418.88	-8.37	9.68	-6.72	0.20	-0.15	-6.18
5,514.00	1.02	118.65	5,512.86	-9.00	11.34	-7.07	0.34	-0.15	15.95
5,609.00	1.19	120.88	5,607.85	-9.91	12.92	-7.71	0.18	0.18	2.35
5,703.00	1.05	126.38	5,701.83	-10.92	14.45	-8.47	0.19	-0.15	5.85
5,797.00	1.29	128.75	5,795.81	-12.10	15.97	-9.38	0.26	0.26	2.52
5,891.00	0.20	92.82	5,889.80	-12.77	16.96	-9.89	1.21	-1.16	-38.22
5,986.00	1.62	293.48	5,984.79	-12.24	15.90	-9.54	1.90	1.49	-167.73
6,081.00	1.81	289.53	6,079.75	-11.20	13.25	-8.94	0.24	0.20	-4.16
6,176.00	2.00	287.42	6,174.69	-10.20	10.26	-8.43	0.21	0.20	-2.22
6,269.00	1.84	288.28	6,267.64	-9.25	7.29	-7.96	0.17	-0.17	0.92
6,362.00	1.75	278.19	6,360.60	-8.58	4.47	-7.75	0.35	-0.10	-10.85
6,456.00	1.69	277.43	6,454.55	-8.20	1.67	-7.82	0.07	-0.06	-0.81
6,551.00	1.65	275.63	6,549.51	-7.88	-1.08	-7.95	0.07	-0.04	-1.89
6,645.00	1.50	267.18	6,643.48	-7.81	-3.66	-8.29	0.29	-0.16	-8.99
6,740.00	1.63	259.02	6,738.44	-8.13	-6.22	-9.02	0.27	0.14	-8.59
6,835.00	1.38	256.43	6,833.41	-8.65	-8.66	-9.93	0.27	-0.26	-2.73
6,930.00	1.13	257.96	6,928.39	-9.12	-10.69	-10.71	0.27	-0.26	1.61
7,025.00	0.78	240.07	7,023.37	-9.63	-12.17	-11.46	0.48	-0.37	-18.83
7,119.00	0.83	237.68	7,117.36	-10.32	-13.30	-12.31	0.06	0.05	-2.54
7,214.00	0.86	346.79	7,212.36	-9.99	-14.04	-12.11	1.45	0.03	114.85
7,308.00	2.01	357.55	7,306.33	-7.66	-14.27	-9.84	1.25	1.22	11.45
7,404.00	2.28	356.69	7,402.26	-4.07	-14.45	-6.33	0.28	0.28	-0.90
7,498.00	2.28	1.15	7,496.19	-0.33	-14.53	-2.65	0.19	0.00	4.74
7,593.00	2.17	358.49	7,591.11	3.35	-14.53	0.98	0.16	-0.12	-2.80
7,687.00	2.13	27.78	7,685.05	6.68	-13.77	4.39	1.16	-0.04	31.16
7,781.00	2.18	42.38	7,778.98	9.54	-11.75	7.54	0.58	0.05	15.53
7,876.00	2.10	45.37	7,873.92	12.10	-9.29	10.46	0.14	-0.08	3.15
7,902.00	2.13	43.39	7,899.90	12.79	-8.62	11.24	0.30	0.12	-7.62
7,996.00	1.97	48.25	7,993.84	15.13	-6.22	13.94	0.25	-0.17	5.17
8,091.00	1.85	56.58	8,088.79	17.07	-3.72	16.25	0.32	-0.13	8.77
8,185.00	2.62	48.44	8,182.72	19.33	-0.84	18.94	0.88	0.82	-8.66
8,277.00	5.04	59.89	8,274.51	22.75	4.23	23.13	2.75	2.63	12.45
8,372.00	5.43	53.71	8,369.11	27.50	11.46	28.98	0.72	0.41	-6.51
8,465.00	5.28	55.07	8,461.70	32.56	18.51	35.10	0.21	-0.16	1.46
8,560.00	6.03	50.27	8,556.24	38.25	25.94	41.91	0.93	0.79	-5.05
8,655.00	7.37	57.07	8,650.59	44.75	34.89	49.76	1.64	1.41	7.16
8,749.00	5.55	67.40	8,743.99	49.78	44.15	56.20	2.29	-1.94	10.99



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-7MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-7MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
8,844.00	5.40	62.28	8,838.56	53.62	52.34	61.31	0.54	-0.16	-5.39
8,940.00	5.13	59.91	8,934.16	57.87	60.06	66.74	0.36	-0.28	-2.47
9,034.00	6.19	56.37	9,027.70	62.79	67.91	72.85	1.19	1.13	-3.77
9,126.00	7.04	49.64	9,119.08	69.19	76.34	80.51	1.25	0.92	-7.32
9,220.00	6.35	54.00	9,212.44	75.97	84.93	88.59	0.91	-0.73	4.64
9,315.00	6.97	42.75	9,306.81	83.29	93.10	97.12	1.52	0.65	-11.84
9,410.00	6.10	47.07	9,401.19	90.96	100.71	105.91	1.05	-0.92	4.55
9,503.00	5.47	50.23	9,493.71	97.17	107.73	113.16	0.76	-0.68	3.40
9,597.00	6.29	45.16	9,587.22	103.66	114.83	120.70	1.03	0.87	-5.39
9,692.00	6.19	49.56	9,681.66	110.65	122.41	128.82	0.51	-0.11	4.63
9,787.00	5.17	50.89	9,776.19	116.68	129.63	135.92	1.08	-1.07	1.40
9,882.00	6.08	53.78	9,870.73	122.35	137.01	142.70	1.00	0.96	3.04
9,977.00	6.67	54.20	9,965.14	128.55	145.55	150.19	0.62	0.62	0.44
10,072.00	6.08	49.60	10,059.56	135.04	153.85	157.92	0.82	-0.62	-4.84
10,166.00	5.89	50.57	10,153.04	141.33	161.37	165.33	0.23	-0.20	1.03
10,261.00	5.35	56.21	10,247.59	146.89	168.82	172.01	0.81	-0.57	5.94
10,356.00	6.20	43.92	10,342.11	153.05	176.06	179.25	1.57	0.89	-12.94
10,451.00	5.67	45.32	10,436.60	160.04	182.95	187.26	0.58	-0.56	1.47
10,545.00	7.05	49.32	10,530.02	167.07	190.63	195.42	1.54	1.47	4.26
10,640.00	6.99	50.49	10,624.31	174.54	199.51	204.23	0.16	-0.06	1.23
10,735.00	6.46	51.19	10,718.65	181.57	208.13	212.54	0.56	-0.56	0.74
10,830.00	6.00	53.73	10,813.09	187.86	216.30	220.06	0.56	-0.48	2.67
10,924.00	5.47	55.28	10,906.62	193.32	223.94	226.67	0.59	-0.56	1.65
11,019.00	4.89	55.69	11,001.23	198.18	231.01	232.60	0.61	-0.61	0.43
11,114.00	4.98	50.62	11,095.88	203.08	237.54	238.48	0.47	0.09	-5.34
11,209.00	7.08	47.97	11,190.35	209.61	245.08	246.14	2.23	2.21	-2.79
11,305.00	6.59	44.36	11,285.67	217.51	253.33	255.25	0.68	-0.51	-3.76
11,333.00	6.37	44.39	11,313.49	219.77	255.54	257.84	0.79	-0.79	0.11
11,404.00	7.92	46.42	11,383.94	225.96	261.83	264.95	2.21	2.18	2.86
11,499.00	19.25	45.58	11,476.13	241.48	277.81	282.83	11.93	11.93	-0.88
11,592.00	25.40	54.65	11,562.14	263.78	305.06	309.21	7.56	6.61	9.75
11,684.00	36.44	53.08	11,640.95	291.69	343.12	342.85	12.03	12.00	-1.71
11,747.00	43.97	53.35	11,689.03	316.02	375.67	372.08	11.96	11.95	0.43
11,779.00	47.85	53.91	11,711.29	329.65	394.18	388.49	12.19	12.13	1.75
11,811.00	51.57	54.66	11,731.98	343.89	413.99	405.72	11.76	11.63	2.34
11,842.00	54.50	54.39	11,750.62	358.26	434.16	423.13	9.48	9.45	-0.87
11,874.00	56.76	53.12	11,768.68	373.88	455.46	441.96	7.79	7.06	-3.97
11,900.00	58.08	52.90	11,782.68	387.06	472.96	457.77	5.13	5.08	-0.85
11,972.00	62.96	51.73	11,818.10	425.38	522.54	503.53	6.92	6.78	-1.63
12,066.00	74.25	49.69	11,852.34	480.76	590.12	569.01	12.18	12.01	-2.17
12,098.00	76.02	47.95	11,860.55	501.12	613.40	592.84	7.63	5.53	-5.44
12,129.00	78.05	48.29	11,867.51	521.29	635.89	616.34	6.64	6.55	1.10
12,160.00	79.56	47.60	11,873.53	541.66	658.47	640.06	5.34	4.87	-2.23



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-7MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-7MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
12,191.00	83.28	48.70	11,878.15	562.10	681.30	663.90	12.50	12.00	3.55	
12,223.00	86.17	48.83	11,881.09	583.10	705.26	688.47	9.04	9.03	0.41	
12,254.00	85.03	47.89	11,883.47	603.64	728.36	712.43	4.76	-3.68	-3.03	
12,348.00	83.77	45.43	11,892.64	667.84	796.39	786.69	2.93	-1.34	-2.62	
12,442.00	86.07	45.70	11,900.97	733.39	863.24	862.10	2.46	2.45	0.29	
12,535.00	87.38	43.71	11,906.28	799.37	928.55	937.68	2.56	1.41	-2.14	
12,629.00	88.39	43.52	11,909.75	867.38	993.35	1,015.19	1.09	1.07	-0.20	
12,723.00	86.10	41.05	11,914.27	936.83	1,056.51	1,093.85	3.58	-2.44	-2.63	
12,816.00	87.35	39.03	11,919.58	1,007.91	1,116.24	1,173.57	2.55	1.34	-2.17	
12,910.00	90.10	38.72	11,921.67	1,081.07	1,175.21	1,255.23	2.94	2.93	-0.33	
13,003.00	89.83	34.69	11,921.73	1,155.61	1,230.79	1,337.70	4.34	-0.29	-4.33	
13,097.00	88.72	33.50	11,922.92	1,233.44	1,283.48	1,422.97	1.73	-1.18	-1.27	
13,191.00	87.45	33.52	11,926.06	1,311.77	1,335.34	1,508.59	1.35	-1.35	0.02	
13,285.00	87.78	31.74	11,929.97	1,390.87	1,385.98	1,594.77	1.92	0.35	-1.89	
13,379.00	84.55	28.59	11,936.26	1,471.93	1,433.10	1,682.33	4.79	-3.44	-3.35	
13,473.00	85.05	27.19	11,944.78	1,554.67	1,476.89	1,771.01	1.58	0.53	-1.49	
13,567.00	85.06	25.76	11,952.88	1,638.50	1,518.64	1,860.44	1.52	0.01	-1.52	
13,661.00	84.86	22.45	11,961.14	1,723.95	1,556.88	1,950.91	3.51	-0.21	-3.52	
13,755.00	89.60	25.28	11,965.68	1,809.78	1,594.85	2,041.71	5.87	5.04	3.01	
13,849.00	90.37	27.09	11,965.71	1,894.13	1,636.33	2,131.61	2.09	0.82	1.93	
13,943.00	87.48	22.51	11,967.47	1,979.41	1,675.74	2,222.10	5.76	-3.07	-4.87	
14,037.00	86.81	20.74	11,972.16	2,066.69	1,710.34	2,313.79	2.01	-0.71	-1.88	
14,131.00	86.51	17.25	11,977.63	2,155.40	1,740.88	2,406.25	3.72	-0.32	-3.71	
14,225.00	87.05	15.50	11,982.91	2,245.44	1,767.33	2,499.36	1.95	0.57	-1.86	
14,318.00	86.61	10.33	11,988.06	2,335.92	1,788.08	2,592.00	5.57	-0.47	-5.56	
14,413.00	90.34	7.83	11,990.59	2,429.67	1,803.06	2,686.94	4.73	3.93	-2.63	
14,506.00	88.15	5.41	11,991.81	2,522.03	1,813.78	2,779.82	3.51	-2.35	-2.60	
14,600.00	85.83	0.99	11,996.75	2,615.73	1,819.02	2,873.15	5.30	-2.47	-4.70	
14,693.00	83.41	6.64	12,005.48	2,708.07	1,825.17	2,965.28	6.58	-2.60	6.08	
14,786.00	85.93	4.06	12,014.12	2,800.25	1,833.80	3,057.65	3.87	2.71	-2.77	
14,880.00	86.94	2.46	12,019.96	2,893.91	1,839.13	3,150.96	2.01	1.07	-1.70	
14,974.00	88.22	0.06	12,023.93	2,987.79	1,841.20	3,243.97	2.89	1.36	-2.55	
15,068.00	84.39	357.84	12,029.99	3,081.56	1,839.48	3,336.25	4.71	-4.07	-2.36	
15,162.00	85.23	357.46	12,038.49	3,175.09	1,835.64	3,427.96	0.98	0.89	-0.40	
15,256.00	88.96	356.45	12,043.26	3,268.82	1,830.66	3,519.69	4.11	3.97	-1.07	
15,350.00	89.13	355.40	12,044.82	3,362.57	1,823.98	3,611.16	1.13	0.18	-1.12	
15,445.00	89.80	358.07	12,045.71	3,457.40	1,818.57	3,703.90	2.90	0.71	2.81	
15,539.00	89.90	358.27	12,045.96	3,551.36	1,815.57	3,796.16	0.24	0.11	0.21	
15,634.00	88.25	357.20	12,047.49	3,646.26	1,811.81	3,889.24	2.07	-1.74	-1.13	
15,728.00	90.84	356.95	12,048.24	3,740.13	1,807.02	3,981.13	2.77	2.76	-0.27	
15,822.00	88.93	356.92	12,048.43	3,833.99	1,801.99	4,072.98	2.03	-2.03	-0.03	
15,916.00	90.97	357.47	12,048.51	3,927.87	1,797.39	4,164.92	2.25	2.17	0.59	
16,010.00	89.50	356.55	12,048.12	4,021.74	1,792.49	4,256.79	1.84	-1.56	-0.98	



Scientific Drilling

Survey Report



Company:	Middle Fork Energy Uinta, LLC	Local Co-ordinate Reference:	Well Dobby 1236-7MVH
Project:	Uintah County, UT	TVD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Site:	Dobby 33-12-722 Pad	MD Reference:	GL 5347.4' & RKB 26' @ 5373.40ft (Cyclone 34)
Well:	Dobby 1236-7MVH	North Reference:	True
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Casper

Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
16,104.00	88.02	357.35	12,050.16	4,115.58	1,787.49	4,348.62	1.79	-1.57	0.85
16,198.00	89.40	358.07	12,052.27	4,209.48	1,783.73	4,440.71	1.66	1.47	0.77
16,291.00	89.46	359.80	12,053.20	4,302.46	1,782.01	4,532.21	1.86	0.06	1.86
16,385.00	85.53	358.28	12,057.31	4,396.33	1,780.43	4,624.62	4.48	-4.18	-1.62
16,480.00	87.95	0.30	12,062.71	4,491.16	1,779.26	4,718.04	3.32	2.55	2.13
16,573.00	90.47	1.98	12,063.99	4,584.12	1,781.11	4,810.10	3.26	2.71	1.81
16,668.00	90.00	1.60	12,063.60	4,679.07	1,784.08	4,904.30	0.64	-0.49	-0.40
16,761.00	90.74	1.88	12,063.00	4,772.03	1,786.90	4,996.51	0.85	0.80	0.30
16,856.00	89.19	2.30	12,063.06	4,866.96	1,790.37	5,090.77	1.69	-1.63	0.44
16,950.00	89.70	4.92	12,063.97	4,960.76	1,796.28	5,184.31	2.84	0.54	2.79
17,044.00	89.53	3.46	12,064.60	5,054.51	1,803.15	5,277.95	1.56	-0.18	-1.55
17,139.00	88.93	3.62	12,065.88	5,149.32	1,809.02	5,372.47	0.65	-0.63	0.17
17,233.00	89.73	2.10	12,066.98	5,243.19	1,813.71	5,465.89	1.83	0.85	-1.62
17,327.00	90.44	2.21	12,066.84	5,337.12	1,817.24	5,559.17	0.76	0.76	0.12
17,420.00	90.00	1.49	12,066.48	5,430.07	1,820.24	5,651.41	0.91	-0.47	-0.77
17,514.00	90.03	1.02	12,066.46	5,524.05	1,822.30	5,744.50	0.50	0.03	-0.50
17,608.00	90.84	1.19	12,065.74	5,618.03	1,824.12	5,837.56	0.88	0.86	0.18
17,701.00	89.26	0.04	12,065.66	5,711.02	1,825.11	5,929.51	2.10	-1.70	-1.24
17,795.00	89.83	359.97	12,066.41	5,805.02	1,825.12	6,022.30	0.61	0.61	-0.07
17,889.00	88.93	359.61	12,067.42	5,899.01	1,824.78	6,115.02	1.03	-0.96	-0.38
17,983.00	86.17	0.32	12,071.44	5,992.91	1,824.72	6,207.71	3.03	-2.94	0.76
18,018.00	87.01	0.50	12,073.52	6,027.85	1,824.97	6,242.23	2.45	2.40	0.51
18,124.00	89.36	0.85	12,076.88	6,133.78	1,826.22	6,347.00	2.24	2.22	0.33
18,218.00	88.19	0.47	12,078.89	6,227.75	1,827.30	6,439.93	1.31	-1.24	-0.40
18,311.00	87.99	2.07	12,081.99	6,320.67	1,829.36	6,531.99	1.73	-0.22	1.72
18,405.00	89.46	2.19	12,084.08	6,414.58	1,832.85	6,625.24	1.57	1.56	0.13
18,499.00	91.58	1.59	12,083.23	6,508.52	1,835.95	6,718.47	2.34	2.26	-0.64
18,593.00	90.84	359.45	12,081.24	6,602.49	1,836.81	6,811.36	2.41	-0.79	-2.28
18,687.00	90.64	358.59	12,080.03	6,696.47	1,835.20	6,903.87	0.94	-0.21	-0.91
18,782.00	90.97	358.92	12,078.70	6,791.44	1,833.13	6,997.28	0.49	0.35	0.35
18,876.00	91.71	358.93	12,076.50	6,885.39	1,831.37	7,089.75	0.79	0.79	0.01
19,025.00	91.71	358.93	12,072.05	7,034.30	1,828.59	7,236.29	0.00	0.00	0.00

Checked By: _____ Approved By: _____ Date: _____
