

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 8

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

1. WELL NAME
RW 2733C-3MVH

2. TYPE OF WELL
Gas Well

3. TYPE OF WORK
DRILL NEW ☒ REENTER P&A ☐ DEEPEN ☐ RECOMP ☐

4. API NUMBER
4304757356

5. NAME OF OPERATOR
Middle Fork Energy Uinta, LLC

6. OPERATOR PHONE
435-789-1017

7. FIELD NAME
RED WASH

8. ADDRESS OF OPERATOR
1401 Wynkoop Street, Suite 300, Denver, CO, 80202

9. OPERATOR E-MAIL
jillj@uintahgroup.com

10. UNIT NAME
RED WASH

11. MINERAL LEASE NUMBER
0000829

12. MINERAL OWNERSHIP
FEDERAL

13. SURFACE OWNERSHIP
FEDERAL

14. COUNTY
UINTAH

15. DATE SPUDDED (SPUD RIG)
04/09/2024

16. DATE SPUDDED (ROTARY RIG)
05/02/2024

17. DATE TOTAL DEPTH REACHED
06/02/2024

18. DATE COMPLETED/ABANDONED
07/28/2024

19. DATE OF FIRST PROD. / INJ.
PROD:07/31/2024 INJ:

20. DEPTH REFERENCE
GROUND LEVEL ☒ KELLY BUSHING ☐ DERRICK FLOOR ☐

21. DEPTH REFERENCE ELEVATION
5738 (US Feet)

22. GRADED GROUND LEVEL ELEVATION
5738 (US Feet)

23. WELLBORE DEVIATION PROFILE
VERTICAL ☐ DIRECTIONAL ☐ HORIZONTAL ☒

24. TOTAL DEPTH
MD 19054 TVD 9528

25. PLUGGED BACK TOTAL DEPTH
MD 19054 TVD 9528

26. CURRENT WELL STATUS
Producing

27. LOCATION OF WELL									
WELL POSITION	FOOTAGES		QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN	UTM EASTING	UTM NORTHING
Surface	250 FNL	925 FWL	NWNW	27	7.0 S	24.0 E	S	652681	4450061
Producing Interval Top	1253 FNL	854 FWL	NWNW	27	7.0 S	24.0 E	S		
Producing Interval Bottom	513 FSL	1834 FEL	SWSE	33	7.0 S	24.0 E	S		
Total Depth	507 FSL	1831 FEL	SWSE	33	7.0 S	24.0 E	S		

28. HOLE, CASING AND CEMENT INFORMATION															
STRING	HOLE SIZE	CASING O.D.	WEIGHT	GRADE	THREAD	TOP (MD)	BOTTOM (MD)	DV TOOL DEPTH	LEAD TAIL	CEMENT TYPE	SACKS	YIELD	WEIGHT	CEMENT TOP	BASIS FOR TOP
COND	24.0	16.0	42.05	X-52	LTC	0	146		L	Class G Cement	282	1.16	15.8	0	
SURF	12.25	9.625	40.0	L-80	LTC	0	3325		L	Class G Cement	630	2.89	11.5	0	
									T	Class G Cement	240	1.16	15.8		
INT	8.75	7.0	29.0	HCP-110	LTC	0	9772		L	Class G Cement	850	2.46	12.0	0	
									T	Class G Cement	190	1.56	13.5		
PROD	6.125	4.5	13.5	P-110	BTC	9011	19052		L	Class G Cement	900	1.31	14.0	9011	

29. TUBING RECORD			
TUBING SIZE	TOP (MD)	BOT (MD)	PACKER DEPTH
4.5	0	9030	

30. RETRIEVABLE / TEMPORARY PLUGS		
PLUG	DEPTH (MD)	TYPE

31. PERMANENT / ABANDONMENT PLUGS		
PLUG	TOP (MD)	BOTTOM (MD)

32. FORMATION DETAILS and STRATIGRAPHIC MARKERS				
FR	FORMATION NAME	TOP (MD)	TOP (TVD)	DESCRIPTION, CONTENTS, ETC.
1	GREEN RIVER	2492	2492	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
2	BIRDS NEST	2691	2691	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
3	MAHOGANY	3326	3326	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
4	WASATCH	5585	5575	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
5	MESA VERDE	7396	7368	
	OIL SHOW? ☒ GAS SHOW? ☒ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☒ COMMINGLED? ☐			

33. COMPLETED and TESTED INTERVALS (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)						
FR	TOP (MD)	BOTTOM (MD)	TOP (TVD)	BOTTOM (TVD)	STIMULATION TREATMENT	INTERVAL STATUS
5	9826	18997	9642	9530	Fracture Stimulated	PRODUCING

34A. PRODUCTION INFORMATION (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)									
FR	TOP (MD)	BOTTOM (MD)	DATE FIRST PROD.	TEST DATE	HRS. TESTED	TBG. PRESSURE	CSG. PRESSURE	PROD. METHOD	
5	9826	18997	07/31/2024	08/27/2024	24	0	486	Flowing	
	TEST PRODUCTION VOLUMES			24-HOUR PRODUCTION RATES			GAS-OIL RATIO	OIL API	GAS BTU
	OIL (BBL)	GAS (MSCF)	WATER (BBL)	OIL (BBL)	GAS (MSCF)	WATER (BBL)	92167	0.0	
	36	3318	3477	36	3318	3477			

35. WELL TREATMENTS (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)						
FR	TREATMENT TYPE	TOP (MD)	BOTTOM (MD)	START DATE	END DATE	AMOUNT AND TYPE OF MATERIAL
5	Fracture Stimulation	9826	18997	07/09/2024	07/28/2024	197,502 BBLs FRESH WATER - 9,215,220 LBS PROPPANT - 62 STAGES

36. LOGS, SURVEYS, AND REPORTS (PDF file of each and LAS file of logs if available are to be submitted.)	
REPORTS AND OTHER INFORMATION.	
Dx Survey ☐	DST Report ☐
Core Analysis ☐	DOGMI Form 7 ☐
Geologic Report ☐	Wellbore Diagram ☐
Other ☐	
SUBMITTED PDF LOGS	SUBMITTED LAS LOGS
GAMMA RAY, CEMENT BOND	

OGM Official Use Only



37. I hereby certify that the foregoing and attached information is complete as determined from all available records.		
NAME	TITLE	DATE
Karlyn Linarte	Permitting Tech - Uintah Group Permitting	09/17/2024
SIGNATURE	PHONE	EMAIL
N/A	435-789-1017	klinarte@uintahgroup.com

LEGEND:

- = SURFACE HOLE LOCATION.
- ◆ = KICK OFF POINT/ PENETRATION POINT.
- ☆ = CROSSING.
- = BOTTOM HOLE LOCATION.
- ▲ = SECTION CORNERS LOCATED.

NOTE:

- Distances referenced on plot to section lines are perpendicular.
- Wellbore data provided by: MIDDLE FORK ENERGY UINTA, LLC.
- As-Drilled wellhead has not been field verified.
- Colored areas within section lines represent Federal oil & gas leases.

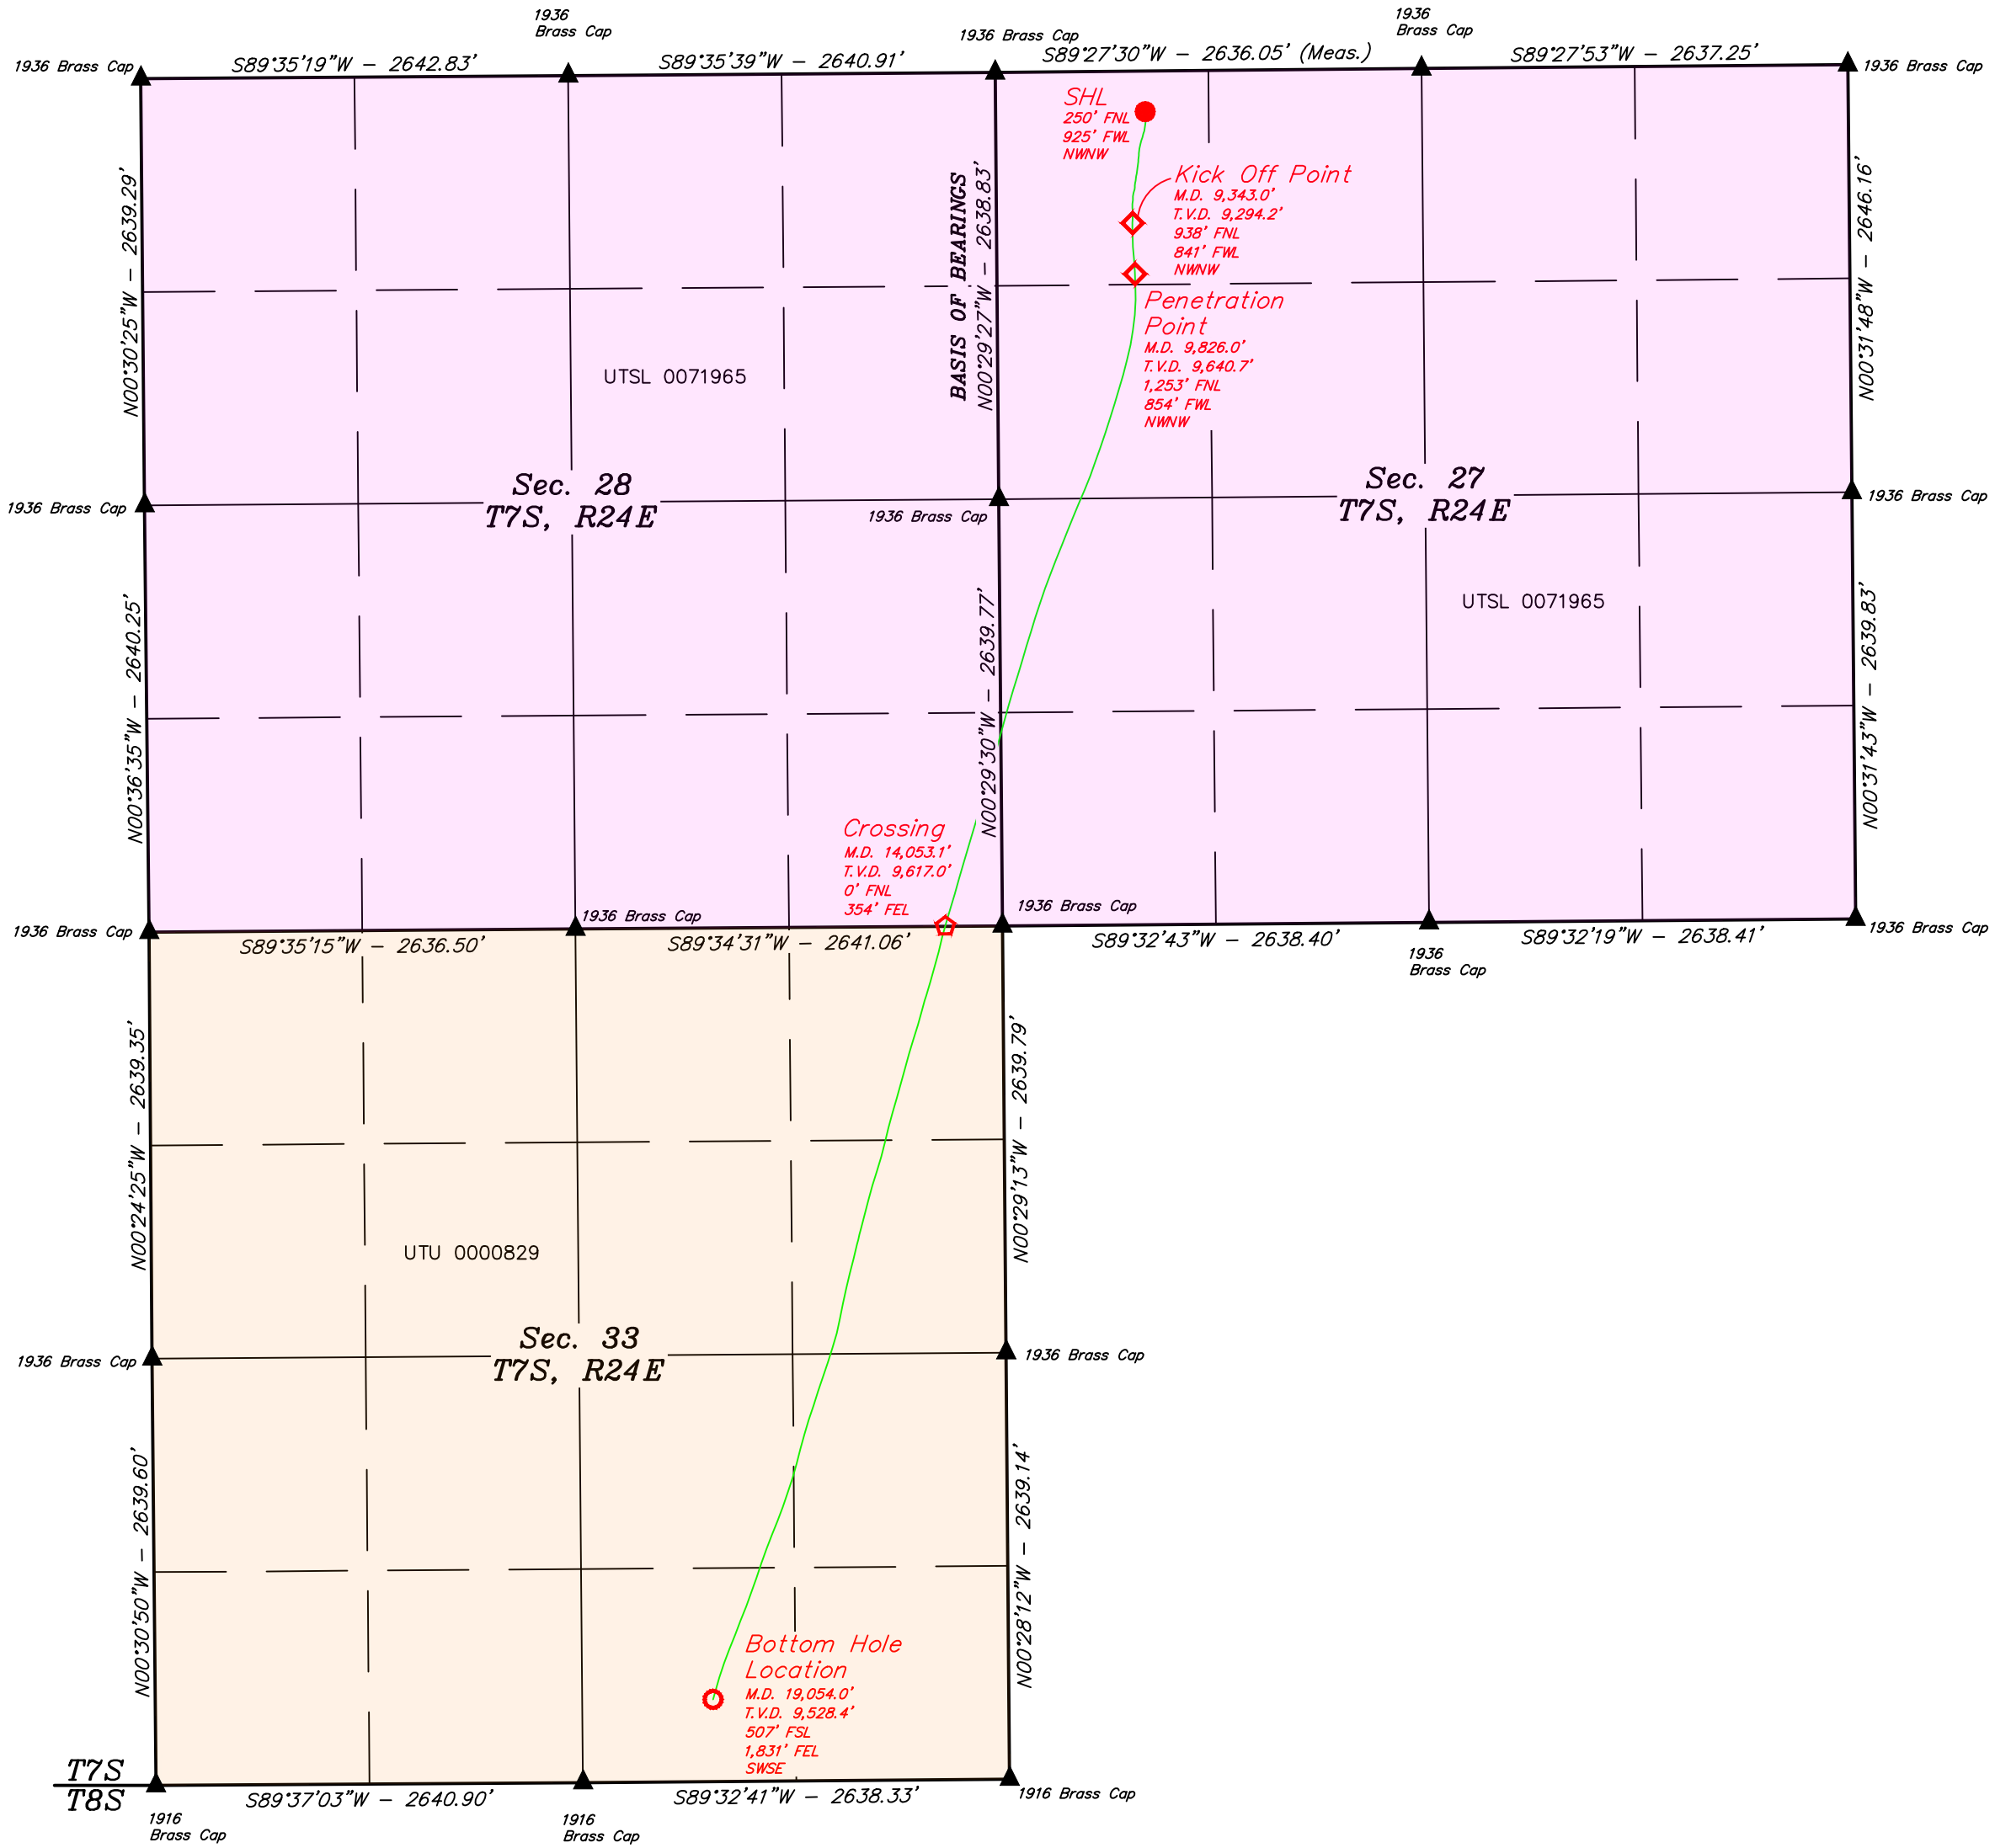

EXISTING GROUND ELEVATION = 3,740.5'

NAD 83 (SURFACE HOLE LOCATION)	NAD 83 (KICK OFF POINT)	NAD 83 (PENETRATION POINT)	NAD 83 (CROSSING)	NAD 83 (BOTTOM HOLE LOCATION)
LATITUDE = 40°11'13.39" (40.187051°)	LATITUDE = 40°11'06.59" (40.185163°)	LATITUDE = 40°11'03.48" (40.184299°)	LATITUDE = 40°10'23.71" (40.173253°)	LATITUDE = 40°09'36.58" (40.160162°)
LONGITUDE = -109°12'23.29" (-109.206471°)	LONGITUDE = -109°12'24.38" (-109.206772°)	LONGITUDE = -109°12'24.22" (-109.206728°)	LONGITUDE = -109°12'39.79" (-109.211054°)	LONGITUDE = -109°12'58.83" (-109.216342°)
NAD 27 (SURFACE HOLE LOCATION)	NAD 27 (KICK OFF POINT)	NAD 27 (PENETRATION POINT)	NAD 27 (CROSSING)	NAD 27 (BOTTOM HOLE LOCATION)
LATITUDE = 40°11'13.51" (40.187086°)	LATITUDE = 40°11'06.71" (40.185198°)	LATITUDE = 40°11'03.60" (40.184334°)	LATITUDE = 40°10'23.83" (40.173287°)	LATITUDE = 40°09'36.71" (40.160197°)
LONGITUDE = -109°12'20.86" (-109.205793°)	LONGITUDE = -109°12'21.94" (-109.206095°)	LONGITUDE = -109°12'21.78" (-109.206051°)	LONGITUDE = -109°12'37.36" (-109.210377°)	LONGITUDE = -109°12'56.40" (-109.215666°)
STATE PLANE NAD 83 (UT. CENTRAL)	STATE PLANE NAD 83 (UT. CENTRAL)	STATE PLANE NAD 83 (UT. CENTRAL)	STATE PLANE NAD 83 (UT. CENTRAL)	STATE PLANE NAD 83 (UT. CENTRAL)
N: 7245073.51' E: 2281099.06'	N: 7244383.85' E: 2281032.59'	N: 7244069.41' E: 2281052.89'	N: 7240015.90' E: 2279947.65'	N: 7235211.28' E: 2278592.10'
UTM, NAD 83 (ZONE 12, METERS)	UTM, NAD 83 (ZONE 12, METERS)	UTM, NAD 83 (ZONE 12, METERS)	UTM, NAD 83 (ZONE 12, METERS)	UTM, NAD 83 (ZONE 12, METERS)
Y: 4450060.73 X: 652680.80	Y: 4449850.64 X: 652659.40	Y: 4449754.77 X: 652665.06	Y: 4448521.15 X: 652321.47	Y: 4447059.02 X: 651900.34
UTM, NAD 27 (ZONE 12, METERS)	UTM, NAD 27 (ZONE 12, METERS)	UTM, NAD 27 (ZONE 12, METERS)	UTM, NAD 27 (ZONE 12, METERS)	UTM, NAD 27 (ZONE 12, METERS)
Y: 4449855.40 X: 652742.40	Y: 4449645.31 X: 652721.00	Y: 4449549.44 X: 652726.66	Y: 4448315.83 X: 652383.07	Y: 4446853.71 X: 651961.92

CERTIFICATE
THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED BY THE SURVEYOR AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF HIS KNOWLEDGE AND BELIEF.
REGISTERED LAND SURVEYOR
STATE OF UTAH
DATE OF PLAT: 09-12-24

BASIS OF ELEVATION
OPUS SOLUTION GENERATED NAVD 88

UELS, LLC
Corporate Office * 85 South 200 East
Vernal, UT 84078 * (435) 789-1017



MIDDLE FORK ENERGY UINTA, LLC

RW 2733C-3MVH
SHL: SECTION 27, T7S, R24E, S.L.B.&M.
UINTAH COUNTY, UTAH

SURVEYED BY	B.H.	03-29-24	SCALE
DRAWN BY	T.L.R.	09-12-24	1" = 1000'
AS-DRILLED WELL LOCATION PLAT			

RECEIVED: Sep. 19, 2024



Middle Fork Daily Completion Activity Report

Well Name: RW 2733C-3MVH

API/UWI 4304757356	Surface Legal Location S27-T7S-R24E	Field Name RED WASH	License # UTU-829	State/Province UTAH	Well Configuration Type HORIZONTAL
Ground Elevation (ft) 5,738.20	Casing Flange Elevation (ft) 5,734.85	KB-Ground Distance (ft) 26.00	KB-Casing Flange Distance (ft) 29.35	Surface Spud Date 5/2/2024 04:30	Rig Release Date 6/4/2024 02:30

Job Category COMPLETION			
Rpt #	Start Date	End Date	Summary
5.0	6/28/2024	6/29/2024	RU TWG run guage rings, run CBL RD TWG
6.0	6/29/2024	6/30/2024	ND HCR NU BOP & test
8.0	7/2/2024	7/3/2024	Polish L/T and PBR POOH LD Tubing
9.0	7/3/2024	7/4/2024	PU Seal Assm RIH with 4-1/2" frac string land and install master valve SIW
10.0	7/4/2024	7/5/2024	RU Cal frac & straightline testing. Try & test frac string no luck!
11.0	7/5/2024	7/6/2024	Test frac string, NO TEST! NU frac stack
12.0	7/8/2024	7/9/2024	Set Plug Test Casing
13.0	7/9/2024	7/10/2024	Perf Stage 1 & D-Fit
14.0	7/17/2024	7/18/2024	Rig in Well Head & Zipper Manifold
15.0	7/18/2024	7/19/2024	MIRU Frac and Wireline
16.0	7/19/2024	7/20/2024	Frac Stages 1-4 Perf Stages 2-4. RIH to perforate stage-5
17.0	7/20/2024	7/21/2024	Perf Stages 5-8 Frac Stages 5-7
18.0	7/21/2024	7/22/2024	Frac Stages 8-14 Perf Stages 9-15,
19.0	7/22/2024	7/23/2024	Frac Stages 15-22 Perf Stages 16-23
20.0	7/23/2024	7/24/2024	Perf Stages 23-31 Frac Stages 23-31
21.0	7/24/2024	7/25/2024	Frac Stages 32-37, Perf stages 32-37. RIH to perf 38
22.0	7/25/2024	7/26/2024	Perf Stages 38-44 Frac Stages 38-44
23.0	7/26/2024	7/27/2024	Perf Stages 45-53 Frac Stages 45-52. Begin stage 53 Frac ops.
24.0	7/27/2024	7/28/2024	Frac Stages 53-62 Perf Stages 54-62, Set Kill Plug.
25.0	7/28/2024	7/29/2024	Set kill plug, Rig down frac Ops
26.0	7/30/2024	7/31/2024	Install tools, Pressure test equip to 6,500 psi, D/O Plugs #68 - #1. Mill on obstructions/PBTD
27.0	7/31/2024	8/1/2024	Clean out to PBTD. Pump sweeps. Pooh turn over to production team.



UT Well Completion Report and Log

Well Name: RW 2733C-3MVH

Fluid Type GAS		Well Subtype NEW DRILL		Operator MIDDLE FORK ENERGY UINTA		Lease	
Surface Legal Location S27-T7S-R24E		North/South Distance (ft) 250.0		N/S Ref FNL		East/West Distance (ft) 925.0	
Ground Elevation (ft) 5,738.20		KB-Ground Distance (ft) 26.00		Total Depth (All) (ftKB) ORIGINAL HOLE - 19,054.0		Total Depth All (TVD) (ftKB) ORIGINAL HOLE - 9,528.4	
Conductor Spud Date 4/9/2024		Surface Spud Date 5/2/2024		Rig Release Date 6/4/2024		Well Name RW 2733C-3MVH	
						API/UWI 4304757356	
						Field Name RED WASH	
TD Date End Date 6/2/2024		Frac Start Date Date 7/9/2024		Completed Date Date 7/28/2024		Initial Production Date On Production Date	

Wellbores

Profile Type Directional	Actual Deviation Survey Table Deviation Survey
-----------------------------	---

Casing Strings

Csg Des	Hole Size (in)	Casing OD (in)	Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
Conductor	24	16	X-52	42.05	29.4	146.0
Surface	12 1/4	9 5/8	HCL-80	40.00	29.4	3,325.0
Intermediate	8 3/4	7	HCP-110	29.00	29.4	9,772.0
Production Liner	6 1/8	4 1/2	P-110 HC	13.50	9,010.5	19,052.0

Casing Components

Csg Des	Item Des	Top (ftKB)	Btm (ftKB)

Cement Fluids

Casing Description Conductor	Stg # 1	Fluid Type Tail	Class G	Amount (sacks) 282	Yield (ft³/sack) 1.16	Density (lb/gal) 15.80	Final Top 29.4
Casing Description Surface	Stg # 1	Fluid Type Lead	Class G	Amount (sacks) 630	Yield (ft³/sack) 2.89	Density (lb/gal) 11.50	Final Top 29.4
Casing Description Surface	Stg # 1	Fluid Type Tail	Class G	Amount (sacks) 240	Yield (ft³/sack) 1.16	Density (lb/gal) 15.80	Final Top 2,834.0
Casing Description Intermediate	Stg # 1	Fluid Type Lead	Class G	Amount (sacks) 850	Yield (ft³/sack) 2.46	Density (lb/gal) 12.00	Final Top 29.4
Casing Description Intermediate	Stg # 1	Fluid Type Tail	Class G	Amount (sacks) 190	Yield (ft³/sack) 1.56	Density (lb/gal) 13.50	Final Top 7,948.0
Casing Description Production Liner	Stg # 1	Fluid Type Tail	Class G	Amount (sacks) 900	Yield (ft³/sack) 1.31	Density (lb/gal) 14.00	Final Top 9,011.0

Tubing Record:

String Max Nominal OD (in) 4 1/2	Tubing Set Depth (ftKB) 9,030.4	Tubing Land Date 7/3/2024
-------------------------------------	------------------------------------	------------------------------

Perforations

Formation	Top (ftKB)	Btm (ftKB)	Top (TVD) (ftKB)	Btm (TVD) (ftKB)	Est Hole Dia (in)	Shot Dens (shots/ft)	Sum of Calculated Shot Total	Current Status
	9,826.0	9,953.0	9,642.1	9,679.2		3.0	45	Open - Flowing (9,826.0 - 9,827.0 ftKB)
	9,961.0	10,088.0	9,680.4	9,685.5		3.0	45	Open - Flowing (9,961.0 - 9,962.0 ftKB)
	10,096.0	10,223.0	9,685.2	9,680.1		3.0	45	Open - Flowing (10,096.0 - 10,097.0 ftKB)
	10,232.0	10,358.0	9,679.6	9,673.1		3.0	45	Open - Flowing (10,232.0 - 10,233.0 ftKB)
	10,367.0	10,491.0	9,672.8	9,668.4		3.0	45	Open - Flowing (10,367.0 - 10,368.0 ftKB)
	10,501.0	10,627.0	9,667.9	9,660.6		3.0	45	Open - Flowing (10,501.0 - 10,502.0 ftKB)
	10,636.0	10,762.0	9,660.0	9,651.3		3.0	45	Open - Flowing (10,636.0 - 10,637.0 ftKB)
	10,771.0	10,898.0	9,650.7	9,645.1		3.0	45	Open - Flowing (10,771.0 - 10,772.0 ftKB)
	10,906.0	11,047.0	9,645.0	9,644.1		3.0	45	Open - Flowing (10,906.0 - 10,907.0 ftKB)
	11,056.0	11,197.0	9,643.8	9,636.5		3.0	45	Open - Flowing (11,056.0 - 11,057.0 ftKB)
	11,206.0	11,347.0	9,636.0	9,628.7		3.0	45	Open - Flowing (11,206.0 - 11,207.0 ftKB)
	11,356.0	11,497.0	9,628.3	9,625.3		3.0	45	Open - Flowing (11,356.0 - 11,357.0 ftKB)
	11,506.0	11,647.0	9,625.3	9,626.9		3.0	45	Open - Flowing (11,506.0 - 11,507.0 ftKB)
	11,656.0	11,797.0	9,627.1	9,629.1		3.0	45	Open - Flowing (11,656.0 - 11,657.0 ftKB)
	11,806.0	11,944.0	9,629.0	9,628.2		3.0	45	Open - Flowing (11,806.0 - 11,807.0 ftKB)
	11,956.0	12,097.0	9,627.8	9,623.1		3.0	45	Open - Flowing (11,956.0 - 11,957.0 ftKB)
	12,106.0	12,247.0	9,623.0	9,622.9		3.0	45	Open - Flowing (12,106.0 - 12,107.0 ftKB)
	12,256.0	12,397.0	9,622.9	9,623.1		3.0	45	Open - Flowing (12,306.0 - 12,307.0 ftKB)
	12,406.0	12,547.0	9,623.0	9,620.8		3.0	45	Open - Flowing (12,406.0 - 12,407.0 ftKB)
	12,559.0	12,697.0	9,620.7	9,621.2		3.0	45	Open - Flowing (12,559.0 - 12,560.0 ftKB)
	12,706.0	12,845.0	9,621.2	9,620.7		3.0	45	Open - Flowing (12,706.0 - 12,707.0 ftKB)
	12,856.0	12,997.0	9,620.7	9,622.4		3.0	45	Open - Flowing (12,856.0 - 12,857.0 ftKB)
	13,006.0	13,147.0	9,622.6	9,623.8		3.0	45	Open - Flowing (13,006.0 - 13,007.0 ftKB)
	13,158.0	13,297.0	9,623.9	9,623.0		3.0	45	Open - Flowing (13,158.0 - 13,159.0 ftKB)
	13,306.0	13,447.0	9,622.8	9,620.9		3.0	45	Open - Flowing (13,306.0 - 13,317.0 ftKB)



UT Well Completion Report and Log

Well Name: RW 2733C-3MVH

Fluid Type GAS		Well Subtype NEW DRILL		Operator MIDDLE FORK ENERGY UINTA		Lease			
Surface Legal Location S27-T7S-R24E		North/South Distance (ft) 250.0		N/S Ref FNL	East/West Distance (ft) 925.0		E/W Ref FWL	Target Formation NESLEN LOWER	
Ground Elevation (ft) 5,738.20	KB-Ground Distance (ft) 26.00	Total Depth (All) (ftKB) ORIGINAL HOLE - 19,054.0			Total Depth All (TVD) (ftKB) ORIGINAL HOLE - 9,528.4			Well Name RW 2733C-3MVH	
Conductor Spud Date 4/9/2024		Surface Spud Date 5/2/2024			Rig Release Date 6/4/2024			API/UWI 4304757356	
								Field Name RED WASH	
TD Date		Frac Start Date		Completed Date		Initial Production Date			
End Date 6/2/2024		Date 7/9/2024		Date 7/28/2024		On Production Date			

Perforations

Formation	Top (ftKB)	Btm (ftKB)	Top (TVD) (ftKB)	Btm (TVD) (ftKB)	Est Hole Dia (in)	Shot Dens (shots/ft)	Sum of Calculated Shot Total	Current Status
	13,456.0	13,597.0	9,620.7	9,615.9		3.0	45	Open - Flowing (13,456.0 - 13,457.0 ftKB)
	13,606.0	13,747.0	9,615.7	9,615.9		3.0	45	Open - Flowing (13,606.0 - 13,607.0 ftKB)
	13,756.0	13,897.0	9,615.9	9,619.4		3.0	45	Open - Flowing (13,756.0 - 13,757.0 ftKB)
	13,906.0	14,047.0	9,619.5	9,616.5		3.0	45	Open - Flowing (13,906.0 - 13,907.0 ftKB)
	14,056.0	14,197.0	9,616.2	9,614.9		3.0	45	Open - Flowing (14,056.0 - 14,057.0 ftKB)
	14,206.0	14,347.0	9,614.4	9,602.3		3.0	45	Open - Flowing (14,206.0 - 14,207.0 ftKB)
	14,356.0	14,497.0	9,601.5	9,597.3		3.0	45	Open - Flowing (14,356.0 - 14,357.0 ftKB)
	14,506.0	14,647.0	9,597.4	9,601.5		3.0	45	Open - Flowing (14,506.0 - 14,507.0 ftKB)
	14,656.0	14,797.0	9,601.5	9,599.1		3.0	45	Open - Flowing (14,656.0 - 14,657.0 ftKB)
	14,806.0	14,947.0	9,598.9	9,598.4		3.0	45	Open - Flowing (14,806.0 - 14,807.0 ftKB)
	14,956.0	15,097.0	9,598.5	9,598.0		3.0	45	Open - Flowing (14,956.0 - 14,957.0 ftKB)
	15,106.0	15,247.0	9,597.7	9,591.3		3.0	45	Open - Flowing (15,106.0 - 15,107.0 ftKB)
	15,256.0	15,397.0	9,591.0	9,589.4		3.0	45	Open - Flowing (15,256.0 - 15,257.0 ftKB)
	15,406.0	15,547.0	9,589.3	9,584.6		3.0	45	Open - Flowing (15,406.0 - 15,407.0 ftKB)
	15,556.0	15,697.0	9,583.9	9,575.4		3.0	45	Open - Flowing (15,556.0 - 15,557.0 ftKB)
	15,706.0	15,847.0	9,575.0	9,576.3		3.0	45	Open - Flowing (15,706.0 - 15,707.0 ftKB)
	15,856.0	15,997.0	9,576.7	9,583.0		3.0	45	Open - Flowing (15,856.0 - 15,857.0 ftKB)
	16,006.0	16,147.0	9,583.6	9,586.9		3.0	45	Open - Flowing (16,006.0 - 16,007.0 ftKB)
	16,156.0	16,297.0	9,586.7	9,580.6		3.0	45	Open - Flowing (16,156.0 - 16,157.0 ftKB)
	16,306.0	16,446.0	9,580.2	9,576.4		3.0	45	Open - Flowing (16,306.0 - 16,307.0 ftKB)
	16,457.0	16,597.0	9,576.3	9,577.4		3.0	45	Open - Flowing (16,457.0 - 16,458.0 ftKB)
	16,606.0	16,746.0	9,577.5	9,574.2		3.0	45	Open - Flowing (16,606.0 - 16,607.0 ftKB)
	16,755.0	16,897.0	9,573.9	9,569.7		3.0	45	Open - Flowing (16,755.0 - 16,756.0 ftKB)
	16,906.0	17,047.0	9,569.5	9,567.1		3.0	45	Open - Flowing (16,906.0 - 16,907.0 ftKB)
	17,056.0	17,197.0	9,567.0	9,565.8		3.0	45	Open - Flowing (17,056.0 - 17,057.0 ftKB)
	17,206.0	17,347.0	9,565.7	9,565.6		3.0	45	Open - Flowing (17,206.0 - 17,207.0 ftKB)
	17,356.0	17,497.0	9,565.7	9,565.2		3.0	45	Open - Flowing (17,356.0 - 17,357.0 ftKB)
	17,506.0	17,647.0	9,565.0	9,563.1		3.0	45	Open - Flowing (17,506.0 - 17,507.0 ftKB)
	17,656.0	17,795.0	9,562.8	9,555.5		3.0	45	Open - Flowing (17,656.0 - 17,657.0 ftKB)
	17,806.0	17,947.0	9,554.6	9,542.8		3.0	45	Open - Flowing (17,806.0 - 17,807.0 ftKB)
	17,956.0	18,097.0	9,542.1	9,534.2		3.0	45	Open - Flowing (17,956.0 - 17,957.0 ftKB)
	18,106.0	18,247.0	9,534.0	9,534.9		3.0	45	Open - Flowing (18,106.0 - 18,107.0 ftKB)
	18,256.0	18,397.0	9,535.0	9,535.8		3.0	45	Open - Flowing (18,256.0 - 18,257.0 ftKB)
	18,406.0	18,547.0	9,535.6	9,532.3		3.0	45	Open - Flowing (18,406.0 - 18,407.0 ftKB)
	18,556.0	18,695.0	9,532.2	9,528.7		3.0	45	Open - Flowing (18,556.0 - 18,557.0 ftKB)
	18,706.0	18,847.0	9,528.4	9,526.0		3.0	45	Open - Flowing (18,706.0 - 18,707.0 ftKB)
	18,856.0	18,997.0	9,526.2	9,529.6		3.0	45	Open - Flowing (18,856.0 - 18,857.0 ftKB)

Total

2,790

Producing Intervals & Perforation Record:

Minimum of Top Depth (ftKB) 9,826.0	Maximum of Bottom Depth (ftKB) 18,997.0
--	--

Acid, Fracture, Treatment, Cement Squeeze, Etc.:

Type Hydraulic Frac	Number of Treatment Intervals 62	Volume Clean Total (bbl) 197,501.69	Proppant Total (lb) 9,215,220.3
Type Sand	Sand Size 100		

Fluid Name
Fresh Water

Plug Back Total Depths

Depth (ftKB)	Depth (TVD) (ftKB)
--------------	--------------------



UT Well Completion Report and Log

Well Name: RW 2733C-3MVH

Fluid Type GAS		Well Subtype NEW DRILL		Operator MIDDLE FORK ENERGY UINTA		Lease					
Surface Legal Location S27-T7S-R24E		North/South Distance (ft) 250.0		N/S Ref FNL		East/West Distance (ft) 925.0		E/W Ref FWL		Target Formation NESLEN LOWER	
Ground Elevation (ft) 5,738.20		KB-Ground Distance (ft) 26.00		Total Depth (All) (ftKB) ORIGINAL HOLE - 19,054.0		Total Depth All (TVD) (ftKB) ORIGINAL HOLE - 9,528.4		Well Name RW 2733C-3MVH			
Conductor Spud Date 4/9/2024		Surface Spud Date 5/2/2024		Rig Release Date 6/4/2024		API/UWI 4304757356					
						Field Name RED WASH					
TD Date End Date 6/2/2024		Frac Start Date Date 7/9/2024		Completed Date Date 7/28/2024		Initial Production Date On Production Date					

Zones			
Zone Name	Top (ftKB)	Btm (ftKB)	Final Top (ftKB)
Neslen	9,348.0		

Formations	
Formation Name	Final Top MD (ftKB)
BIRDS NEST	2,691.0
MAHOGANY	3,326.0
GREEN RIVER	2,492.0
WASATCH	5,585.0
MESAVERDE	7,396.0
