

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS AND MINING										FORM 8	
WELL COMPLETION OR RECOMPLETION REPORT AND LOG										1. WELL NAME Wild 62-3328-22F	
2. TYPE OF WELL Oil Well			3. TYPE OF WORK DRILL NEW ☒ REENTER P&A ☐ DEEPEN ☐ RECOMP ☐							4. API NUMBER 4301354308	
5. NAME OF OPERATOR XCL AssetCo, LLC					6. OPERATOR PHONE 720-208-8877			7. FIELD NAME UNDESIGNATED			
8. ADDRESS OF OPERATOR 600 N Shepherd Drive, Suite 390, Houston, TX, 77007					9. OPERATOR E-MAIL blake@xclresources.com			10. UNIT NAME			
11. MINERAL LEASE NUMBER MULTIPLE LEASES			12. MINERAL OWNERSHIP INDIAN,FEE			13. SURFACE OWNERSHIP FEE			14. COUNTY DUCHESNE		
15. DATE SPUDED (SPUD RIG) 03/14/2023		16. DATE SPUDED (ROTARY RIG) 05/24/2023		17. DATE TOTAL DEPTH REACHED 06/04/2023		18. DATE COMPLETED/ABANDONED 02/22/2024			19. DATE OF FIRST PROD. / INJ. PROD:04/17/2024 INJ:		
20. DEPTH REFERENCE GROUND LEVEL ☐ KELLY BUSHING ☒ DERRICK FLOOR ☐					21. DEPTH REFERENCE ELEVATION 5409 (US Feet)			22. GRADED GROUND LEVEL ELEVATION 5379 (US Feet)			
23. WELLBORE DEVIATION PROFILE VERTICAL ☐ DIRECTIONAL ☐ HORIZONTAL ☒					24. TOTAL DEPTH MD 20556 TVD 9948			25. PLUGGED BACK TOTAL DEPTH MD TVD			
26. CURRENT WELL STATUS Producing											

27. LOCATION OF WELL								
WELL POSITION	FOOTAGES	QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN	UTM EASTING	UTM NORTHING
Surface	460 FSL 334 FEL	SESE	32	2.0 S	2.0 W	U	574368	4456917
Producing Interval Top	131 FSL 1697 FWL	SESW	33	2.0 S	2.0 W	U		
Producing Interval Bottom	151 FNL 1710 FWL	NENW	28	2.0 S	2.0 W	U		
Total Depth	46 FSL 1709 FWL	NENW	28	2.0 S	2.0 W	U		

28. HOLE, CASING AND CEMENT INFORMATION															
STRING	HOLE SIZE	CASING O.D.	WEIGHT	GRADE	THREAD	TOP (MD)	BOTTOM (MD)	DV TOOL DEPTH	LEAD TAIL	CEMENT TYPE	SACKS	YIELD	WEIGHT	CEMENT TOP	BASIS FOR TOP
COND	16.0	16.0	36.0	J-55	NT	0	120		L	Class A Cement	447	1.21	14.0	0	Calculated
SURF	12.25	9.625	36.0	J-55	LTC	0	2578		L	Class G Cement	1170	1.13	16.0	0	Calculated
INT	8.75	7.0	29.0	P-110	NT	0	9092		T	Class G Cement	190	1.15	15.8		
									L	Class G Cement	710	2.51	12.0		
LINER	6.125	5.0	18.0	P-110	NT	8876	20522		T	Class G Cement	800	1.2	14.5		

29. TUBING RECORD			
TUBING SIZE	TOP (MD)	BOT (MD)	PACKER DEPTH

30. RETRIEVABLE / TEMPORARY PLUGS		
PLUG	DEPTH (MD)	TYPE

31. PERMANENT / ABANDONMENT PLUGS		
PLUG	TOP (MD)	BOTTOM (MD)

32. FORMATION DETAILS and STRATIGRAPHIC MARKERS				
FR	FORMATION NAME	TOP (MD)	TOP (TVD)	DESCRIPTION, CONTENTS, ETC.
1	GREEN RIVER	4276	4258	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
2	MAHOGANY BENCH	6340	6152	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
3	GARDEN GULCH	7893	7582	
	OIL SHOW? ☐ GAS SHOW? ☐ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☐ COMMINGLED? ☐			
4	GREEN RIVER - LOWER	8725	8342	
	OIL SHOW? ☒ GAS SHOW? ☒ WATER FLOW? ☐ DRILL STEM TESTED? ☐ CORED? ☐ COMPLETED OR TESTED? ☒ COMMINGLED? ☐			

33. COMPLETED and TESTED INTERVALS (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)						
FR	TOP (MD)	BOTTOM (MD)	TOP (TVD)	BOTTOM (TVD)	STIMULATION TREATMENT	INTERVAL STATUS
4	10250	20451	9494	9946	Fracture Stimulated	PRODUCING

34A. PRODUCTION INFORMATION (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)								
FR	TOP (MD)	BOTTOM (MD)	DATE FIRST PROD.	TEST DATE	HRS. TESTED	TBG. PRESSURE	CSG. PRESSURE	PROD. METHOD
	10250	20451	04/17/2024	05/30/2024	24		744	Flowing

4	TEST PRODUCTION VOLUMES			24-HOUR PRODUCTION RATES			GAS-OIL RATIO	OIL API	GAS BTU
	OIL (BBL)	GAS (MSCF)	WATER (BBL)	OIL (BBL)	GAS (MSCF)	WATER (BBL)	686	0.0	
	1849	1268	1499	1849	1268	1499			

35. WELL TREATMENTS (Formation Reference (FR) 1, 2, 3, ..., etc. as in Section 32.)						
FR	TREATMENT TYPE	TOP (MD)	BOTTOM (MD)	START DATE	END DATE	AMOUNT AND TYPE OF MATERIAL
4	Fracture Stimulation	10250	20451	11/02/2023	01/09/2024	please see attachments

36. LOGS, SURVEYS, AND REPORTS (PDF file of each and LAS file of logs if available are to be submitted.)						
REPORTS AND OTHER INFORMATION.						
Dx Survey ☒ DST Report ☐ Core Analysis ☐ DOGM Form 7 ☐ Geologic Report ☐ Wellbore Diagram ☐ Other ☐						
SUBMITTED PDF LOGS			SUBMITTED LAS LOGS			
MUD LOG, MEASURED WHILE DRILLING, CEMENT BOND, CALIPER			MUD LOG, MEASURED WHILE DRILLING, CEMENT BOND, CALIPER			

OGM Official Use Only

37. I hereby certify that the foregoing and attached information is complete as determined from all available records.		
NAME Oaklee Reary	TITLE Ops Tech-Regulatory	DATE 07/31/2024
SIGNATURE N/A	PHONE 435-823-1530	EMAIL oaklee@xclresources.com

NAD 83(2011) (BOTTOM HOLE LOCATION)
LATITUDE = N40°17'12.65754" (40.2868493°)
LONGITUDE = W110°07'05.34146" (-110.1181504°)

SPC UT C-4302
NORTHING = 7,276,190.269 (us ft)
EASTING = 2,025,892.620 (us ft)

UTM NAD 83 ZONE 12
NORTHING = 4,459,968.496 (m)
EASTING = 574,958.985 (m)

NAD 83(2011) (LAST TAKE POINT)
LATITUDE = N40°17'12.12067" (40.2867002°)
LONGITUDE = W110°07'05.33242" (-110.1181479°)

SPC UT C-4302
NORTHING = 7,276,135.962 (us ft)
EASTING = 2,025,894.160 (us ft)

UTM NAD 83 ZONE 12
NORTHING = 4,459,951.945 (m)
EASTING = 574,959.363 (m)

NAD 83(2011) (FIRST TAKE POINT)
LATITUDE = N40°15'30.67334" (40.2585204°)
LONGITUDE = W110°07'05.43674" (-110.1181769°)

SPC UT C-4302
NORTHING = 7,265,871.802 (us ft)
EASTING = 2,026,044.659 (us ft)

UTM NAD 83 ZONE 12
NORTHING = 4,456,824.027 (m)
EASTING = 574,988.022 (m)

NAD 83(2011) (KOP)
LATITUDE = N40°15'25.56828" (40.2571023°)
LONGITUDE = W110°07'08.46218" (-110.1190173°)

SPC UT C-4302
NORTHING = 7,265,351.672 (us ft)
EASTING = 2,025,818.121 (us ft)

UTM NAD 83 ZONE 12
NORTHING = 4,456,665.914 (m)
EASTING = 574,918.120 (m)

NAD 83(2011) (SURFACE LOCATION)
LATITUDE = N40°15'33.89268" (40.2594146°)
LONGITUDE = W110°07'31.62501" (-110.1254514°)

SPC UT C-4302
NORTHING = 7,266,166.240 (us ft)
EASTING = 2,024,009.700 (us ft)

UTM NAD 83 ZONE 12
NORTHING = 4,456,917.160 (m)
EASTING = 574,368.428 (m)

DATUM FOR REPORTED DISTANCES

- **MD** REPORTED IN STATE PLANE DISTANCES
- **TVD** REPORTED IN STATE PLANE DISTANCES
- **Δ NORTH & Δ EAST** ARE REPORTED IN STATE PLANE DISTANCES MEASURED TO THE SURFACE HOLE LOCATION (SHL)

***BASIS OF ELEVATION**

SPOT ELEVATION AT THE SOUTHEAST CORNER OF SECTION 32, T.2S., R.2W., U.S.B.&M. NAVD 88 DATUM, GEIOD12B, USING THE UTAH REFERENCE NETWORK SYSTEM. SAID ELEVATION IS 5,390.60 FEET.

LEGEND



FOUND SECTION CORNER

SURFACE HOLE LOCATION (SHL)

AS-DRILLED WELL PATH

DATA SOURCE:


"XCL Resources - WILD 62-3328-22F Surveys.xlsx"
COMPANY: XCL Resources
WELL NAME: WILD 62-3328-22F
SITE: Sprouse 32-4D-22 (Wild-Taparoo Pad)
WELLPATH: Wellbore #1
DESIGN: Surveys
STATE: UTAH
COUNTY: DUCHESNE

NOTES:

1. WELL FOOTAGES ARE MEASURED AT RIGHT ANGLES TO THE SECTION LINE USING LOCAL DISTANCES ROUNDED TO THE NEAREST FOOT.
2. BEARINGS ARE DERIVED FROM G.P.S. OBSERVATIONS AND EQUIPMENT.
3. THE GENERAL LAND OFFICE G.L.O. PLAT WAS USED FOR REFERENCE
4. **AS-DRILLED WELL PATH SHOWN HEREON WAS PLOTTED USING DATA PROVIDED TO OUTLAW ENGINEERING THAT WAS CONVERTED INTO THE LOCAL COORDINATE SYSTEM. THE WELL PATH SHOWN IS TRUE AND ACCURATE ONLY TO THE EXTENT OF THE RELIABILITY OF THE PROVIDED DATA SET.
5. ALL BEARINGS AND DISTANCES SHOWN HEREON ARE MEASURED IN A LOCAL COORDINATE SYSTEM UNLESS OTHERWISE NOTED.

G.P.S. LOCAL SITE PARAMETERS

TRANSVERSE MERCATOR PROJECTION
ORIGIN LATITUDE: N40°18'57.65023"
ORIGIN LONGITUDE: W110°06'18.93129"
PROJECT HEIGHT: 5,300 (usft)
GEOID MODEL: GEOID03 (Conus)




**OUTLAW
ENGINEERING INC.**
510 West 200 North
Roosevelt, UTAH 84066
(435) 232-4321



CERTIFICATE

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM THE FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION, AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.
REGISTERED LAND SURVEYOR, UTAH PLS #5047065





DATE SURVEYED: N/A
SURVEYED BY: N/A
DRAWN: 10/16/2023
DRAWN: JLW
SCALE: 1" = 1000'

SHEET NO.
1

**XCL
RESOURCES**

WELL PRE-COMPLETION PLAT

WELL: WILD 62-3328-22F

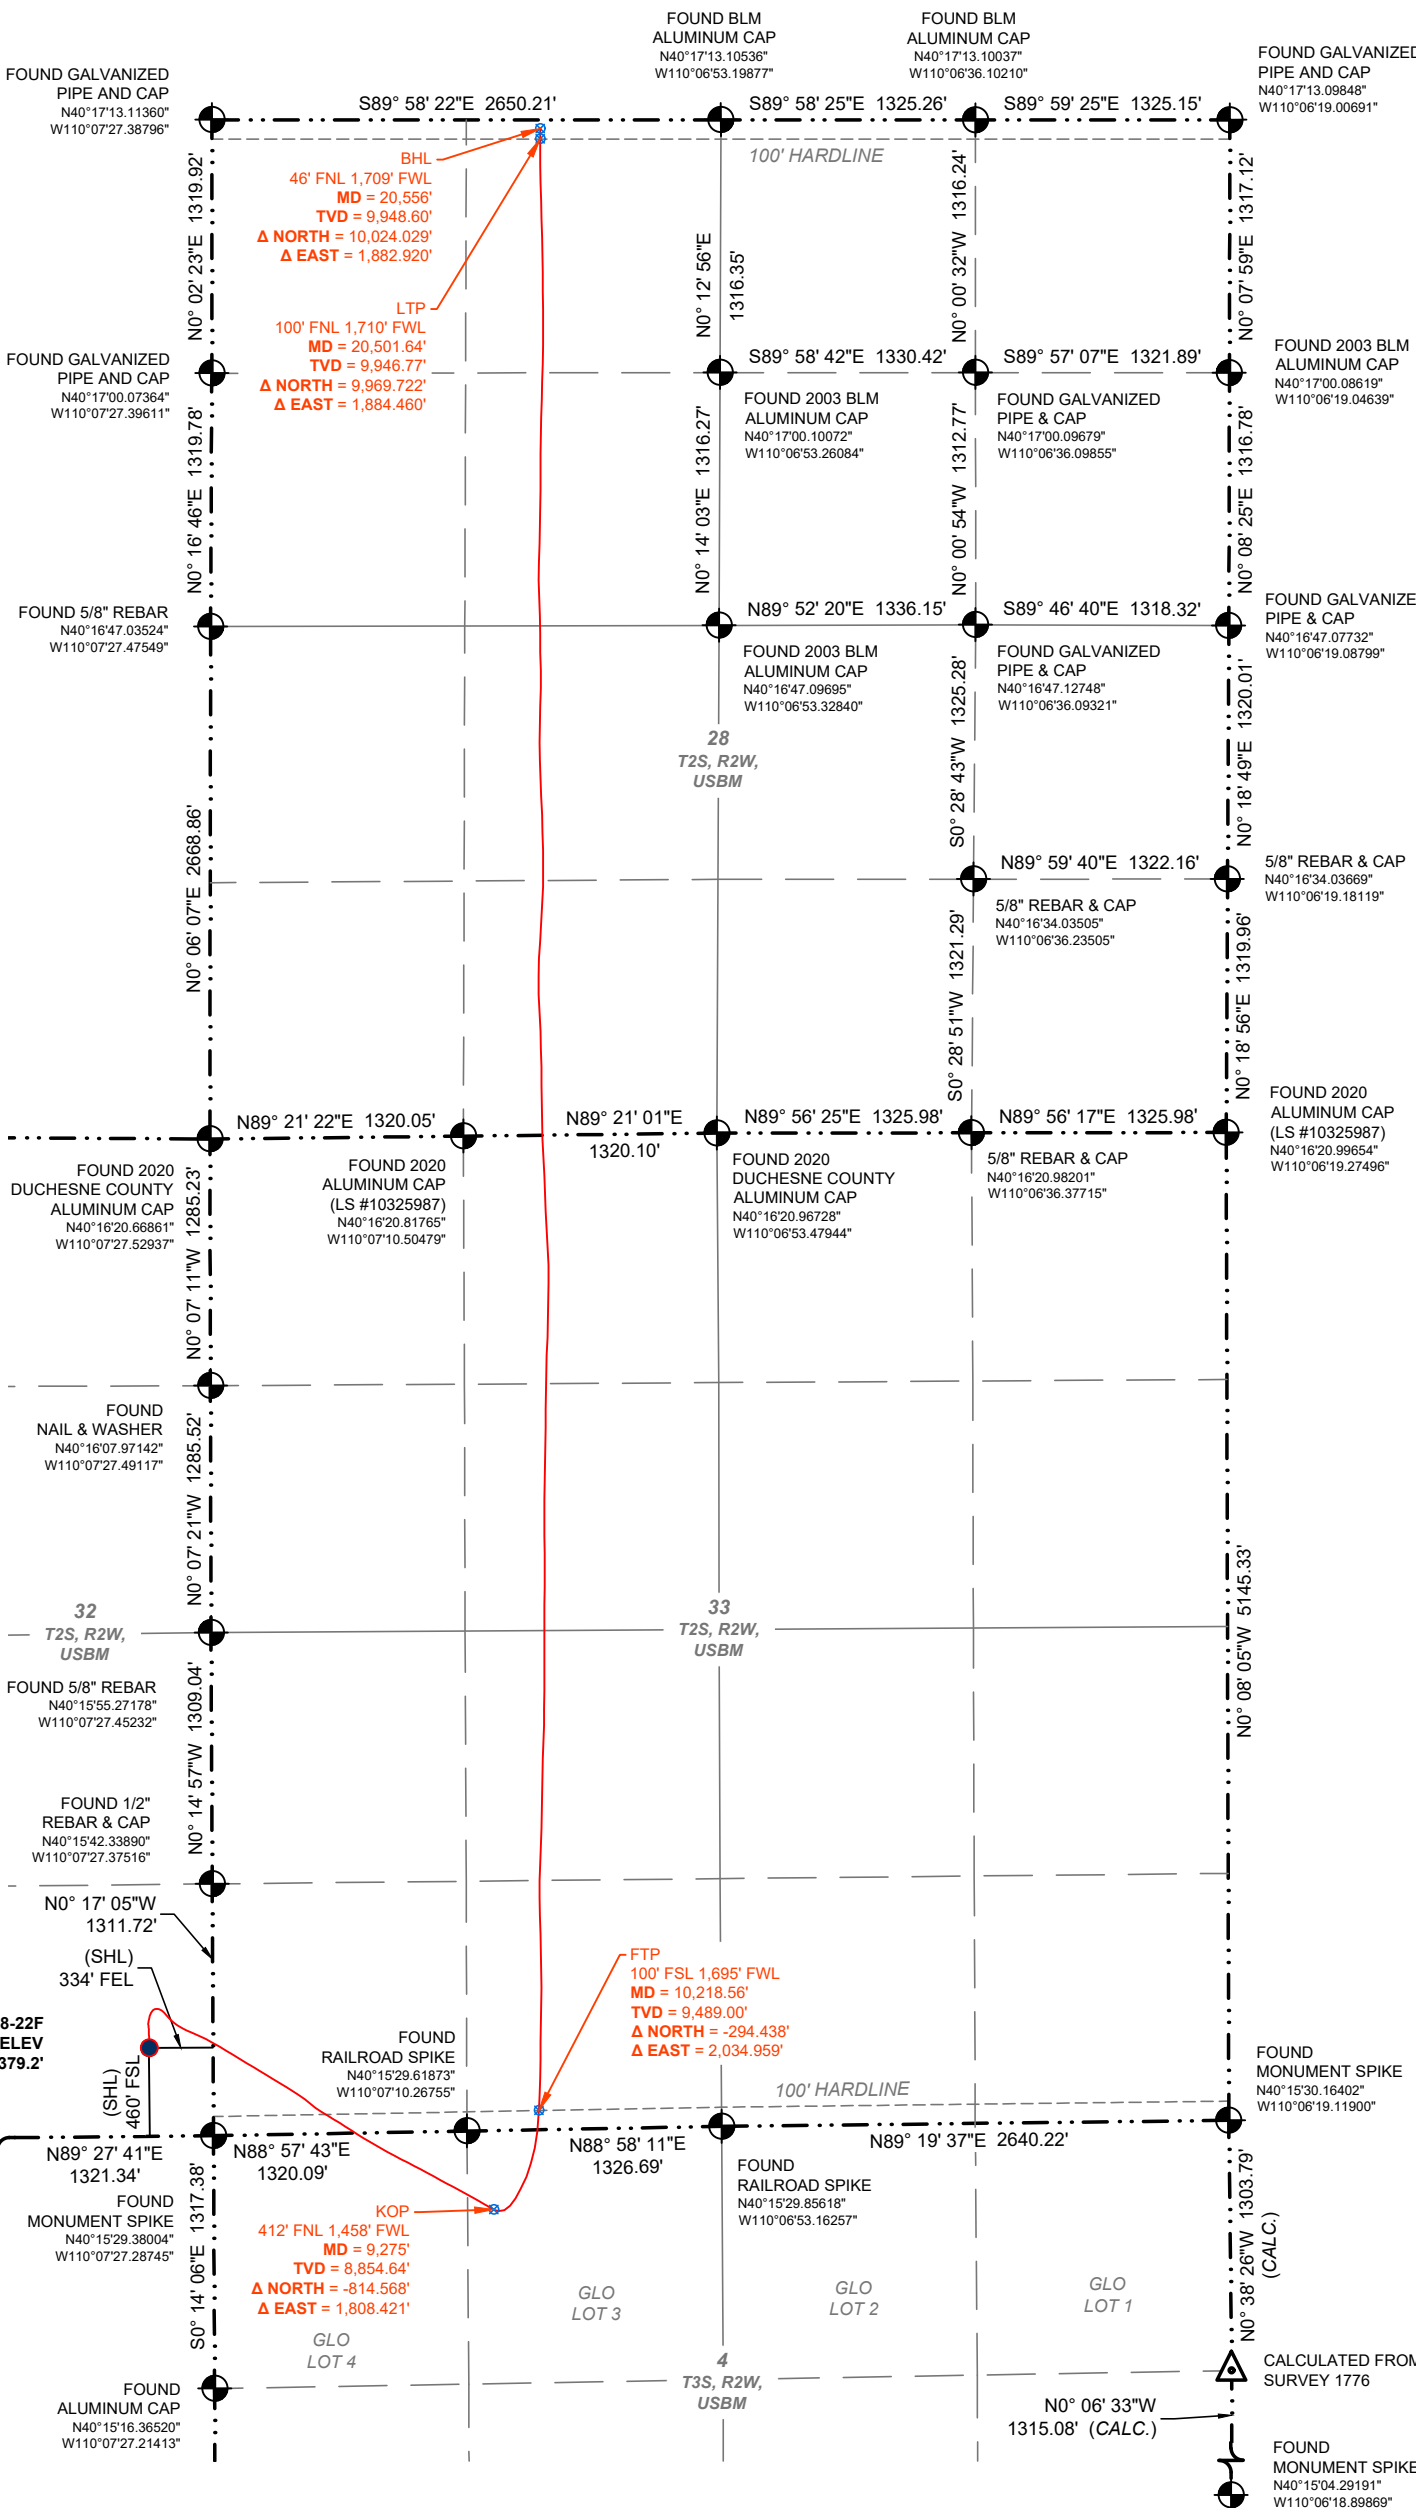

WELL PRE-COMPLETION PLAT

WELL: WILD 62-3328-22F

**PAD LOCATION: SE 1/4 OF THE SE 1/4 OF SECTION 32,
T. 2 S., R. 2 W., U.S.B.&M.
DUCHESNE COUNTY, UTAH**

XCL Resources

Duchesne County, UT (NAD83-True)
Sprouse 32-4D-22 (Wild-Taparoo Pad)
WILD 62-3328-22F

Wellbore #1

Surveys



Standard Survey Report

14 June, 2023

Total Report Version 1.50

COMPASS 5000.16 Build 97

Survey Report

Company:	XCL Resources	Local Co-ordinate Reference:	Well WILD 62-3328-22F
Project:	Duchesne County, UT (NAD83-True)	TVD Reference:	5,379' GL + 30' KB @ 5409.00usft
Site:	Sprouse 32-4D-22 (Wild-Taparoo Pad)	MD Reference:	5,379' GL + 30' KB @ 5409.00usft
Well:	WILD 62-3328-22F	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	EDM 5000.1 Single User Db

Project	Duchesne County, UT (NAD83-True)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	Utah Central Zone	Using geodetic scale factor	

Site	Sprouse 32-4D-22 (Wild-Taparoo Pad)			
Site Position:		Northing:	7,266,165.51 usft	Latitude: 40.2594139
From:	Lat/Long	Easting:	2,023,979.70 usft	Longitude: -110.1255589
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "	

Well	WILD 62-3328-22F			
Well Position	+N/-S	0.00 usft	Northing:	7,266,166.24 usft
	+E/-W	0.00 usft	Easting:	2,024,009.69 usft
Position Uncertainty	0.50 usft	Wellhead Elevation:	usft	Ground Level: 5,379.00 usft
Grid Convergence:	0.88 °			

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM2023	2/26/2023	10.48	65.70	51,243.30000000

Design	Surveys				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.00	0.00	0.00	359.96	

Survey Program	Date 6/13/2023				
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
232.00	2,698.00	Survey #1 (Wellbore #1)	MWD	MWD - Standard	
2,755.00	20,556.00	Survey #2 (Wellbore #1)	MWD+IFR1+MS	OWSG MWD + IFR1 + Multi-Station Correction	

Survey													
Measured Depth (usft)	INC (°)	AZI (°)	Vertical Depth (usft)	Local Coordinates		Map Coordinates		Geo Coordinates		Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
				+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude (°)	Longitude (°)				
0.00	0.00	0.00	0.00	0.00	0.00	7,266,166.23	2,024,009.70	40.2594146	-110.1254514	0.00	0.00	0.00	0.00
232.00	0.53	337.48	232.00	0.99	-0.41	7,266,167.22	2,024,009.27	40.2594174	-110.1254529	0.99	0.23	0.23	0.00
323.00	0.64	350.40	322.99	1.88	-0.66	7,266,168.11	2,024,009.01	40.2594198	-110.1254538	1.88	0.19	0.12	14.20
414.00	0.77	355.98	413.99	2.99	-0.78	7,266,169.21	2,024,008.87	40.2594229	-110.1254542	2.99	0.16	0.14	6.13
504.00	0.74	13.79	503.98	4.16	-0.69	7,266,170.38	2,024,008.95	40.2594261	-110.1254539	4.16	0.26	-0.03	19.79
595.00	0.76	17.01	594.97	5.31	-0.37	7,266,171.54	2,024,009.24	40.2594292	-110.1254527	5.31	0.05	0.02	3.54

Survey Report

Company:	XCL Resources	Local Co-ordinate Reference:	Well WILD 62-3328-22F
Project:	Duchesne County, UT (NAD83-True)	TVD Reference:	5,379' GL + 30' KB @ 5409.00usft
Site:	Sprouse 32-4D-22 (Wild-Taparoo Pad)	MD Reference:	5,379' GL + 30' KB @ 5409.00usft
Well:	WILD 62-3328-22F	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	EDM 5000.1 Single User Db

Survey

Measured Depth (usft)	INC (°)	AZI (°)	Vertical Depth (usft)	Local Coordinates +N/-S (usft)	+E/-W (usft)	Map Coordinates Northing (usft)	Easting (usft)	Geo Coordinates Latitude (°)	Longitude (°)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
686.00	0.74	39.71	685.96	6.34	0.18	7,266,172.57	2,024,009.78	40.2594320	-110.1254508	6.34	0.33	-0.02	24.95
778.00	0.81	52.25	777.95	7.19	1.07	7,266,173.44	2,024,010.66	40.2594344	-110.1254476	7.19	0.20	0.08	13.63
873.00	1.49	22.58	872.93	8.74	2.08	7,266,175.01	2,024,011.64	40.2594386	-110.1254440	8.74	0.93	0.72	-31.23
967.00	2.42	6.61	966.88	11.84	2.78	7,266,178.12	2,024,012.29	40.2594471	-110.1254415	11.84	1.14	0.99	-16.99
1,061.00	3.19	0.86	1,060.77	16.43	3.04	7,266,182.71	2,024,012.49	40.2594597	-110.1254405	16.43	0.87	0.82	-6.12
1,156.00	3.40	358.45	1,155.61	21.89	3.01	7,266,188.17	2,024,012.37	40.2594747	-110.1254406	21.89	0.26	0.22	-2.54
1,250.00	3.51	356.34	1,249.44	27.55	2.75	7,266,193.82	2,024,012.02	40.2594903	-110.1254416	27.55	0.18	0.12	-2.24
1,344.00	4.06	356.31	1,343.23	33.74	2.35	7,266,200.00	2,024,011.53	40.2595073	-110.1254430	33.74	0.59	0.59	-0.03
1,439.00	5.01	356.50	1,437.93	41.24	1.88	7,266,207.49	2,024,010.94	40.2595278	-110.1254447	41.23	1.00	1.00	0.20
1,533.00	5.22	357.24	1,531.56	49.60	1.42	7,266,215.85	2,024,010.36	40.2595508	-110.1254463	49.60	0.23	0.22	0.79
1,628.00	5.71	357.92	1,626.13	58.64	1.05	7,266,224.88	2,024,009.84	40.2595756	-110.1254477	58.64	0.52	0.52	0.72
1,722.00	6.11	358.12	1,719.63	68.32	0.71	7,266,234.55	2,024,009.36	40.2596022	-110.1254489	68.32	0.43	0.43	0.21
1,817.00	5.70	358.86	1,814.12	78.09	0.45	7,266,244.31	2,024,008.95	40.2596290	-110.1254498	78.09	0.44	-0.43	0.78
1,911.00	4.77	357.79	1,907.73	86.66	0.21	7,266,252.88	2,024,008.57	40.2596525	-110.1254507	86.66	0.99	-0.99	-1.14
2,005.00	4.39	356.78	2,001.43	94.16	-0.14	7,266,260.37	2,024,008.11	40.2596731	-110.1254519	94.16	0.41	-0.40	-1.07
2,100.00	3.91	356.76	2,096.18	101.02	-0.53	7,266,267.23	2,024,007.61	40.2596919	-110.1254533	101.02	0.51	-0.51	-0.02
2,195.00	3.36	354.83	2,190.99	107.03	-0.97	7,266,273.23	2,024,007.09	40.2597084	-110.1254549	107.03	0.59	-0.58	-2.03
2,289.00	2.83	352.86	2,284.85	112.07	-1.50	7,266,278.26	2,024,006.47	40.2597223	-110.1254568	112.07	0.57	-0.56	-2.10
2,384.00	3.25	352.15	2,379.72	117.07	-2.16	7,266,283.25	2,024,005.74	40.2597360	-110.1254592	117.07	0.44	0.44	-0.75
2,478.00	3.45	357.10	2,473.56	122.53	-2.67	7,266,288.70	2,024,005.15	40.2597510	-110.1254610	122.53	0.37	0.21	5.27
2,572.00	3.68	4.77	2,567.38	128.36	-2.56	7,266,294.53	2,024,005.16	40.2597670	-110.1254606	128.36	0.56	0.24	8.16
2,667.00	3.45	9.21	2,662.19	134.22	-1.85	7,266,300.40	2,024,005.79	40.2597831	-110.1254580	134.22	0.38	-0.24	4.67
2,698.00	3.22	10.70	2,693.14	136.00	-1.54	7,266,302.18	2,024,006.07	40.2597880	-110.1254569	136.00	0.79	-0.74	4.81
2,755.00	3.12	9.01	2,750.05	139.10	-1.00	7,266,305.30	2,024,006.56	40.2597965	-110.1254550	139.10	0.24	-0.18	-2.96
Start MWD @ 2755.00 MD													
2,849.00	4.11	7.47	2,843.87	144.97	-0.16	7,266,311.18	2,024,007.31	40.2598126	-110.1254520	144.97	1.06	1.05	-1.64
2,944.00	5.00	8.75	2,938.56	152.44	0.91	7,266,318.66	2,024,008.27	40.2598331	-110.1254481	152.44	0.94	0.94	1.35
3,038.00	5.07	16.41	3,032.20	160.47	2.71	7,266,326.72	2,024,009.94	40.2598551	-110.1254417	160.47	0.72	0.07	8.15
3,132.00	5.19	19.35	3,125.83	168.47	5.29	7,266,334.75	2,024,012.40	40.2598771	-110.1254325	168.46	0.31	0.13	3.13
3,226.00	5.08	22.63	3,219.45	176.32	8.30	7,266,342.65	2,024,015.29	40.2598986	-110.1254217	176.31	0.33	-0.12	3.49
3,321.00	5.29	30.14	3,314.06	183.99	12.12	7,266,350.37	2,024,018.99	40.2599197	-110.1254080	183.98	0.75	0.22	7.91
3,415.00	5.04	37.33	3,407.68	191.02	16.80	7,266,357.48	2,024,023.56	40.2599390	-110.1253912	191.01	0.74	-0.27	7.65
3,509.00	5.17	43.29	3,501.31	197.39	22.21	7,266,363.92	2,024,028.87	40.2599565	-110.1253719	197.37	0.58	0.14	6.34
3,603.00	6.29	68.76	3,594.85	202.33	29.91	7,266,368.99	2,024,036.49	40.2599700	-110.1253442	202.31	2.92	1.19	27.10
3,698.00	7.41	89.69	3,689.19	204.25	40.89	7,266,371.08	2,024,047.44	40.2599753	-110.1253049	204.23	2.86	1.18	22.03
3,792.00	8.36	107.66	3,782.31	202.21	53.46	7,266,369.23	2,024,060.04	40.2599697	-110.1252599	202.18	2.80	1.01	19.12
3,886.00	9.14	123.85	3,875.23	195.98	66.18	7,266,363.19	2,024,072.85	40.2599526	-110.1252143	195.93	2.74	0.83	17.22
3,981.00	10.02	139.19	3,968.92	185.52	77.85	7,266,352.92	2,024,084.68	40.2599239	-110.1251725	185.47	2.83	0.93	16.15

Survey Report

Company:	XCL Resources	Local Co-ordinate Reference:	Well WILD 62-3328-22F
Project:	Duchesne County, UT (NAD83-True)	TVD Reference:	5,379' GL + 30' KB @ 5409.00usft
Site:	Sprouse 32-4D-22 (Wild-Taparoo Pad)	MD Reference:	5,379' GL + 30' KB @ 5409.00usft
Well:	WILD 62-3328-22F	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	EDM 5000.1 Single User Db

Survey

Measured Depth (usft)	INC (°)	AZI (°)	Vertical Depth (usft)	Local Coordinates +N/-S (usft)	+E/-W (usft)	Map Coordinates Northing (usft)	Easting (usft)	Geo Coordinates Latitude (°)	Longitude (°)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
4,075.00	11.22	139.45	4,061.31	172.38	89.14	7,266,339.95	2,024,096.17	40.2598878	-110.1251320	172.32	1.28	1.28	0.28
4,170.00	12.20	136.37	4,154.33	158.09	102.07	7,266,325.87	2,024,109.32	40.2598486	-110.1250857	158.02	1.22	1.03	-3.24
4,264.00	12.35	134.40	4,246.18	143.87	116.11	7,266,311.86	2,024,123.57	40.2598096	-110.1250354	143.79	0.47	0.16	-2.10
4,359.00	12.95	128.47	4,338.88	130.14	131.70	7,266,298.37	2,024,139.38	40.2597719	-110.1249795	130.05	1.50	0.63	-6.24
4,453.00	13.60	123.44	4,430.37	117.50	149.17	7,266,286.00	2,024,157.04	40.2597372	-110.1249169	117.39	1.41	0.69	-5.35
4,548.00	15.78	118.98	4,522.26	105.08	169.80	7,266,273.90	2,024,177.85	40.2597031	-110.1248430	104.96	2.58	2.29	-4.69
4,642.00	19.01	115.09	4,611.96	92.39	194.85	7,266,261.60	2,024,203.09	40.2596683	-110.1247533	92.26	3.65	3.44	-4.14
4,737.00	22.86	113.47	4,700.67	78.48	225.80	7,266,248.17	2,024,234.25	40.2596301	-110.1246424	78.32	4.10	4.05	-1.71
4,831.00	24.35	113.11	4,786.80	63.60	260.37	7,266,233.82	2,024,269.04	40.2595892	-110.1245185	63.42	1.59	1.59	-0.38
4,925.00	25.01	116.08	4,872.22	47.26	296.05	7,266,218.03	2,024,304.96	40.2595443	-110.1243907	47.05	1.49	0.70	3.16
5,020.00	26.14	120.22	4,957.91	27.89	332.17	7,266,199.23	2,024,341.37	40.2594912	-110.1242613	27.66	2.23	1.19	4.36
5,114.00	26.19	120.88	5,042.28	6.82	367.87	7,266,178.71	2,024,377.39	40.2594334	-110.1241334	6.57	0.31	0.05	0.70
5,209.00	26.19	121.01	5,127.53	-14.74	403.83	7,266,157.71	2,024,413.67	40.2593742	-110.1240045	-15.02	0.06	0.00	0.14
5,303.00	25.99	120.97	5,211.95	-36.02	439.26	7,266,136.97	2,024,449.43	40.2593157	-110.1238776	-36.33	0.21	-0.21	-0.04
5,397.00	25.67	121.63	5,296.56	-57.30	474.26	7,266,116.24	2,024,484.75	40.2592573	-110.1237522	-57.63	0.46	-0.34	0.70
5,492.00	25.90	121.02	5,382.10	-78.78	509.56	7,266,095.30	2,024,520.37	40.2591984	-110.1236257	-79.14	0.37	0.24	-0.64
5,586.00	25.81	120.87	5,466.69	-99.86	544.72	7,266,074.76	2,024,555.85	40.2591405	-110.1234997	-100.24	0.12	-0.10	-0.16
5,680.00	25.11	120.90	5,551.56	-120.60	579.40	7,266,054.56	2,024,590.84	40.2590836	-110.1233755	-121.01	0.74	-0.74	0.03
5,775.00	24.90	121.49	5,637.66	-141.40	613.75	7,266,034.29	2,024,625.50	40.2590265	-110.1232524	-141.83	0.34	-0.22	0.62
5,869.00	24.39	121.62	5,723.10	-161.91	647.15	7,266,014.30	2,024,659.21	40.2589702	-110.1231327	-162.36	0.55	-0.54	0.14
5,963.00	25.36	121.17	5,808.37	-182.51	680.90	7,265,994.22	2,024,693.27	40.2589136	-110.1230118	-182.98	1.05	1.03	-0.48
6,057.00	24.14	122.01	5,893.74	-203.12	714.43	7,265,974.14	2,024,727.11	40.2588571	-110.1228917	-203.62	1.35	-1.30	0.89
6,151.00	24.02	122.01	5,979.56	-223.45	746.95	7,265,954.31	2,024,759.93	40.2588013	-110.1227752	-223.97	0.13	-0.13	0.00
6,246.00	24.28	121.86	6,066.24	-244.00	779.93	7,265,934.26	2,024,793.23	40.2587448	-110.1226570	-244.55	0.28	0.27	-0.16
6,340.00	22.46	127.78	6,152.54	-265.21	810.54	7,265,913.53	2,024,824.16	40.2586866	-110.1225473	-265.78	3.16	-1.94	6.30
6,434.00	21.90	130.64	6,239.59	-287.63	838.04	7,265,891.54	2,024,852.00	40.2586251	-110.1224488	-288.21	1.29	-0.60	3.04
6,528.00	23.33	127.71	6,326.36	-310.43	866.07	7,265,869.17	2,024,880.37	40.2585625	-110.1223484	-311.04	1.94	1.52	-3.12
6,623.00	23.25	121.67	6,413.63	-331.79	896.91	7,265,848.29	2,024,911.54	40.2585038	-110.1222379	-332.41	2.51	-0.08	-6.36
6,717.00	23.30	121.08	6,499.98	-351.13	928.63	7,265,829.45	2,024,943.54	40.2584508	-110.1221242	-351.77	0.25	0.05	-0.63
6,811.00	23.37	121.20	6,586.29	-370.38	960.50	7,265,810.68	2,024,975.70	40.2583979	-110.1220101	-371.05	0.09	0.07	0.13
6,906.00	22.99	121.19	6,673.62	-389.75	992.48	7,265,791.81	2,025,007.98	40.2583447	-110.1218955	-390.44	0.40	-0.40	-0.01
7,000.00	22.49	122.60	6,760.32	-408.94	1,023.33	7,265,773.10	2,025,039.12	40.2582920	-110.1217849	-409.66	0.79	-0.53	1.50
7,095.00	21.53	123.44	6,848.39	-428.34	1,053.19	7,265,754.16	2,025,069.26	40.2582388	-110.1216780	-429.07	1.06	-1.01	0.88
7,189.00	22.68	122.61	6,935.48	-447.61	1,082.85	7,265,735.35	2,025,099.21	40.2581859	-110.1215717	-448.37	1.27	1.22	-0.88
7,283.00	23.45	120.96	7,021.97	-467.00	1,114.15	7,265,716.45	2,025,130.81	40.2581327	-110.1214595	-467.78	1.07	0.82	-1.76
7,378.00	22.43	120.56	7,109.45	-485.94	1,145.97	7,265,698.00	2,025,162.91	40.2580807	-110.1213455	-486.74	1.09	-1.07	-0.42
7,472.00	22.54	120.35	7,196.31	-504.16	1,176.96	7,265,680.26	2,025,194.18	40.2580307	-110.1212345	-504.98	0.14	0.12	-0.22

Survey Report

Company:	XCL Resources	Local Co-ordinate Reference:	Well WILD 62-3328-22F
Project:	Duchesne County, UT (NAD83-True)	TVD Reference:	5,379' GL + 30' KB @ 5409.00usft
Site:	Sprouse 32-4D-22 (Wild-Taparoo Pad)	MD Reference:	5,379' GL + 30' KB @ 5409.00usft
Well:	WILD 62-3328-22F	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	EDM 5000.1 Single User Db

Survey

Measured Depth (usft)	INC (°)	AZI (°)	Vertical Depth (usft)	Local Coordinates +N/-S (usft)	+E/-W (usft)	Map Coordinates Northing (usft)	Easting (usft)	Geo Coordinates Latitude (°)	Longitude (°)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
7,566.00	23.16	118.85	7,282.93	-522.18	1,208.70	7,265,662.72	2,025,226.19	40.2579812	-110.1211208	-523.03	0.90	0.66	-1.60
7,660.00	23.52	118.93	7,369.24	-540.18	1,241.30	7,265,645.24	2,025,259.06	40.2579318	-110.1210040	-541.04	0.38	0.38	0.09
7,763.00	24.98	117.96	7,463.15	-560.32	1,278.50	7,265,625.67	2,025,296.56	40.2578765	-110.1208707	-561.21	1.47	1.42	-0.94
7,858.00	23.55	118.30	7,549.75	-578.72	1,312.93	7,265,607.80	2,025,331.27	40.2578260	-110.1207474	-579.64	1.51	-1.51	0.36
7,952.00	25.02	117.13	7,635.43	-596.69	1,347.16	7,265,590.36	2,025,365.77	40.2577766	-110.1206247	-597.63	1.65	1.56	-1.24
8,046.00	22.99	116.68	7,721.30	-614.00	1,381.26	7,265,573.58	2,025,400.12	40.2577291	-110.1205026	-614.96	2.17	-2.16	-0.48
8,140.00	23.98	119.16	7,807.51	-631.55	1,414.34	7,265,556.54	2,025,433.47	40.2576809	-110.1203840	-632.53	1.49	1.05	2.64
8,235.00	23.77	117.84	7,894.38	-649.89	1,448.13	7,265,538.72	2,025,467.54	40.2576306	-110.1202630	-650.91	0.60	-0.22	-1.39
8,329.00	24.67	118.94	7,980.11	-668.23	1,482.05	7,265,520.90	2,025,501.73	40.2575802	-110.1201415	-669.27	1.07	0.96	1.17
8,423.00	22.32	118.88	8,066.31	-686.35	1,514.85	7,265,503.29	2,025,534.80	40.2575305	-110.1200239	-687.41	2.50	-2.50	-0.06
8,518.00	23.41	117.04	8,153.85	-703.64	1,547.46	7,265,486.50	2,025,567.67	40.2574830	-110.1199071	-704.72	1.37	1.15	-1.94
8,612.00	24.85	119.06	8,239.63	-721.73	1,581.36	7,265,468.94	2,025,601.84	40.2574334	-110.1197857	-722.83	1.77	1.53	2.15
8,707.00	25.37	118.56	8,325.65	-741.15	1,616.68	7,265,450.06	2,025,637.46	40.2573800	-110.1196591	-742.28	0.59	0.55	-0.53
8,801.00	23.70	118.84	8,411.16	-759.90	1,650.92	7,265,431.85	2,025,671.98	40.2573286	-110.1195364	-761.05	1.78	-1.78	0.30
8,895.00	22.48	118.18	8,497.63	-777.50	1,683.31	7,265,414.75	2,025,704.63	40.2572803	-110.1194204	-778.67	1.33	-1.30	-0.70
8,989.00	20.46	119.69	8,585.10	-794.12	1,713.43	7,265,398.59	2,025,735.00	40.2572346	-110.1193125	-795.32	2.23	-2.15	1.61
9,075.00	19.67	119.96	8,665.88	-808.79	1,739.03	7,265,384.32	2,025,760.82	40.2571944	-110.1192208	-810.01	0.92	-0.92	0.31
9,165.00	19.65	121.63	8,750.64	-824.30	1,765.03	7,265,369.22	2,025,787.06	40.2571518	-110.1191276	-825.53	0.62	-0.02	1.86
9,259.00	18.55	123.13	8,839.46	-840.76	1,791.01	7,265,353.16	2,025,813.29	40.2571066	-110.1190345	-842.01	1.28	-1.17	1.60
9,353.00	19.46	93.57	8,928.54	-849.92	1,819.23	7,265,344.43	2,025,841.64	40.2570814	-110.1189334	-851.19	10.18	0.97	-31.45
9,447.00	20.77	65.07	9,017.02	-843.86	1,850.04	7,265,350.97	2,025,872.35	40.2570981	-110.1188230	-845.15	10.42	1.39	-30.32
9,541.00	27.55	43.73	9,102.90	-821.06	1,880.28	7,265,374.23	2,025,902.23	40.2571607	-110.1187147	-822.37	11.66	7.21	-22.70
9,636.00	32.87	30.68	9,185.05	-782.94	1,908.67	7,265,412.77	2,025,930.03	40.2572653	-110.1186130	-784.27	8.87	5.60	-13.74
9,729.00	44.19	26.32	9,257.70	-732.01	1,936.01	7,265,464.12	2,025,956.59	40.2574051	-110.1185150	-733.36	12.51	12.17	-4.69
9,823.00	48.38	24.16	9,322.65	-670.55	1,964.93	7,265,526.00	2,025,984.56	40.2575738	-110.1184114	-671.93	4.76	4.46	-2.30
9,918.00	55.56	14.69	9,381.22	-600.07	1,989.47	7,265,596.85	2,026,008.00	40.2577672	-110.1183234	-601.46	10.89	7.56	-9.97
10,012.00	64.55	11.89	9,428.10	-520.87	2,008.08	7,265,676.32	2,026,025.40	40.2579846	-110.1182567	-522.27	9.90	9.56	-2.98
10,106.00	72.47	6.30	9,462.54	-434.60	2,021.77	7,265,762.78	2,026,037.76	40.2582214	-110.1182076	-436.01	10.08	8.43	-5.95
10,110.00	72.72	6.17	9,463.73	-430.81	2,022.19	7,265,766.58	2,026,038.12	40.2582319	-110.1182061	-432.22	6.85	6.16	-3.13
Crossed Section - 10110.00' MD (0' FSL, 1686' FWL)													
10,200.00	78.28	3.44	9,486.27	-344.02	2,029.46	7,265,853.46	2,026,044.06	40.2584701	-110.1181801	-345.44	6.85	6.18	-3.04
10,213.00	79.18	3.25	9,488.81	-331.29	2,030.21	7,265,866.20	2,026,044.60	40.2585050	-110.1181774	-332.71	7.07	6.92	-1.48
Crossed Hardline - 10213.00' MD (100' FSL, 1694' FWL)													
10,294.00	84.79	2.07	9,500.10	-251.21	2,033.92	7,265,946.33	2,026,047.09	40.2587249	-110.1181641	-252.63	7.07	6.93	-1.45
10,389.00	88.18	1.55	9,505.92	-156.45	2,036.91	7,266,041.12	2,026,048.62	40.2589850	-110.1181533	-157.87	3.61	3.57	-0.55
10,483.00	86.89	0.00	9,509.96	-62.55	2,038.18	7,266,135.02	2,026,048.45	40.2592427	-110.1181487	-63.97	2.14	-1.37	-1.65
10,577.00	86.98	0.60	9,514.99	31.32	2,038.67	7,266,228.87	2,026,047.50	40.2595004	-110.1181469	29.89	0.64	0.10	0.64
10,671.00	90.08	1.40	9,517.40	125.26	2,040.31	7,266,322.82	2,026,047.70	40.2597582	-110.1181410	123.84	3.41	3.30	0.85

Survey Report

Company:	XCL Resources	Local Co-ordinate Reference:	Well WILD 62-3328-22F
Project:	Duchesne County, UT (NAD83-True)	TVD Reference:	5,379' GL + 30' KB @ 5409.00usft
Site:	Sprouse 32-4D-22 (Wild-Taparoo Pad)	MD Reference:	5,379' GL + 30' KB @ 5409.00usft
Well:	WILD 62-3328-22F	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	EDM 5000.1 Single User Db

Survey

Measured Depth (usft)	INC (°)	AZI (°)	Vertical Depth (usft)	Local Coordinates +N/-S (usft)	+E/-W (usft)	Map Coordinates Northing (usft)	Easting (usft)	Geo Coordinates Latitude (°)	Longitude (°)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
10,765.00	89.97	1.11	9,517.36	219.24	2,042.37	7,266,416.81	2,026,048.31	40.2600162	-110.1181336	217.81	0.33	-0.12	-0.31
10,859.00	88.71	0.19	9,518.44	313.22	2,043.44	7,266,510.80	2,026,047.93	40.2602742	-110.1181298	311.80	1.66	-1.34	-0.98
10,953.00	85.77	359.18	9,522.97	407.10	2,042.92	7,266,604.65	2,026,045.97	40.2605319	-110.1181316	405.67	3.31	-3.13	-1.07
11,047.00	85.13	358.73	9,530.42	500.79	2,041.22	7,266,698.29	2,026,042.83	40.2607891	-110.1181377	499.36	0.83	-0.68	-0.48
11,141.00	85.83	357.68	9,537.83	594.45	2,038.28	7,266,791.89	2,026,038.45	40.2610462	-110.1181482	593.02	1.34	0.74	-1.12
11,235.00	88.04	358.35	9,542.86	688.25	2,035.03	7,266,885.62	2,026,033.76	40.2613036	-110.1181598	686.83	2.46	2.35	0.71
11,330.00	88.80	359.97	9,545.48	783.20	2,033.64	7,266,980.53	2,026,030.91	40.2615643	-110.1181648	781.78	1.88	0.80	1.71
11,419.00	87.06	0.73	9,548.69	872.14	2,034.18	7,267,069.46	2,026,030.09	40.2618084	-110.1181628	870.72	2.13	-1.96	0.85
11,508.00	87.42	2.41	9,552.98	961.00	2,036.62	7,267,158.34	2,026,031.16	40.2620523	-110.1181540	959.57	1.93	0.40	1.89
11,598.00	85.41	2.32	9,558.61	1,050.74	2,040.32	7,267,248.12	2,026,033.48	40.2622987	-110.1181407	1,049.31	2.24	-2.23	-0.10
11,689.00	84.25	1.37	9,566.81	1,141.32	2,043.24	7,267,338.73	2,026,035.01	40.2625473	-110.1181303	1,139.89	1.64	-1.27	-1.04
11,780.00	86.13	1.28	9,574.44	1,231.97	2,045.34	7,267,429.40	2,026,035.71	40.2627961	-110.1181227	1,230.54	2.07	2.07	-0.10
11,874.00	84.59	1.42	9,582.04	1,325.63	2,047.55	7,267,523.08	2,026,036.48	40.2630532	-110.1181148	1,324.20	1.65	-1.64	0.15
11,964.00	87.79	0.87	9,588.02	1,415.41	2,049.34	7,267,612.86	2,026,036.89	40.2632997	-110.1181083	1,413.97	3.61	3.56	-0.61
12,054.00	88.07	1.18	9,591.27	1,505.33	2,050.95	7,267,702.79	2,026,037.12	40.2635465	-110.1181025	1,503.90	0.46	0.31	0.34
12,141.00	87.09	2.28	9,594.94	1,592.21	2,053.57	7,267,789.70	2,026,038.41	40.2637850	-110.1180931	1,590.78	1.69	-1.13	1.26
12,230.00	86.39	1.32	9,600.01	1,681.02	2,056.36	7,267,878.53	2,026,039.84	40.2640288	-110.1180831	1,679.59	1.33	-0.79	-1.08
12,319.00	88.46	0.60	9,604.00	1,769.92	2,057.85	7,267,967.43	2,026,039.96	40.2642728	-110.1180777	1,768.48	2.46	2.33	-0.81
12,408.00	87.87	0.87	9,606.85	1,858.86	2,058.99	7,268,056.38	2,026,039.73	40.2645169	-110.1180736	1,857.42	0.73	-0.66	0.30
12,498.00	87.51	359.54	9,610.48	1,948.79	2,059.31	7,268,146.29	2,026,038.67	40.2647638	-110.1180724	1,947.35	1.53	-0.40	-1.48
12,587.00	86.61	359.36	9,615.05	2,037.66	2,058.46	7,268,235.14	2,026,036.45	40.2650077	-110.1180755	2,036.23	1.03	-1.01	-0.20
12,677.00	89.94	0.40	9,617.75	2,127.61	2,058.27	7,268,325.06	2,026,034.88	40.2652546	-110.1180761	2,126.17	3.88	3.70	1.16
12,767.00	89.08	0.06	9,618.52	2,217.60	2,058.64	7,268,415.05	2,026,033.86	40.2655017	-110.1180748	2,216.17	1.03	-0.96	-0.38
12,857.00	88.66	0.37	9,620.30	2,307.59	2,058.97	7,268,505.02	2,026,032.82	40.2657487	-110.1180735	2,306.15	0.58	-0.47	0.34
12,948.00	88.57	0.59	9,622.50	2,398.56	2,059.74	7,268,595.98	2,026,032.18	40.2659984	-110.1180708	2,397.12	0.26	-0.10	0.24
13,037.00	87.06	359.97	9,625.89	2,487.49	2,060.17	7,268,684.90	2,026,031.25	40.2662425	-110.1180692	2,486.05	1.83	-1.70	-0.70
13,127.00	86.53	359.82	9,630.92	2,577.35	2,060.01	7,268,774.74	2,026,029.70	40.2664891	-110.1180698	2,575.91	0.61	-0.59	-0.17
13,217.00	87.45	358.98	9,635.65	2,667.21	2,059.06	7,268,864.58	2,026,027.38	40.2667358	-110.1180731	2,665.78	1.38	1.02	-0.93
13,311.00	87.26	0.29	9,639.99	2,761.11	2,058.47	7,268,958.45	2,026,025.34	40.2669936	-110.1180752	2,759.67	1.41	-0.20	1.39
13,405.00	86.89	0.59	9,644.78	2,854.98	2,059.19	7,269,052.31	2,026,024.62	40.2672512	-110.1180726	2,853.55	0.51	-0.39	0.32
13,499.00	89.16	0.77	9,648.02	2,948.92	2,060.30	7,269,146.24	2,026,024.29	40.2675091	-110.1180686	2,947.48	2.42	2.41	0.19
13,593.00	88.96	1.48	9,649.57	3,042.88	2,062.15	7,269,240.22	2,026,024.69	40.2677670	-110.1180620	3,041.44	0.78	-0.21	0.76
13,687.00	88.52	0.72	9,651.63	3,136.84	2,063.95	7,269,334.19	2,026,025.05	40.2680249	-110.1180555	3,135.40	0.93	-0.47	-0.81
13,781.00	89.52	0.34	9,653.24	3,230.82	2,064.82	7,269,428.17	2,026,024.48	40.2682829	-110.1180523	3,229.38	1.14	1.06	-0.40
13,875.00	89.33	1.55	9,654.18	3,324.81	2,066.37	7,269,522.15	2,026,024.58	40.2685409	-110.1180467	3,323.36	1.30	-0.20	1.29
13,968.00	87.06	0.35	9,657.11	3,417.74	2,067.91	7,269,615.09	2,026,024.70	40.2687960	-110.1180412	3,416.29	2.76	-2.44	-1.29
14,063.00	86.67	0.99	9,662.31	3,512.59	2,069.02	7,269,709.94	2,026,024.35	40.2690563	-110.1180372	3,511.14	0.79	-0.41	0.67
14,157.00	86.50	1.81	9,667.91	3,606.39	2,071.31	7,269,803.76	2,026,025.20	40.2693138	-110.1180289	3,604.95	0.89	-0.18	0.87

Survey Report

Company:	XCL Resources	Local Co-ordinate Reference:	Well WILD 62-3328-22F
Project:	Duchesne County, UT (NAD83-True)	TVD Reference:	5,379' GL + 30' KB @ 5409.00usft
Site:	Sprouse 32-4D-22 (Wild-Taparoo Pad)	MD Reference:	5,379' GL + 30' KB @ 5409.00usft
Well:	WILD 62-3328-22F	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	EDM 5000.1 Single User Db

Survey

Measured Depth (usft)	INC (°)	AZI (°)	Vertical Depth (usft)	Local Coordinates +N/-S (usft)	+E/-W (usft)	Map Coordinates Northing (usft)	Easting (usft)	Geo Coordinates Latitude (°)	Longitude (°)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
14,251.00	86.70	2.62	9,673.48	3,700.16	2,074.94	7,269,897.57	2,026,027.38	40.2695712	-110.1180159	3,698.71	0.89	0.21	0.86
14,345.00	87.45	0.58	9,678.28	3,793.99	2,077.56	7,269,991.42	2,026,028.56	40.2698288	-110.1180065	3,792.54	2.31	0.80	-2.17
14,439.00	86.61	0.81	9,683.15	3,887.86	2,078.70	7,270,085.29	2,026,028.26	40.2700864	-110.1180024	3,886.41	0.93	-0.89	0.24
14,533.00	87.68	1.00	9,687.83	3,981.73	2,080.18	7,270,179.16	2,026,028.30	40.2703441	-110.1179970	3,980.28	1.16	1.14	0.20
14,627.00	87.93	358.78	9,691.43	4,075.65	2,080.00	7,270,273.07	2,026,026.67	40.2706019	-110.1179977	4,074.20	2.37	0.27	-2.36
14,722.00	88.63	356.85	9,694.28	4,170.54	2,076.38	7,270,367.88	2,026,021.60	40.2708624	-110.1180106	4,169.09	2.16	0.74	-2.03
14,816.00	85.57	356.39	9,699.04	4,264.24	2,070.85	7,270,461.48	2,026,014.62	40.2711196	-110.1180304	4,262.79	3.29	-3.26	-0.49
14,910.00	83.94	357.08	9,707.63	4,357.69	2,065.52	7,270,554.83	2,026,007.86	40.2713761	-110.1180495	4,356.25	1.88	-1.73	0.73
15,004.00	85.60	358.10	9,716.20	4,451.21	2,061.58	7,270,648.27	2,026,002.49	40.2716328	-110.1180636	4,449.77	2.07	1.77	1.09
15,098.00	84.70	358.01	9,724.15	4,544.82	2,058.40	7,270,741.81	2,025,997.87	40.2718898	-110.1180749	4,543.38	0.96	-0.96	-0.10
15,192.00	87.14	356.61	9,730.84	4,638.47	2,054.00	7,270,835.38	2,025,992.03	40.2721469	-110.1180907	4,637.04	2.99	2.60	-1.49
15,287.00	85.35	357.82	9,737.06	4,733.15	2,049.39	7,270,929.97	2,025,985.97	40.2724067	-110.1181072	4,731.72	2.27	-1.88	1.27
15,298.00	85.53	357.94	9,737.93	4,744.11	2,048.99	7,270,940.92	2,025,985.39	40.2724368	-110.1181086	4,742.68	1.98	1.66	1.10
Crossed Section - 15298.00' MD (0' FSL, 1731' FWL)													
15,380.00	86.89	358.84	9,743.35	4,825.89	2,046.69	7,271,022.65	2,025,981.84	40.2726613	-110.1181168	4,824.46	1.98	1.66	1.10
15,474.00	89.41	359.44	9,746.39	4,919.83	2,045.28	7,271,116.54	2,025,978.99	40.2729192	-110.1181218	4,918.40	2.76	2.68	0.64
15,569.00	89.02	359.54	9,747.69	5,014.81	2,044.44	7,271,211.50	2,025,976.68	40.2731799	-110.1181248	5,013.38	0.42	-0.41	0.11
15,663.00	88.82	359.17	9,749.46	5,108.79	2,043.38	7,271,305.44	2,025,974.18	40.2734379	-110.1181286	5,107.36	0.45	-0.21	-0.39
15,757.00	88.77	358.30	9,751.44	5,202.74	2,041.30	7,271,399.35	2,025,970.66	40.2736958	-110.1181360	5,201.32	0.93	-0.05	-0.93
15,851.00	88.23	358.29	9,753.90	5,296.67	2,038.51	7,271,493.21	2,025,966.42	40.2739536	-110.1181460	5,295.25	0.57	-0.57	-0.01
15,945.00	87.70	356.65	9,757.23	5,390.52	2,034.36	7,271,586.98	2,025,960.84	40.2742112	-110.1181608	5,389.09	1.83	-0.56	-1.74
16,040.00	87.59	357.79	9,761.14	5,485.32	2,029.76	7,271,681.69	2,025,954.78	40.2744714	-110.1181773	5,483.90	1.20	-0.12	1.20
16,134.00	86.19	0.58	9,766.24	5,579.16	2,028.42	7,271,775.50	2,025,952.00	40.2747290	-110.1181821	5,577.75	3.32	-1.49	2.97
16,228.00	87.40	3.16	9,771.49	5,672.96	2,031.48	7,271,869.32	2,025,953.62	40.2749865	-110.1181711	5,671.54	3.03	1.29	2.74
16,322.00	86.83	3.20	9,776.23	5,766.69	2,036.69	7,271,963.12	2,025,957.39	40.2752438	-110.1181524	5,765.27	0.61	-0.61	0.04
16,416.00	85.99	3.21	9,782.11	5,860.36	2,041.94	7,272,056.85	2,025,961.19	40.2755009	-110.1181335	5,858.93	0.89	-0.89	0.01
16,510.00	85.77	3.99	9,788.87	5,953.93	2,047.82	7,272,150.49	2,025,965.64	40.2757577	-110.1181124	5,952.50	0.86	-0.23	0.83
16,604.00	85.15	0.76	9,796.31	6,047.54	2,051.71	7,272,244.14	2,025,968.08	40.2760147	-110.1180985	6,046.11	3.49	-0.66	-3.44
16,698.00	86.97	0.29	9,802.77	6,141.31	2,052.57	7,272,337.91	2,025,967.50	40.2762721	-110.1180954	6,139.88	2.00	1.94	-0.50
16,792.00	88.82	358.99	9,806.22	6,235.24	2,051.98	7,272,431.81	2,025,965.47	40.2765299	-110.1180975	6,233.81	2.40	1.97	-1.38
16,886.00	87.20	357.97	9,809.48	6,329.15	2,049.48	7,272,525.66	2,025,961.53	40.2767877	-110.1181064	6,327.72	2.04	-1.72	-1.09
16,979.00	86.58	358.57	9,814.53	6,421.97	2,046.68	7,272,618.42	2,025,957.30	40.2770425	-110.1181164	6,420.54	0.93	-0.67	0.65
17,073.00	88.07	355.86	9,818.92	6,515.74	2,042.12	7,272,712.11	2,025,951.30	40.2772999	-110.1181327	6,514.32	3.29	1.59	-2.88
17,167.00	89.86	359.53	9,820.62	6,609.63	2,038.34	7,272,805.92	2,025,946.08	40.2775576	-110.1181462	6,608.21	4.34	1.90	3.90
17,262.00	88.40	358.17	9,822.06	6,704.60	2,036.43	7,272,900.84	2,025,942.72	40.2778183	-110.1181530	6,703.17	2.10	-1.54	-1.43
17,355.00	86.95	359.29	9,825.83	6,797.49	2,034.37	7,272,993.68	2,025,939.23	40.2780733	-110.1181604	6,796.07	1.97	-1.56	1.20
17,450.00	89.16	1.89	9,829.06	6,892.42	2,035.35	7,273,088.61	2,025,938.75	40.2783339	-110.1181568	6,891.00	3.59	2.33	2.74

Survey Report

Company:	XCL Resources	Local Co-ordinate Reference:	Well WILD 62-3328-22F
Project:	Duchesne County, UT (NAD83-True)	TVD Reference:	5,379' GL + 30' KB @ 5409.00usft
Site:	Sprouse 32-4D-22 (Wild-Taparoo Pad)	MD Reference:	5,379' GL + 30' KB @ 5409.00usft
Well:	WILD 62-3328-22F	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	EDM 5000.1 Single User Db

Survey

Measured Depth (usft)	INC (°)	AZI (°)	Vertical Depth (usft)	Local Coordinates +N/-S (usft)	+E/-W (usft)	Map Coordinates Northing (usft)	Easting (usft)	Geo Coordinates Latitude (°)	Longitude (°)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
17,544.00	86.89	1.36	9,832.29	6,986.32	2,038.02	7,273,182.53	2,025,939.97	40.2785916	-110.1181473	6,984.89	2.48	-2.41	-0.56
17,638.00	89.19	1.32	9,835.51	7,080.23	2,040.21	7,273,276.46	2,025,940.72	40.2788494	-110.1181394	7,078.81	2.45	2.45	-0.04
17,732.00	87.31	358.73	9,838.38	7,174.18	2,040.25	7,273,370.38	2,025,939.32	40.2791073	-110.1181392	7,172.75	3.40	-2.00	-2.76
17,826.00	86.75	358.65	9,843.25	7,268.02	2,038.11	7,273,464.18	2,025,935.73	40.2793649	-110.1181469	7,266.60	0.60	-0.60	-0.09
17,920.00	89.50	359.85	9,846.33	7,361.96	2,036.88	7,273,558.08	2,025,933.06	40.2796227	-110.1181512	7,360.53	3.19	2.93	1.28
18,014.00	86.78	357.85	9,849.38	7,455.87	2,035.00	7,273,651.95	2,025,929.74	40.2798805	-110.1181580	7,454.45	3.59	-2.89	-2.13
18,108.00	89.47	358.23	9,852.45	7,549.76	2,031.78	7,273,745.77	2,025,925.08	40.2801382	-110.1181694	7,548.34	2.89	2.86	0.40
18,202.00	89.52	358.47	9,853.28	7,643.72	2,029.08	7,273,839.66	2,025,920.93	40.2803961	-110.1181791	7,642.30	0.26	0.05	0.26
18,296.00	89.30	3.36	9,854.25	7,737.67	2,030.58	7,273,933.62	2,025,920.99	40.2806540	-110.1181737	7,736.25	5.21	-0.23	5.20
18,391.00	89.10	0.74	9,855.58	7,832.59	2,033.97	7,274,028.58	2,025,922.93	40.2809146	-110.1181615	7,831.17	2.77	-0.21	-2.76
18,484.00	85.71	0.93	9,859.79	7,925.47	2,035.33	7,274,121.46	2,025,922.85	40.2811695	-110.1181566	7,924.05	3.65	-3.65	0.20
18,579.00	85.12	0.93	9,867.38	8,020.16	2,036.87	7,274,216.15	2,025,922.93	40.2814294	-110.1181511	8,018.73	0.62	-0.62	0.00
18,672.00	84.25	1.16	9,876.00	8,112.74	2,038.55	7,274,308.74	2,025,923.20	40.2816836	-110.1181450	8,111.32	0.97	-0.94	0.25
18,767.00	87.93	359.92	9,882.47	8,207.50	2,039.44	7,274,403.50	2,025,922.63	40.2819437	-110.1181418	8,206.07	4.09	3.87	-1.31
18,861.00	88.49	0.13	9,885.41	8,301.45	2,039.49	7,274,497.43	2,025,921.23	40.2822016	-110.1181416	8,300.03	0.64	0.60	0.22
18,955.00	87.09	1.37	9,889.03	8,395.37	2,040.71	7,274,591.35	2,025,921.02	40.2824594	-110.1181372	8,393.94	1.99	-1.49	1.32
19,050.00	86.81	1.62	9,894.09	8,490.20	2,043.19	7,274,686.20	2,025,922.03	40.2827197	-110.1181283	8,488.77	0.39	-0.29	0.26
19,144.00	87.11	1.27	9,899.07	8,584.04	2,045.56	7,274,780.06	2,025,922.96	40.2829773	-110.1181198	8,582.61	0.49	0.32	-0.37
19,238.00	87.59	1.38	9,903.42	8,677.91	2,047.73	7,274,873.95	2,025,923.69	40.2832349	-110.1181120	8,676.48	0.52	0.51	0.12
19,332.00	85.97	1.65	9,908.70	8,771.73	2,050.21	7,274,967.78	2,025,924.73	40.2834925	-110.1181030	8,770.30	1.75	-1.72	0.29
19,426.00	87.09	0.71	9,914.39	8,865.53	2,052.14	7,275,061.60	2,025,925.22	40.2837500	-110.1180961	8,864.10	1.55	1.19	-1.00
19,520.00	87.93	359.62	9,918.47	8,959.44	2,052.41	7,275,155.50	2,025,924.04	40.2840077	-110.1180951	8,958.01	1.46	0.89	-1.16
19,614.00	87.96	359.52	9,921.84	9,053.38	2,051.71	7,275,249.40	2,025,921.90	40.2842656	-110.1180976	9,051.95	0.11	0.03	-0.11
19,708.00	86.92	0.21	9,926.04	9,147.28	2,051.48	7,275,343.29	2,025,920.23	40.2845233	-110.1180984	9,145.85	1.33	-1.11	0.73
19,802.00	87.17	359.35	9,930.89	9,241.16	2,051.12	7,275,437.14	2,025,918.43	40.2847810	-110.1180996	9,239.72	0.95	0.27	-0.91
19,896.00	85.96	358.28	9,936.52	9,334.97	2,049.18	7,275,530.90	2,025,915.05	40.2850385	-110.1181066	9,333.53	1.72	-1.29	-1.14
19,990.00	89.86	358.69	9,939.95	9,428.85	2,046.70	7,275,624.73	2,025,911.12	40.2852962	-110.1181154	9,427.42	4.17	4.15	0.44
20,084.00	89.72	358.88	9,940.29	9,522.83	2,044.71	7,275,718.66	2,025,907.69	40.2855542	-110.1181225	9,521.40	0.25	-0.15	0.20
20,178.00	89.22	358.24	9,941.16	9,616.80	2,042.35	7,275,812.57	2,025,903.88	40.2858121	-110.1181310	9,615.37	0.86	-0.53	-0.68
20,273.00	88.99	358.30	9,942.65	9,711.74	2,039.48	7,275,907.45	2,025,899.55	40.2860728	-110.1181412	9,710.31	0.25	-0.24	0.06
20,366.00	89.22	0.00	9,944.10	9,804.72	2,038.10	7,276,000.39	2,025,896.75	40.2863280	-110.1181461	9,803.29	1.84	0.25	1.83
20,461.00	88.88	359.80	9,945.67	9,899.70	2,037.93	7,276,095.35	2,025,895.12	40.2865887	-110.1181467	9,898.28	0.42	-0.36	-0.21
20,505.00	88.04	359.24	9,946.86	9,943.68	2,037.56	7,276,139.32	2,025,894.08	40.2867094	-110.1181480	9,942.26	2.29	-1.91	-1.27
End MWD @ 20505.00 MD													
20,556.00	88.04	359.24	9,948.60	9,994.65	2,036.89	7,276,190.27	2,025,892.62	40.2868493	-110.1181504	9,993.23	0.00	0.00	0.00
Prj to Bit @ 20556.00 MD (46' FNL, 1708' FWL)													

Survey Report

Company:	XCL Resources	Local Co-ordinate Reference:	Well WILD 62-3328-22F
Project:	Duchesne County, UT (NAD83-True)	TVD Reference:	5,379' GL + 30' KB @ 5409.00usft
Site:	Sprouse 32-4D-22 (Wild-Taparoo Pad)	MD Reference:	5,379' GL + 30' KB @ 5409.00usft
Well:	WILD 62-3328-22F	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	EDM 5000.1 Single User Db

Design Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
2,755.00	2,750.05	139.10	-1.00	Start MWD @ 2755.00 MD
10,110.00	9,463.73	-430.81	2,022.19	Crossed Section - 10110.00' MD (0' FSL, 1686' FWL)
10,213.00	9,488.81	-331.29	2,030.21	Crossed Hardline - 10213.00' MD (100' FSL, 1694' FWL)
15,298.00	9,737.93	4,744.11	2,048.99	Crossed Section - 15298.00' MD (0' FSL, 1731' FWL)
20,505.00	9,946.86	9,943.68	2,037.56	End MWD @ 20505.00 MD
20,556.00	9,948.60	9,994.65	2,036.89	Prj to Bit @ 20556.00 MD (46' FNL, 1708' FWL)

Checked By: _____ Approved By: _____ Date: _____



WILD 62-3328-22F




WELL DETAILS: WILD 62-3328-22F Surveys



		GL Elev (ft).: 5379.00			
+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
0.00	0.00	7266166.23	2024009.70	40.2594146	-110.1254514

ANNOTATIONS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Vsect	Departure	Annotation
2755.00	3.12	9.01	2750.05	139.10	-1.00	139.10	140.66	Start MWD @ 2755.00 MD
10110.00	72.72	6.17	9463.73	-430.81	2022.19	-432.22	2793.34	Crossed Section - 10110.00' MD (0' FSL, 1686' FWL)
10213.00	79.18	3.25	9488.81	-331.29	2030.21	-332.71	2893.24	Crossed Hardline - 10213.00' MD (100' FSL, 1694' FWL)
15298.00	85.53	357.94	9737.93	4744.11	2048.99	4742.68	7970.26	Crossed Section - 15298.00' MD (0' FSL, 1731' FWL)
20505.00	88.04	359.24	9946.86	9943.68	2037.56	9942.26	13171.86	End MWD @ 20505.00 MD
20556.00	88.04	359.24	9948.60	9994.65	2036.89	9993.23	13222.83	Prj to Bit @ 20556.00 MD (46' FNL, 1708' FWL)

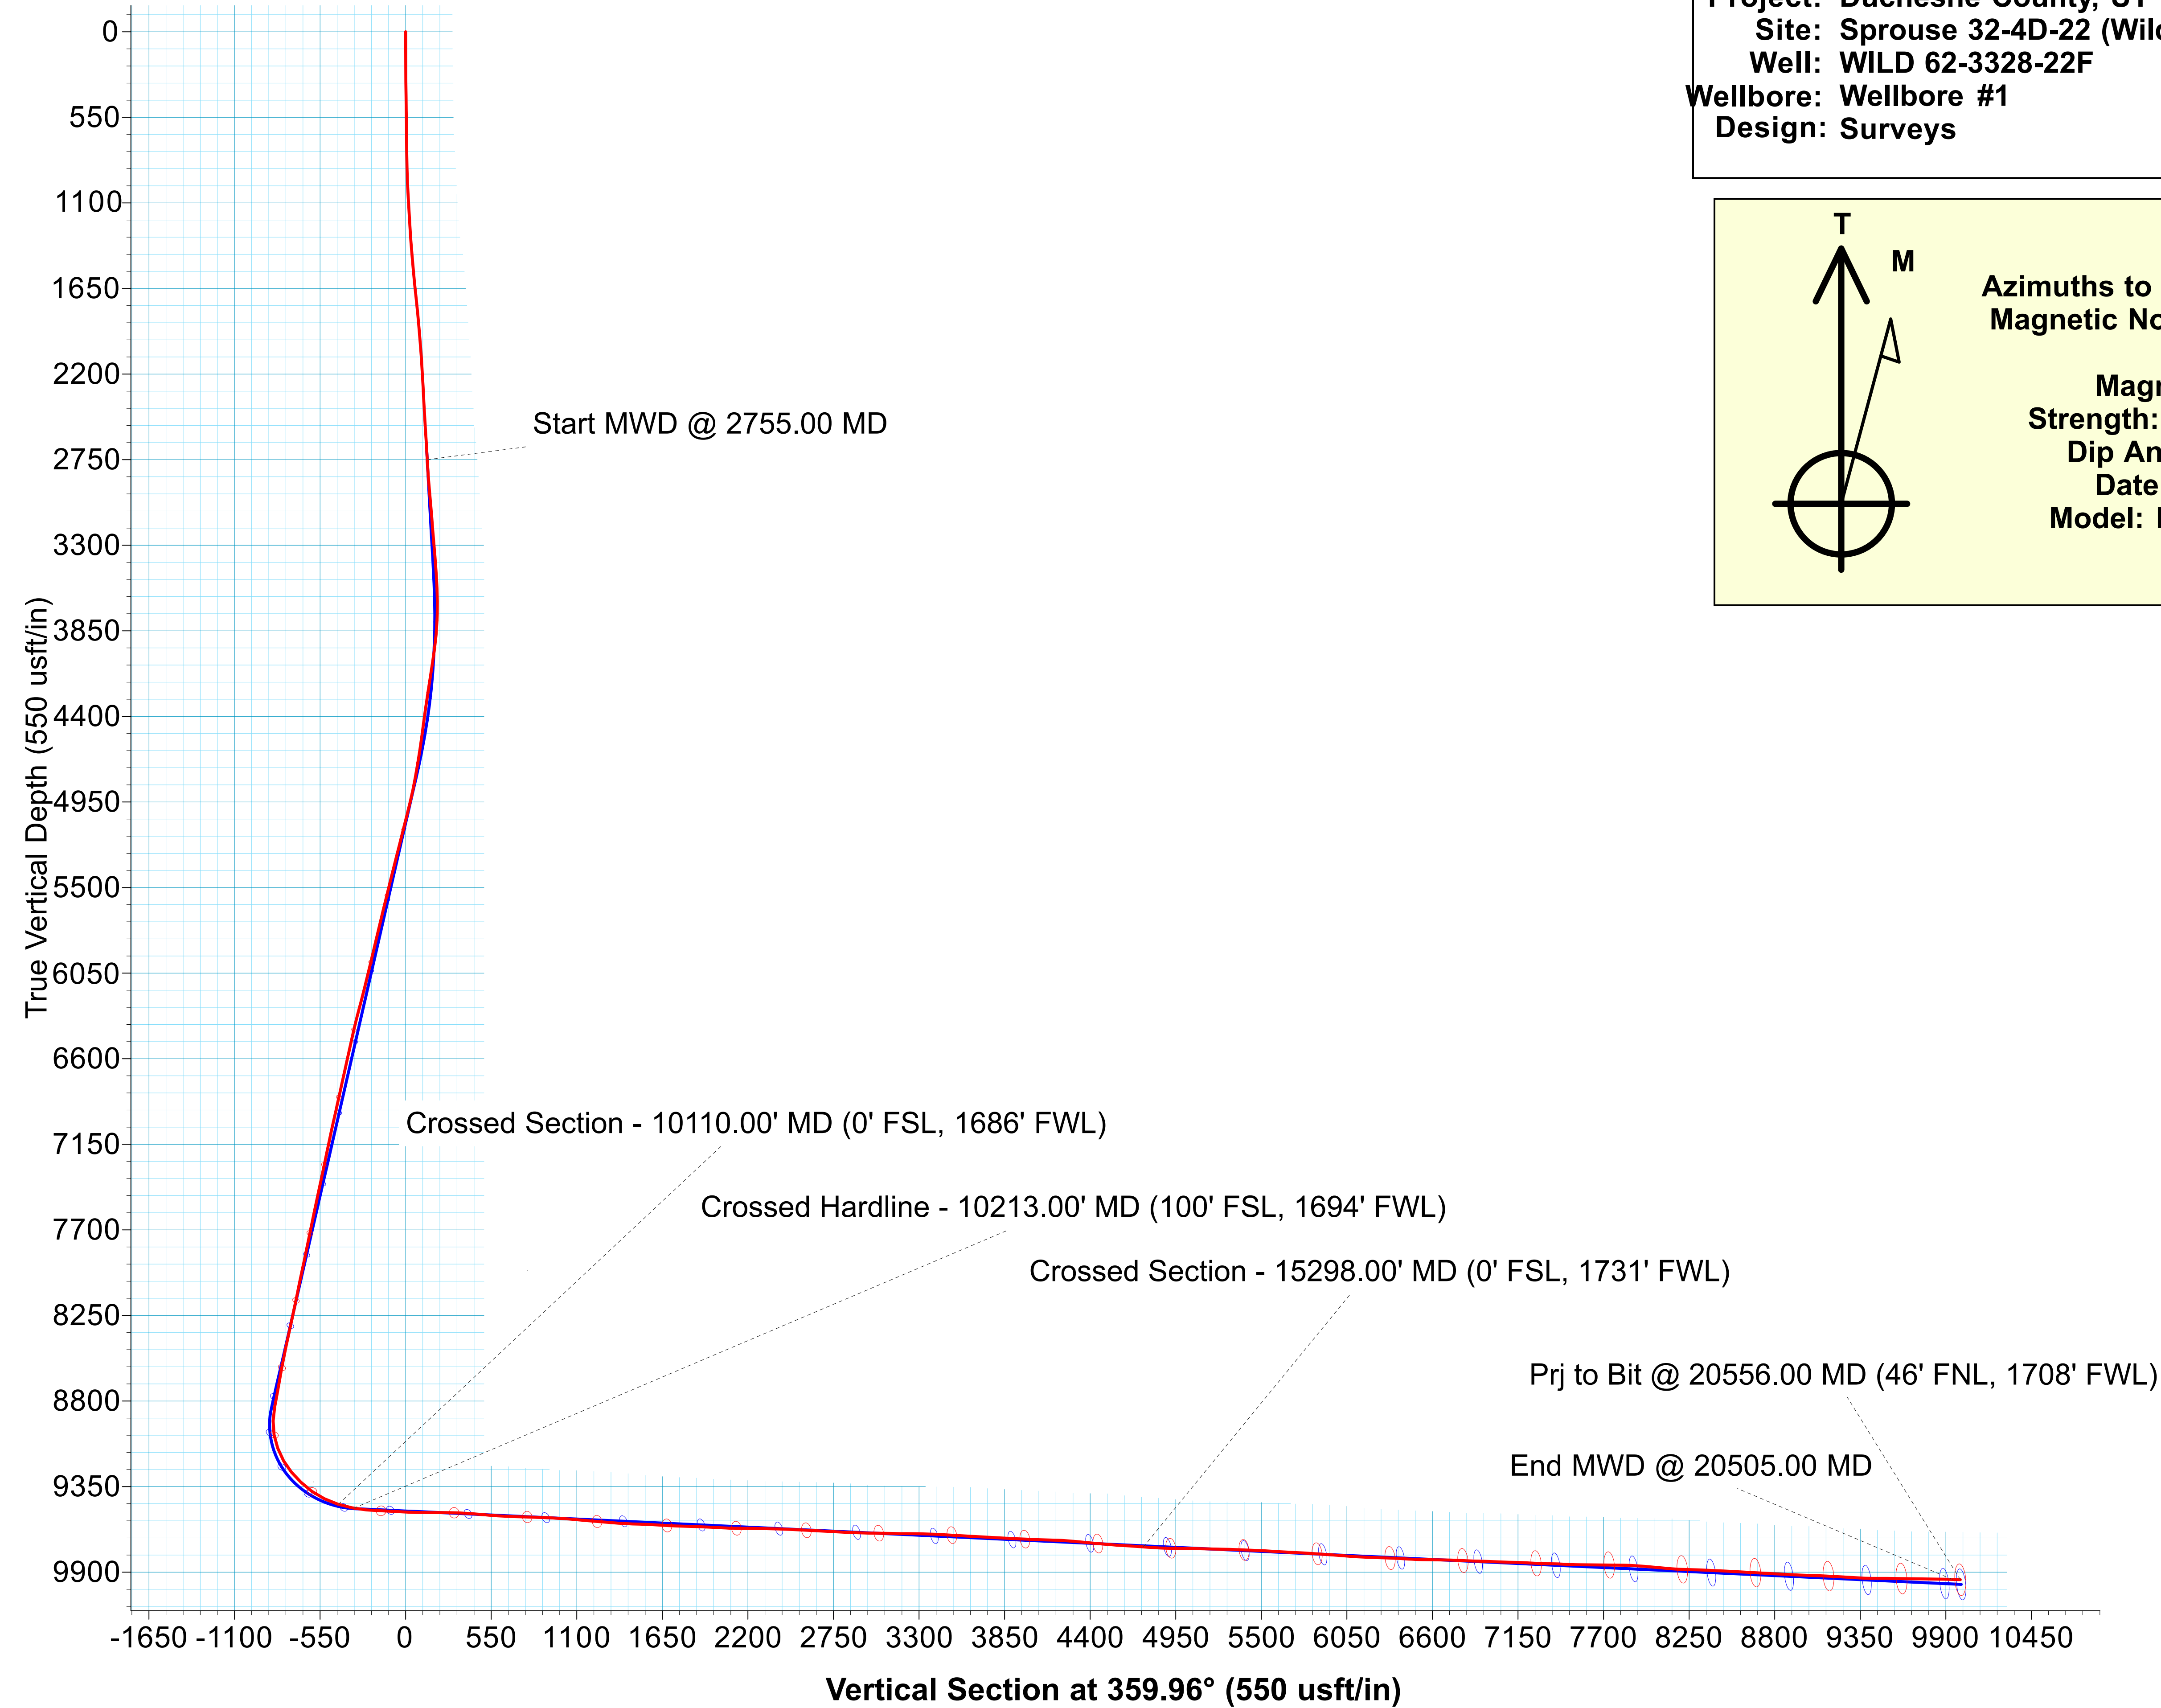

Project: Duchesne County, UT (NAD83-True)
Site: Sprouse 32-4D-22 (Wild-Taparoo Pad)
Well: WILD 62-3328-22F
Wellbore: Wellbore #1
Design: Surveys

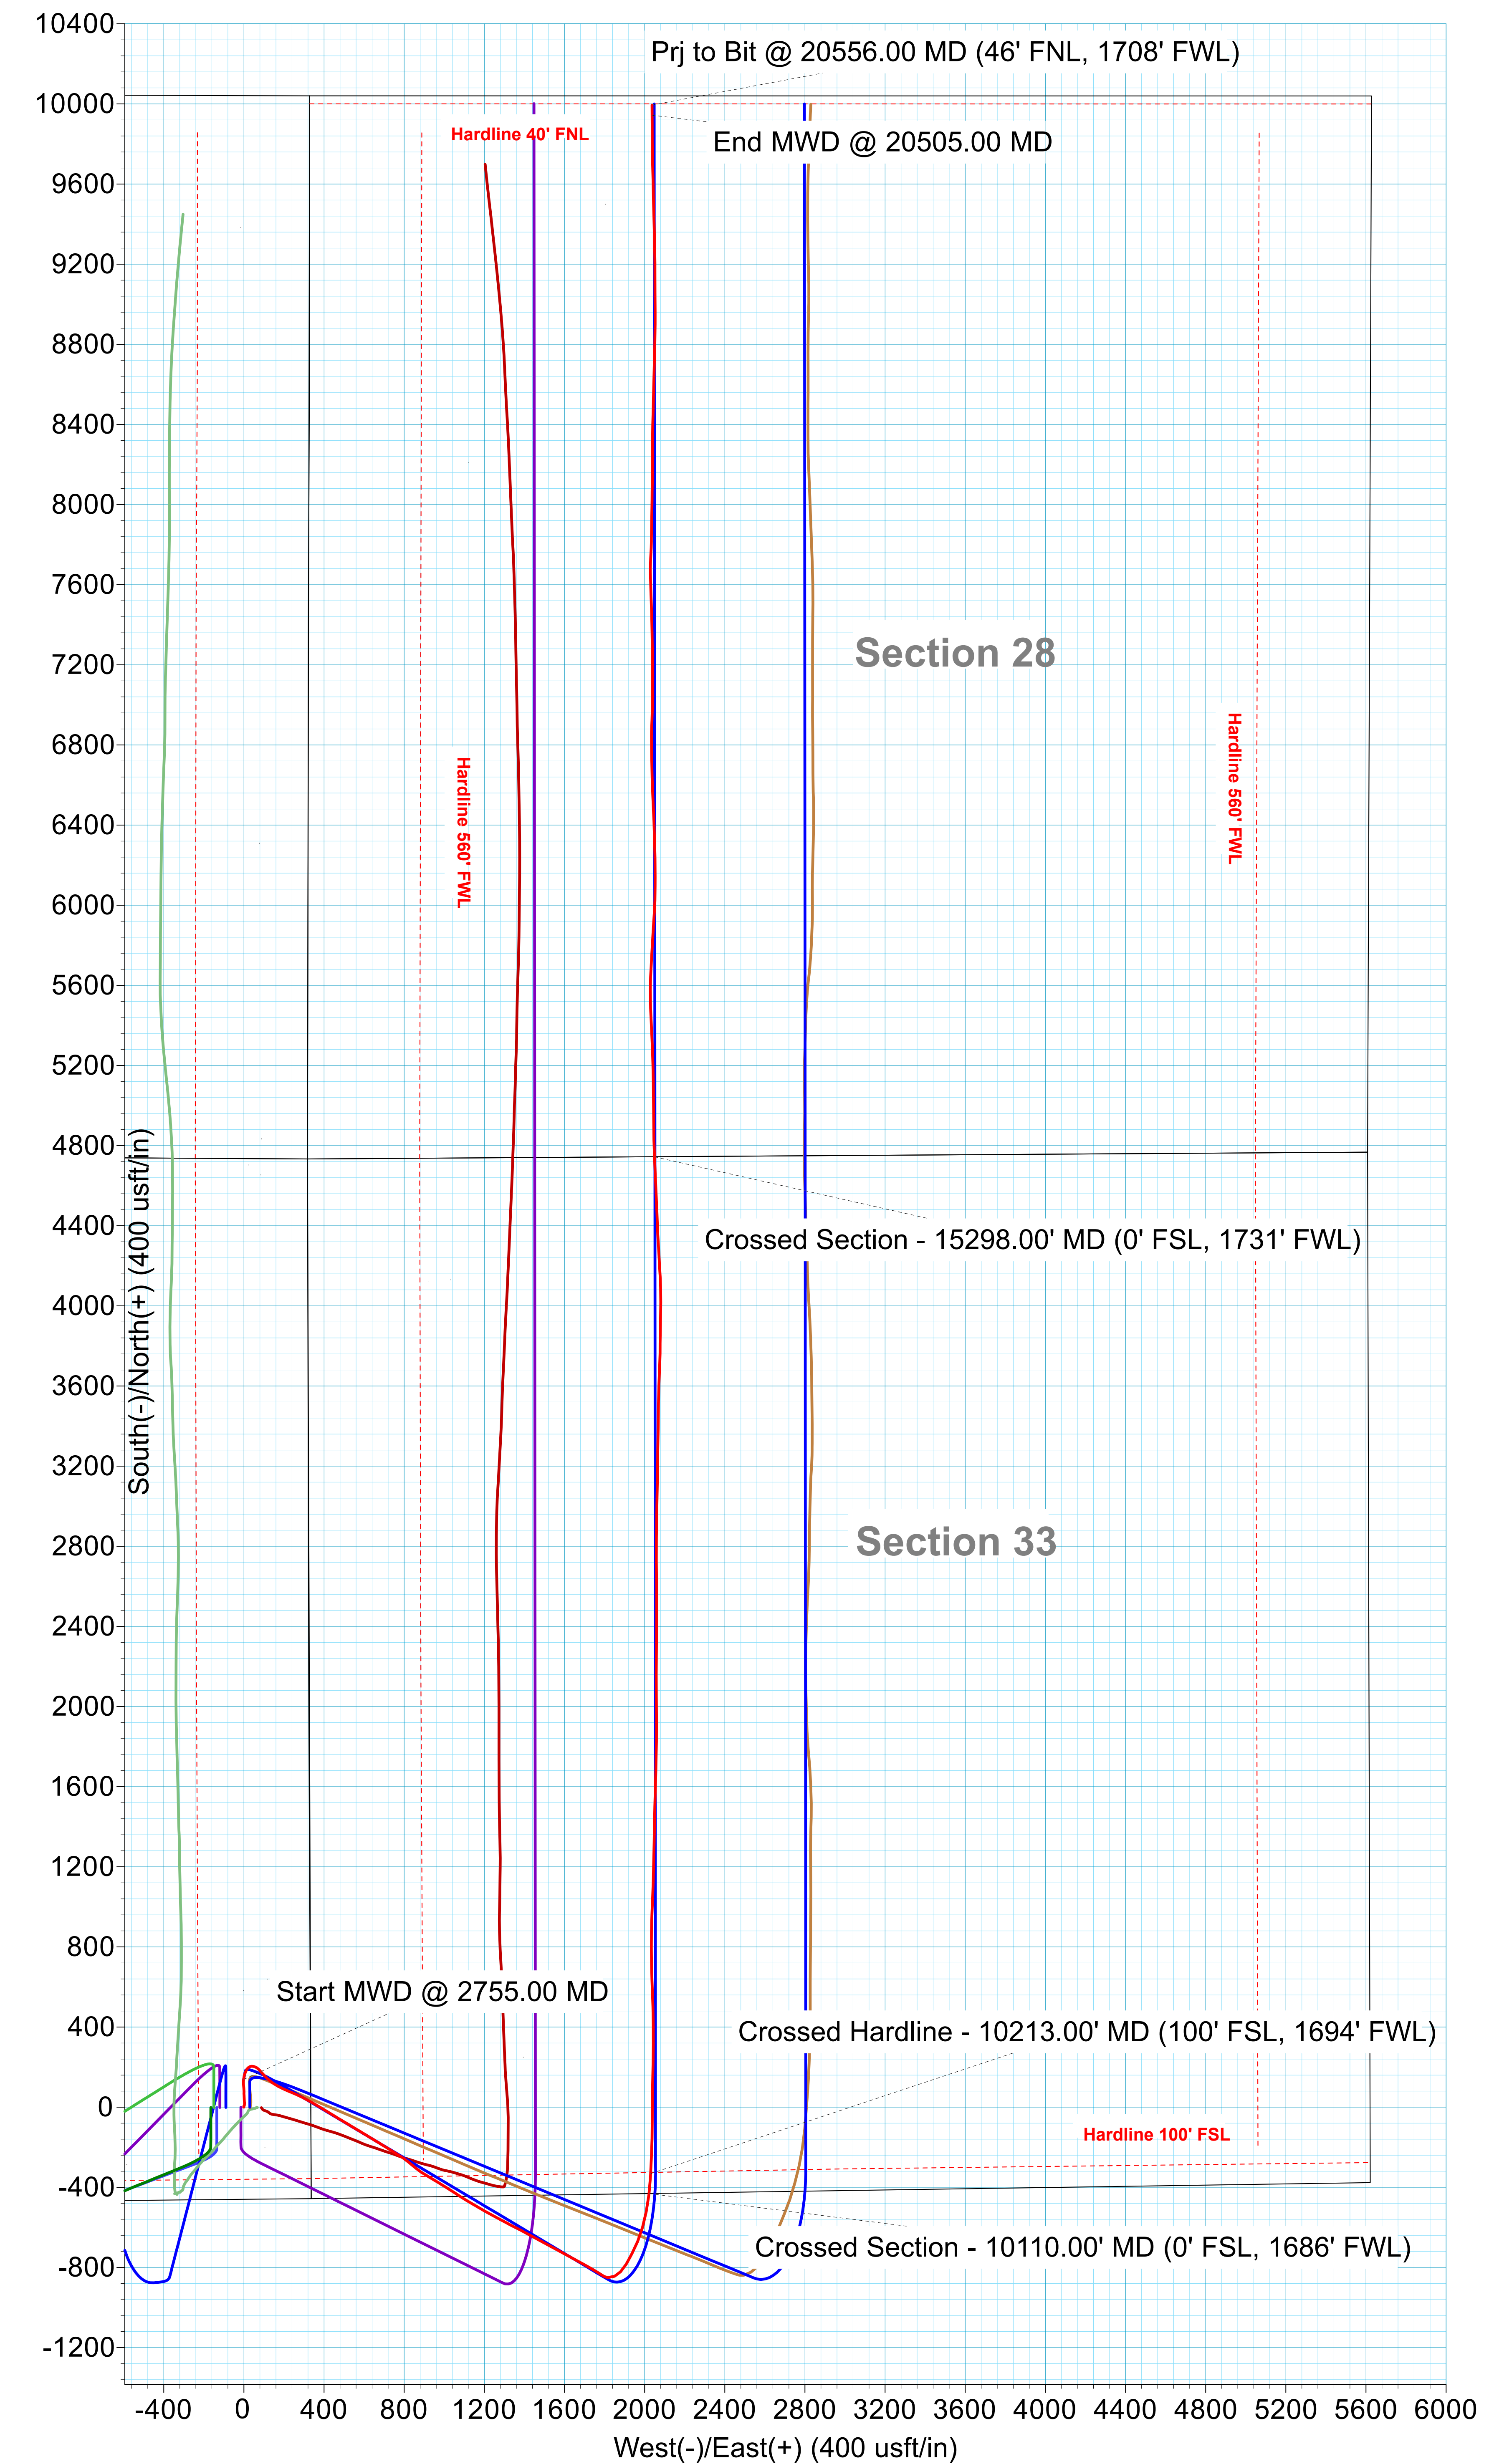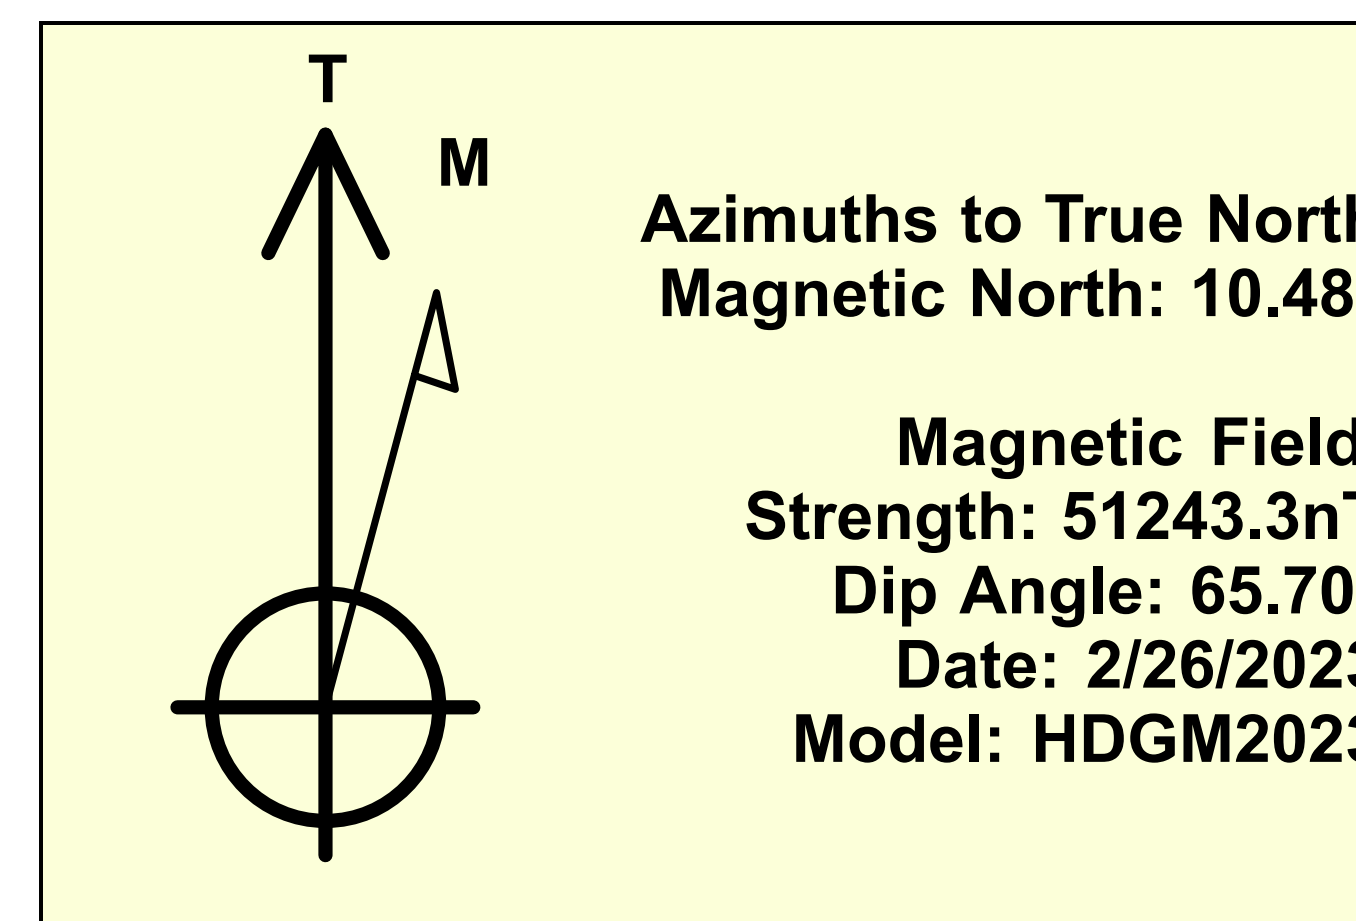



Regulatory- Perforations

Well Name: Wild 62-3328-22F

Well Name Wild 62-3328-22F	Lease Multiple Leases	API/UWI 43013543080000	Government Authority BLM/UTERO
Original KB Elevation (ft) 5,409.00	KB-Mud Line Distance (ft)		KB-Wellhead (ft)

Perforations

Int #	Date	Type	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Shots Plan	Entered Shot Total
1	11/16/2023	Perforated	20,450.0	20,451.0	3.0		21
1	11/16/2023	Perforated	20,430.0	20,431.0	3.0		21
1	11/16/2023	Perforated	20,410.0	20,411.0	3.0		21
1	11/16/2023	Perforated	20,390.0	20,391.0	3.0		21
1	11/16/2023	Perforated	20,370.0	20,371.0	3.0		21
1	11/16/2023	Perforated	20,350.0	20,351.0	3.0		21
1	11/16/2023	Perforated	20,330.0	20,331.0	3.0		21
2	12/8/2023	Perforated	20,310.0	20,311.0	3.0		21
2	12/8/2023	Perforated	20,290.0	20,291.0	3.0		21
2	12/8/2023	Perforated	20,270.0	20,271.0	3.0		21
2	12/8/2023	Perforated	20,250.0	20,251.0	3.0		21
2	12/8/2023	Perforated	20,230.0	20,231.0	3.0		21
2	12/8/2023	Perforated	20,210.0	20,211.0	3.0		21
2	12/8/2023	Perforated	20,190.0	20,191.0	3.0		21
3	12/8/2023	Perforated	20,170.0	20,171.0	3.0		21
3	12/8/2023	Perforated	20,150.0	20,151.0	3.0		21
3	12/8/2023	Perforated	20,130.0	20,131.0	3.0		21
3	12/8/2023	Perforated	20,110.0	20,111.0	3.0		21
3	12/8/2023	Perforated	20,090.0	20,091.0	3.0		21
3	12/8/2023	Perforated	20,070.0	20,071.0	3.0		21
3	12/9/2023	Perforated	20,050.0	20,051.0	3.0		21
4	12/9/2023	Perforated	20,030.0	20,031.0	3.0		21
4	12/9/2023	Perforated	20,010.0	20,011.0	3.0		21
4	12/9/2023	Perforated	19,990.0	19,991.0	3.0		21
4	12/9/2023	Perforated	19,970.0	19,971.0	3.0		21
4	12/9/2023	Perforated	19,950.0	19,951.0	3.0		21
4	12/9/2023	Perforated	19,930.0	19,931.0	3.0		21
4	12/9/2023	Perforated	19,910.0	19,911.0	3.0		21
5	12/10/2023	Perforated	19,888.0	19,889.0	3.0		21
5	12/10/2023	Perforated	19,870.0	19,871.0	3.0		21
5	12/10/2023	Perforated	19,850.0	19,851.0	3.0		21
5	12/10/2023	Perforated	19,830.0	19,831.0	3.0		21
5	12/10/2023	Perforated	19,810.0	19,811.0	3.0		21
5	12/10/2023	Perforated	19,790.0	19,791.0	3.0		21
5	12/10/2023	Perforated	19,770.0	19,771.0	3.0		21
6	12/10/2023	Perforated	19,750.0	19,751.0	3.0		21
6	12/10/2023	Perforated	19,730.0	19,731.0	3.0		21
6	12/10/2023	Perforated	19,710.0	19,711.0	3.0		21
6	12/10/2023	Perforated	19,690.0	19,691.0	3.0		21
6	12/10/2023	Perforated	19,670.0	19,671.0	3.0		21
6	12/10/2023	Perforated	19,650.0	19,651.0	3.0		21
6	12/10/2023	Perforated	19,630.0	19,631.0	3.0		21
7	12/10/2023	Perforated	19,610.0	19,611.0	3.0		21
7	12/10/2023	Perforated	19,590.0	19,591.0	3.0		21
7	12/10/2023	Perforated	19,574.0	19,575.0	3.0		21
7	12/10/2023	Perforated	19,551.0	19,552.0	3.0		21
7	12/10/2023	Perforated	19,530.0	19,531.0	3.0		21
7	12/10/2023	Perforated	19,510.0	19,511.0	3.0		21
7	12/10/2023	Perforated	19,490.0	19,491.0	3.0		21
8	12/11/2023	Perforated	19,470.0	19,471.0	3.0		21
8	12/11/2023	Perforated	19,450.0	19,451.0	3.0		21
8	12/11/2023	Perforated	19,430.0	19,431.0	3.0		21
8	12/11/2023	Perforated	19,411.0	19,412.0	3.0		21
8	12/11/2023	Perforated	19,390.0	19,391.0	3.0		21
8	12/11/2023	Perforated	19,370.0	19,371.0	3.0		21
8	12/11/2023	Perforated	19,350.0	19,351.0	3.0		21
9	12/11/2023	Perforated	19,330.0	19,331.0	3.0		21



Regulatory- Perforations

Well Name: Wild 62-3328-22F

Well Name Wild 62-3328-22F	Lease Multiple Leases	API/UWI 43013543080000	Government Authority BLM/UTERO
Original KB Elevation (ft) 5,409.00	KB-Mud Line Distance (ft)		KB-Wellhead (ft)

Perforations

Int #	Date	Type	Top (ftKB)	Btn (ftKB)	Shot Dens (shots/ft)	Shots Plan	Entered Shot Total
9	12/11/2023	Perforated	19,310.0	19,311.0	3.0		21
9	12/11/2023	Perforated	19,290.0	19,291.0	3.0		21
9	12/11/2023	Perforated	19,268.0	19,269.0	3.0		21
9	12/11/2023	Perforated	19,250.0	19,251.0	3.0		21
9	12/11/2023	Perforated	19,230.0	19,231.0	3.0		21
9	12/11/2023	Perforated	19,210.0	19,211.0	3.0		21
10	12/11/2023	Perforated	19,190.0	19,191.0	3.0		21
10	12/11/2023	Perforated	19,170.0	19,171.0	3.0		21
10	12/11/2023	Perforated	19,150.0	19,151.0	3.0		21
10	12/11/2023	Perforated	19,129.0	19,130.0	3.0		21
10	12/11/2023	Perforated	19,110.0	19,111.0	3.0		21
10	12/11/2023	Perforated	19,090.0	19,091.0	3.0		21
10	12/11/2023	Perforated	19,070.0	19,071.0	3.0		21
11	12/12/2023	Perforated	19,050.0	19,051.0	3.0		21
11	12/12/2023	Perforated	19,030.0	19,031.0	3.0		21
11	12/12/2023	Perforated	19,010.0	19,011.0	3.0		21
11	12/12/2023	Perforated	18,989.0	18,990.0	3.0		21
11	12/12/2023	Perforated	18,970.0	18,971.0	3.0		21
11	12/12/2023	Perforated	18,950.0	18,951.0	3.0		21
11	12/12/2023	Perforated	18,930.0	18,931.0	3.0		21
12	12/12/2023	Perforated	18,910.0	18,911.0	3.0		21
12	12/12/2023	Perforated	18,890.0	18,891.0	3.0		21
12	12/12/2023	Perforated	18,870.0	18,871.0	3.0		21
12	12/12/2023	Perforated	18,850.0	18,851.0	3.0		21
12	12/12/2023	Perforated	18,830.0	18,831.0	3.0		21
12	12/12/2023	Perforated	18,810.0	18,811.0	3.0		21
12	12/12/2023	Perforated	18,790.0	18,791.0	3.0		21
13	12/18/2023	Perforated	18,770.0	18,771.0	3.0		21
13	12/18/2023	Perforated	18,750.0	18,751.0	3.0		21
13	12/18/2023	Perforated	18,730.0	18,731.0	3.0		21
13	12/18/2023	Perforated	18,710.0	18,711.0	3.0		21
13	12/18/2023	Perforated	18,690.0	18,691.0	3.0		21
13	12/18/2023	Perforated	18,671.0	18,672.0	3.0		21
13	12/18/2023	Perforated	18,650.0	18,651.0	3.0		21
14	12/18/2023	Perforated	18,630.0	18,631.0	3.0		21
14	12/18/2023	Perforated	18,610.0	18,611.0	3.0		21
14	12/18/2023	Perforated	18,590.0	18,591.0	3.0		21
14	12/18/2023	Perforated	18,570.0	18,571.0	3.0		21
14	12/18/2023	Perforated	18,550.0	18,551.0	3.0		21
14	12/18/2023	Perforated	18,532.0	18,533.0	3.0		21
14	12/18/2023	Perforated	18,510.0	18,511.0	3.0		21
15	12/19/2023	Perforated	18,490.0	18,491.0	3.0		21
15	12/19/2023	Perforated	18,470.0	18,471.0	3.0		21
15	12/19/2023	Perforated	18,450.0	18,451.0	3.0		21
15	12/19/2023	Perforated	18,430.0	18,431.0	3.0		21
15	12/19/2023	Perforated	18,410.0	18,411.0	3.0		21
15	12/19/2023	Perforated	18,388.0	18,389.0	3.0		21
15	12/19/2023	Perforated	18,370.0	18,371.0	3.0		21
16	12/19/2023	Perforated	18,350.0	18,351.0	3.0		21
16	12/19/2023	Perforated	18,330.0	18,331.0	3.0		21
16	12/19/2023	Perforated	18,310.0	18,311.0	3.0		21
16	12/19/2023	Perforated	18,290.0	18,291.0	3.0		21
16	12/19/2023	Perforated	18,270.0	18,271.0	3.0		21
16	12/19/2023	Perforated	18,249.0	18,250.0	3.0		21
16	12/19/2023	Perforated	18,230.0	18,231.0	3.0		21
17	12/20/2023	Perforated	18,210.0	18,211.0	3.0		21
17	12/20/2023	Perforated	18,190.0	18,191.0	3.0		21



Regulatory- Perforations

Well Name: Wild 62-3328-22F

Well Name Wild 62-3328-22F	Lease Multiple Leases	API/UWI 43013543080000	Government Authority BLM/UTERO
Original KB Elevation (ft) 5,409.00	KB-Mud Line Distance (ft)		KB-Wellhead (ft)

Perforations

Int #	Date	Type	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Shots Plan	Entered Shot Total
17	12/20/2023	Perforated	18,170.0	18,171.0	3.0		21
17	12/20/2023	Perforated	18,150.0	18,151.0	3.0		21
17	12/20/2023	Perforated	18,130.0	18,131.0	3.0		21
17	12/20/2023	Perforated	18,110.0	18,111.0	3.0		21
17	12/20/2023	Perforated	18,090.0	18,091.0	3.0		21
18	12/20/2023	Perforated	18,070.0	18,071.0	3.0		21
18	12/20/2023	Perforated	18,050.0	18,051.0	3.0		21
18	12/20/2023	Perforated	18,030.0	18,031.0	3.0		21
18	12/20/2023	Perforated	18,010.0	18,011.0	3.0		21
18	12/20/2023	Perforated	17,990.0	17,991.0	3.0		21
18	12/20/2023	Perforated	17,970.0	17,971.0	3.0		21
18	12/20/2023	Perforated	17,950.0	17,951.0	3.0		21
19	12/20/2023	Perforated	17,931.0	17,932.0	3.0		21
19	12/20/2023	Perforated	17,910.0	17,911.0	3.0		21
19	12/20/2023	Perforated	17,890.0	17,891.0	3.0		21
19	12/20/2023	Perforated	17,870.0	17,871.0	3.0		21
19	12/20/2023	Perforated	17,850.0	17,851.0	3.0		21
19	12/20/2023	Perforated	17,830.0	17,831.0	3.0		21
19	12/20/2023	Perforated	17,810.0	17,811.0	3.0		21
20	12/20/2023	Perforated	17,791.0	17,792.0	3.0		21
20	12/20/2023	Perforated	17,770.0	17,771.0	3.0		21
20	12/20/2023	Perforated	17,750.0	17,751.0	3.0		21
20	12/20/2023	Perforated	17,730.0	17,731.0	3.0		21
20	12/20/2023	Perforated	17,710.0	17,711.0	3.0		21
20	12/20/2023	Perforated	17,690.0	17,691.0	3.0		21
20	12/20/2023	Perforated	17,670.0	17,671.0	3.0		21
21	12/21/2023	Perforated	17,654.0	17,655.0	3.0		21
21	12/21/2023	Perforated	17,630.0	17,631.0	3.0		21
21	12/21/2023	Perforated	17,610.0	17,611.0	3.0		21
21	12/21/2023	Perforated	17,590.0	17,591.0	3.0		21
21	12/21/2023	Perforated	17,570.0	17,571.0	3.0		21
21	12/21/2023	Perforated	17,550.0	17,551.0	3.0		21
21	12/21/2023	Perforated	17,530.0	17,531.0	3.0		21
22	12/21/2023	Perforated	17,510.0	17,511.0	3.0		21
22	12/21/2023	Perforated	17,490.0	17,491.0	3.0		21
22	12/21/2023	Perforated	17,470.0	17,471.0	3.0		21
22	12/21/2023	Perforated	17,450.0	17,451.0	3.0		21
22	12/21/2023	Perforated	17,430.0	17,431.0	3.0		21
22	12/21/2023	Perforated	17,410.0	17,411.0	3.0		21
22	12/21/2023	Perforated	17,390.0	17,391.0	3.0		21
23	12/21/2023	Perforated	17,370.0	17,371.0	3.0		21
23	12/21/2023	Perforated	17,350.0	17,351.0	3.0		21
23	12/21/2023	Perforated	17,330.0	17,331.0	3.0		21
23	12/21/2023	Perforated	17,310.0	17,311.0	3.0		21
23	12/21/2023	Perforated	17,290.0	17,291.0	3.0		21
23	12/21/2023	Perforated	17,270.0	17,271.0	3.0		21
23	12/21/2023	Perforated	17,250.0	17,251.0	3.0		21
24	12/22/2023	Perforated	17,230.0	17,231.0	3.0		21
24	12/22/2023	Perforated	17,210.0	17,211.0	3.0		21
24	12/22/2023	Perforated	17,192.0	17,193.0	3.0		21
24	12/22/2023	Perforated	17,170.0	17,171.0	3.0		21
24	12/22/2023	Perforated	17,150.0	17,151.0	3.0		21
24	12/22/2023	Perforated	17,130.0	17,131.0	3.0		21
24	12/22/2023	Perforated	17,110.0	17,111.0	3.0		21
25	12/22/2023	Perforated	17,090.0	17,091.0	3.0		21
25	12/22/2023	Perforated	17,070.0	17,071.0	3.0		21
25	12/22/2023	Perforated	17,052.0	17,053.0	3.0		21



Regulatory- Perforations

Well Name: Wild 62-3328-22F

Well Name Wild 62-3328-22F	Lease Multiple Leases	API/UWI 43013543080000	Government Authority BLM/UTERO
Original KB Elevation (ft) 5,409.00	KB-Mud Line Distance (ft)		KB-Wellhead (ft)

Perforations

Int #	Date	Type	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Shots Plan	Entered Shot Total
25	12/22/2023	Perforated	17,030.0	17,031.0	3.0		21
25	12/22/2023	Perforated	17,010.0	17,011.0	3.0		21
25	12/22/2023	Perforated	16,990.0	16,991.0	3.0		21
25	12/22/2023	Perforated	16,970.0	16,971.0	3.0		21
26	12/22/2023	Perforated	16,950.0	16,951.0	3.0		21
26	12/22/2023	Perforated	16,930.0	16,931.0	3.0		21
26	12/22/2023	Perforated	16,908.0	16,909.0	3.0		21
26	12/22/2023	Perforated	16,890.0	16,891.0	3.0		21
26	12/22/2023	Perforated	16,870.0	16,871.0	3.0		21
26	12/22/2023	Perforated	16,850.0	16,851.0	3.0		21
26	12/22/2023	Perforated	16,830.0	16,831.0	3.0		21
27	12/23/2023	Perforated	16,810.0	16,811.0	3.0		21
27	12/23/2023	Perforated	16,790.0	16,791.0	3.0		21
27	12/23/2023	Perforated	16,770.0	16,771.0	3.0		21
27	12/23/2023	Perforated	16,750.0	16,751.0	3.0		21
27	12/23/2023	Perforated	16,730.0	16,731.0	3.0		21
27	12/23/2023	Perforated	16,710.0	16,711.0	3.0		21
27	12/23/2023	Perforated	16,690.0	16,691.0	3.0		21
28	12/23/2023	Perforated	16,670.0	16,671.0	3.0		21
28	12/23/2023	Perforated	16,650.0	16,651.0	3.0		21
28	12/23/2023	Perforated	16,628.0	16,629.0	3.0		21
28	12/23/2023	Perforated	16,610.0	16,611.0	3.0		21
28	12/23/2023	Perforated	16,590.0	16,591.0	3.0		21
28	12/23/2023	Perforated	16,570.0	16,571.0	3.0		21
28	12/23/2023	Perforated	16,550.0	16,551.0	3.0		21
29	12/23/2023	Perforated	16,530.0	16,531.0	3.0		21
29	12/23/2023	Perforated	16,510.0	16,511.0	3.0		21
29	12/23/2023	Perforated	16,490.0	16,491.0	3.0		21
29	12/23/2023	Perforated	16,470.0	16,471.0	3.0		21
29	12/23/2023	Perforated	16,450.0	16,451.0	3.0		21
29	12/23/2023	Perforated	16,430.0	16,431.0	3.0		21
29	12/23/2023	Perforated	16,410.0	16,411.0	3.0		21
30	12/24/2023	Perforated	16,390.0	16,391.0	3.0		21
30	12/24/2023	Perforated	16,370.0	16,371.0	3.0		21
30	12/24/2023	Perforated	16,350.0	16,351.0	3.0		21
30	12/24/2023	Perforated	16,330.0	16,331.0	3.0		21
30	12/24/2023	Perforated	16,310.0	16,311.0	3.0		21
30	12/24/2023	Perforated	16,290.0	16,291.0	3.0		21
30	12/24/2023	Perforated	16,272.0	16,273.0	3.0		21
31	12/25/2023	Perforated	16,250.0	16,251.0	3.0		21
31	12/25/2023	Perforated	16,230.0	16,231.0	3.0		21
31	12/25/2023	Perforated	16,210.0	16,211.0	3.0		21
31	12/25/2023	Perforated	16,190.0	16,191.0	3.0		21
31	12/25/2023	Perforated	16,172.0	16,173.0	3.0		21
31	12/25/2023	Perforated	16,150.0	16,151.0	3.0		21
31	12/25/2023	Perforated	16,132.0	16,133.0	3.0		21
32	12/25/2023	Perforated	16,110.0	16,111.0	3.0		21
32	12/25/2023	Perforated	16,090.0	16,091.0	3.0		21
32	12/25/2023	Perforated	16,070.0	16,071.0	3.0		21
32	12/25/2023	Perforated	16,050.0	16,051.0	3.0		21
32	12/25/2023	Perforated	16,030.0	16,031.0	3.0		21
32	12/25/2023	Perforated	16,010.0	16,011.0	3.0		21
32	12/25/2023	Perforated	15,995.0	15,996.0	3.0		21
33	12/25/2023	Perforated	15,970.0	15,971.0	3.0		21
33	12/25/2023	Perforated	15,950.0	15,951.0	3.0		21
33	12/25/2023	Perforated	15,930.0	15,931.0	3.0		21
33	12/25/2023	Perforated	15,910.0	15,911.0	3.0		21



Regulatory- Perforations

Well Name: Wild 62-3328-22F

Well Name Wild 62-3328-22F	Lease Multiple Leases	API/UWI 43013543080000	Government Authority BLM/UTERO
Original KB Elevation (ft) 5,409.00	KB-Mud Line Distance (ft)		KB-Wellhead (ft)

Perforations

Int #	Date	Type	Top (ftKB)	Btn (ftKB)	Shot Dens (shots/ft)	Shots Plan	Entered Shot Total
33	12/25/2023	Perforated	15,893.0	15,894.0	3.0		21
33	12/25/2023	Perforated	15,870.0	15,871.0	3.0		21
33	12/25/2023	Perforated	15,853.0	15,854.0	3.0		21
34	12/26/2023	Perforated	15,830.0	15,831.0	3.0		21
34	12/26/2023	Perforated	15,810.0	15,811.0	3.0		21
34	12/26/2023	Perforated	15,790.0	15,791.0	3.0		21
34	12/26/2023	Perforated	15,770.0	15,771.0	3.0		21
34	12/26/2023	Perforated	15,753.0	15,754.0	3.0		21
34	12/26/2023	Perforated	15,730.0	15,731.0	3.0		21
34	12/26/2023	Perforated	15,714.0	15,715.0	3.0		21
35	12/26/2023	Perforated	15,690.0	15,691.0	3.0		21
35	12/26/2023	Perforated	15,670.0	15,671.0	3.0		21
35	12/26/2023	Perforated	15,650.0	15,651.0	3.0		21
35	12/26/2023	Perforated	15,630.0	15,631.0	3.0		21
35	12/26/2023	Perforated	15,608.0	15,609.0	3.0		21
35	12/26/2023	Perforated	15,590.0	15,591.0	3.0		21
35	12/26/2023	Perforated	15,575.0	15,576.0	3.0		21
36	12/26/2023	Perforated	15,550.0	15,551.0	3.0		21
36	12/26/2023	Perforated	15,530.0	15,531.0	3.0		21
36	12/26/2023	Perforated	15,510.0	15,511.0	3.0		21
36	12/26/2023	Perforated	15,490.0	15,491.0	3.0		21
36	12/26/2023	Perforated	15,470.0	15,471.0	3.0		21
36	12/26/2023	Perforated	15,450.0	15,451.0	3.0		21
36	12/26/2023	Perforated	15,430.0	15,431.0	3.0		21
37	12/26/2023	Perforated	15,410.0	15,411.0	3.0		21
37	12/26/2023	Perforated	15,390.0	15,391.0	3.0		21
37	12/26/2023	Perforated	15,370.0	15,371.0	3.0		21
37	12/26/2023	Perforated	15,350.0	15,351.0	3.0		21
37	12/26/2023	Perforated	15,330.0	15,331.0	3.0		21
37	12/26/2023	Perforated	15,310.0	15,311.0	3.0		21
37	12/26/2023	Perforated	15,290.0	15,291.0	3.0		21
38	12/27/2023	Perforated	15,270.0	15,271.0	3.0		21
38	12/27/2023	Perforated	15,250.0	15,251.0	3.0		21
38	12/27/2023	Perforated	15,230.0	15,231.0	3.0		21
38	12/27/2023	Perforated	15,210.0	15,211.0	3.0		21
38	12/27/2023	Perforated	15,190.0	15,191.0	3.0		21
38	12/27/2023	Perforated	15,170.0	15,171.0	3.0		21
38	12/27/2023	Perforated	15,151.0	15,152.0	3.0		21
39	12/27/2023	Perforated	15,130.0	15,131.0	3.0		21
39	12/27/2023	Perforated	15,110.0	15,111.0	3.0		21
39	12/27/2023	Perforated	15,090.0	15,091.0	3.0		21
39	12/27/2023	Perforated	15,070.0	15,071.0	3.0		21
39	12/27/2023	Perforated	15,050.0	15,051.0	3.0		21
39	12/27/2023	Perforated	15,030.0	15,031.0	3.0		21
39	12/27/2023	Perforated	15,011.0	15,010.0	3.0		21
40	12/27/2023	Perforated	14,990.0	14,991.0	3.0		21
40	12/27/2023	Perforated	14,970.0	14,971.0	3.0		21
40	12/27/2023	Perforated	14,950.0	14,951.0	3.0		21
40	12/27/2023	Perforated	14,930.0	14,931.0	3.0		21
40	12/27/2023	Perforated	14,910.0	14,911.0	3.0		21
40	12/27/2023	Perforated	14,890.0	14,891.0	3.0		21
40	12/27/2023	Perforated	14,874.0	14,875.0	3.0		21
41	12/28/2023	Perforated	14,850.0	14,851.0	3.0		21
41	12/28/2023	Perforated	14,830.0	14,831.0	3.0		21
41	12/28/2023	Perforated	14,810.0	14,811.0	3.0		21
41	12/28/2023	Perforated	14,790.0	14,791.0	3.0		21
41	12/28/2023	Perforated	14,770.0	14,771.0	3.0		21



Regulatory- Perforations

Well Name: Wild 62-3328-22F

Well Name Wild 62-3328-22F	Lease Multiple Leases	API/UWI 43013543080000	Government Authority BLM/UTERO
Original KB Elevation (ft) 5,409.00	KB-Mud Line Distance (ft)		KB-Wellhead (ft)

Perforations

Int #	Date	Type	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Shots Plan	Entered Shot Total
41	12/28/2023	Perforated	14,750.0	14,751.0	3.0		21
41	12/28/2023	Perforated	14,730.0	14,731.0	3.0		21
42	12/28/2023	Perforated	14,710.0	14,711.0	3.0		21
42	12/28/2023	Perforated	14,690.0	14,691.0	3.0		21
42	12/28/2023	Perforated	14,670.0	14,671.0	3.0		21
42	12/28/2023	Perforated	14,650.0	14,651.0	3.0		21
42	12/28/2023	Perforated	14,630.0	14,631.0	3.0		21
42	12/28/2023	Perforated	14,610.0	14,611.0	3.0		21
42	12/28/2023	Perforated	14,590.0	14,591.0	3.0		21
43	12/29/2023	Perforated	14,570.0	14,571.0	3.0		21
43	12/29/2023	Perforated	14,551.0	14,552.0	3.0		21
43	12/29/2023	Perforated	14,530.0	14,531.0	3.0		21
43	12/29/2023	Perforated	14,510.0	14,511.0	3.0		21
43	12/29/2023	Perforated	14,490.0	14,491.0	3.0		21
43	12/29/2023	Perforated	14,470.0	14,471.0	3.0		21
43	12/29/2023	Perforated	14,450.0	14,451.0	3.0		21
44	12/29/2023	Perforated	14,430.0	14,431.0	3.0		21
44	12/29/2023	Perforated	14,411.0	14,412.0	3.0		21
44	12/29/2023	Perforated	14,390.0	14,391.0	3.0		21
44	12/29/2023	Perforated	14,370.0	14,371.0	3.0		21
44	12/29/2023	Perforated	14,350.0	14,351.0	3.0		21
44	12/29/2023	Perforated	14,330.0	14,331.0	3.0		21
44	12/29/2023	Perforated	14,310.0	14,311.0	3.0		21
45	12/29/2023	Perforated	14,290.0	14,291.0	3.0		21
45	12/29/2023	Perforated	14,271.0	14,272.0	3.0		21
45	12/29/2023	Perforated	14,250.0	14,251.0	3.0		21
45	12/29/2023	Perforated	14,230.0	14,231.0	3.0		21
45	12/29/2023	Perforated	14,210.0	14,211.0	3.0		21
45	12/29/2023	Perforated	14,190.0	14,191.0	3.0		21
45	12/29/2023	Perforated	14,170.0	14,171.0	3.0		21
46	12/30/2023	Perforated	14,150.0	14,151.0	3.0		21
46	12/30/2023	Perforated	14,133.0	14,134.0	3.0		21
46	12/30/2023	Perforated	14,110.0	14,111.0	3.0		21
46	12/30/2023	Perforated	14,090.0	14,091.0	3.0		21
46	12/30/2023	Perforated	14,070.0	14,071.0	3.0		21
46	12/30/2023	Perforated	14,050.0	14,051.0	3.0		21
46	12/30/2023	Perforated	14,030.0	14,031.0	3.0		21
47	12/31/2023	Perforated	14,010.0	14,011.0	3.0		21
47	12/31/2023	Perforated	13,987.0	13,988.0	3.0		21
47	12/31/2023	Perforated	13,970.0	13,971.0	3.0		21
47	12/31/2023	Perforated	13,950.0	13,951.0	3.0		21
47	12/31/2023	Perforated	13,930.0	13,931.0	3.0		21
47	12/31/2023	Perforated	13,910.0	13,911.0	3.0		21
47	12/31/2023	Perforated	13,890.0	13,891.0	3.0		21
48	12/31/2023	Perforated	13,870.0	13,871.0	3.0		21
48	12/31/2023	Perforated	13,849.0	13,850.0	3.0		21
48	12/31/2023	Perforated	13,830.0	13,831.0	3.0		21
48	12/31/2023	Perforated	13,810.0	13,811.0	3.0		21
48	12/31/2023	Perforated	13,790.0	13,791.0	3.0		21
48	12/31/2023	Perforated	13,770.0	13,771.0	3.0		21
48	12/31/2023	Perforated	13,750.0	13,751.0	3.0		21
49	12/31/2023	Perforated	13,730.0	13,731.0	3.0		21
49	12/31/2023	Perforated	13,709.0	13,710.0	3.0		21
49	12/31/2023	Perforated	13,690.0	13,691.0	3.0		21
49	12/31/2023	Perforated	13,670.0	13,671.0	3.0		21
49	12/31/2023	Perforated	13,650.0	13,651.0	3.0		21
49	12/31/2023	Perforated	13,630.0	13,631.0	3.0		21



Regulatory- Perforations

Well Name: Wild 62-3328-22F

Well Name Wild 62-3328-22F	Lease Multiple Leases	API/UWI 43013543080000	Government Authority BLM/UTERO
Original KB Elevation (ft) 5,409.00	KB-Mud Line Distance (ft)		KB-Wellhead (ft)

Perforations

Int #	Date	Type	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Shots Plan	Entered Shot Total
49	12/31/2023	Perforated	13,610.0	13,611.0	3.0		21
50	12/31/2023	Perforated	13,590.0	13,591.0	3.0		21
50	12/31/2023	Perforated	13,570.0	13,571.0	3.0		21
50	12/31/2023	Perforated	13,550.0	13,551.0	3.0		21
50	12/31/2023	Perforated	13,530.0	13,531.0	3.0		21
50	12/31/2023	Perforated	13,510.0	13,511.0	3.0		21
50	12/31/2023	Perforated	13,491.0	13,492.0	3.0		21
50	12/31/2023	Perforated	13,470.0	13,471.0	3.0		21
51	1/1/2024	Perforated	13,450.0	13,451.0	3.0		21
51	1/1/2024	Perforated	13,430.0	13,431.0	3.0		21
51	1/1/2024	Perforated	13,410.0	13,411.0	3.0		21
51	1/1/2024	Perforated	13,390.0	13,391.0	3.0		21
51	1/1/2024	Perforated	13,370.0	13,371.0	3.0		21
51	1/1/2024	Perforated	13,353.0	13,354.0	3.0		21
51	1/1/2024	Perforated	13,330.0	13,331.0	3.0		21
52	1/1/2024	Perforated	13,310.0	13,311.0	3.0		21
52	1/1/2024	Perforated	13,290.0	13,291.0	3.0		21
52	1/1/2024	Perforated	13,270.0	13,271.0	3.0		21
52	1/1/2024	Perforated	13,250.0	13,251.0	3.0		21
52	1/1/2024	Perforated	13,230.0	13,231.0	3.0		21
52	1/1/2024	Perforated	13,213.0	13,214.0	3.0		21
52	1/1/2024	Perforated	13,190.0	13,191.0	3.0		21
53	1/2/2024	Perforated	13,170.0	13,171.0	3.0		21
53	1/2/2024	Perforated	13,150.0	13,151.0	3.0		21
53	1/2/2024	Perforated	13,130.0	13,131.0	3.0		21
53	1/2/2024	Perforated	13,110.0	13,111.0	3.0		21
53	1/2/2024	Perforated	13,090.0	13,091.0	3.0		21
53	1/2/2024	Perforated	13,068.0	13,069.0	3.0		21
53	1/2/2024	Perforated	13,050.0	13,051.0	3.0		21
54	1/2/2024	Perforated	13,031.0	13,032.0	3.0		21
54	1/2/2024	Perforated	13,010.0	13,011.0	3.0		21
54	1/2/2024	Perforated	12,990.0	12,991.0	3.0		21
54	1/2/2024	Perforated	12,970.0	12,971.0	3.0		21
54	1/2/2024	Perforated	12,950.0	12,951.0	3.0		21
54	1/2/2024	Perforated	12,930.0	12,931.0	3.0		21
54	1/2/2024	Perforated	12,910.0	12,911.0	3.0		21
55	1/2/2024	Perforated	12,891.0	12,892.0	3.0		21
55	1/2/2024	Perforated	12,870.0	12,871.0	3.0		21
55	1/2/2024	Perforated	12,850.0	12,851.0	3.0		21
55	1/2/2024	Perforated	12,830.0	12,831.0	3.0		21
55	1/2/2024	Perforated	12,810.0	12,811.0	3.0		21
55	1/2/2024	Perforated	12,790.0	12,791.0	3.0		21
55	1/2/2024	Perforated	12,770.0	12,771.0	3.0		21
56	1/2/2024	Perforated	12,753.0	12,754.0	3.0		21
56	1/2/2024	Perforated	12,730.0	12,731.0	3.0		21
56	1/2/2024	Perforated	12,710.0	12,711.0	3.0		21
56	1/2/2024	Perforated	12,690.0	12,691.0	3.0		21
56	1/2/2024	Perforated	12,670.0	12,671.0	3.0		21
56	1/2/2024	Perforated	12,650.0	12,651.0	3.0		21
56	1/2/2024	Perforated	12,630.0	12,631.0	3.0		21
57	1/3/2024	Perforated	12,613.0	12,614.0	3.0		21
57	1/3/2024	Perforated	12,590.0	12,591.0	3.0		21
57	1/3/2024	Perforated	12,570.0	12,571.0	3.0		21
57	1/3/2024	Perforated	12,550.0	12,551.0	3.0		21
57	1/3/2024	Perforated	12,530.0	12,531.0	3.0		21
57	1/3/2024	Perforated	12,510.0	12,511.0	3.0		21
57	1/3/2024	Perforated	12,490.0	12,491.0	3.0		21



Regulatory- Perforations

Well Name: Wild 62-3328-22F

Well Name Wild 62-3328-22F	Lease Multiple Leases	API/UWI 43013543080000	Government Authority BLM/UTERO
Original KB Elevation (ft) 5,409.00	KB-Mud Line Distance (ft)		KB-Wellhead (ft)

Perforations

Int #	Date	Type	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Shots Plan	Entered Shot Total
58	1/3/2024	Perforated	12,468.0	12,469.0	3.0		21
58	1/3/2024	Perforated	12,450.0	12,451.0	3.0		21
58	1/3/2024	Perforated	12,430.0	12,431.0	3.0		21
58	1/3/2024	Perforated	12,410.0	12,411.0	3.0		21
58	1/3/2024	Perforated	12,390.0	12,391.0	3.0		21
58	1/3/2024	Perforated	12,370.0	12,371.0	3.0		21
58	1/3/2024	Perforated	12,350.0	12,351.0	3.0		21
59	1/4/2024	Perforated	12,330.0	12,331.0	3.0		21
59	1/4/2024	Perforated	12,310.0	12,311.0	3.0		21
59	1/4/2024	Perforated	12,290.0	12,291.0	3.0		21
59	1/4/2024	Perforated	12,270.0	12,271.0	3.0		21
59	1/4/2024	Perforated	12,250.0	12,251.0	3.0		21
59	1/4/2024	Perforated	12,230.0	12,231.0	3.0		21
59	1/4/2024	Perforated	12,210.0	12,211.0	3.0		21
60	1/4/2024	Perforated	12,190.0	12,191.0	3.0		21
60	1/4/2024	Perforated	12,170.0	12,171.0	3.0		21
60	1/4/2024	Perforated	12,152.0	12,153.0	3.0		21
60	1/4/2024	Perforated	12,130.0	12,131.0	3.0		21
60	1/4/2024	Perforated	12,110.0	12,111.0	3.0		21
60	1/4/2024	Perforated	12,090.0	12,091.0	3.0		21
60	1/4/2024	Perforated	12,070.0	12,071.0	3.0		21
61	1/4/2024	Perforated	12,050.0	12,051.0	3.0		21
61	1/4/2024	Perforated	12,030.0	12,031.0	3.0		21
61	1/4/2024	Perforated	12,012.0	12,013.0	3.0		21
61	1/4/2024	Perforated	11,990.0	11,991.0	3.0		21
61	1/4/2024	Perforated	11,970.0	11,971.0	3.0		21
61	1/4/2024	Perforated	11,950.0	11,951.0	3.0		21
61	1/4/2025	Perforated	11,930.0	11,931.0	3.0		21
62	1/5/2025	Perforated	11,910.0	11,911.0	3.0		21
62	1/5/2025	Perforated	11,890.0	11,891.0	3.0		21
62	1/5/2025	Perforated	11,872.0	11,873.0	3.0		21
62	1/5/2025	Perforated	11,850.0	11,851.0	3.0		21
62	1/5/2025	Perforated	11,830.0	11,831.0	3.0		21
62	1/5/2025	Perforated	11,810.0	11,811.0	3.0		21
62	1/5/2025	Perforated	11,790.0	11,791.0	3.0		21
63	1/6/2024	Perforated	11,770.0	11,771.0	3.0		21
63	1/6/2024	Perforated	11,750.0	11,751.0	3.0		21
63	1/6/2024	Perforated	11,733.0	11,734.0	3.0		21
63	1/6/2024	Perforated	11,710.0	11,711.0	3.0		21
63	1/6/2024	Perforated	11,690.0	11,691.0	3.0		21
63	1/6/2024	Perforated	11,670.0	11,671.0	3.0		21
63	1/6/2024	Perforated	11,650.0	11,651.0	3.0		21
64	1/6/2024	Perforated	11,630.0	11,631.0	3.0		21
64	1/6/2024	Perforated	11,610.0	11,611.0	3.0		21
64	1/6/2024	Perforated	11,587.0	11,588.0	3.0		21
64	1/6/2024	Perforated	11,570.0	11,571.0	3.0		21
64	1/6/2024	Perforated	11,550.0	11,551.0	3.0		21
64	1/6/2024	Perforated	11,530.0	11,531.0	3.0		21
64	1/6/2024	Perforated	11,510.0	11,511.0	3.0		21
65	1/7/2024	Perforated	11,490.0	11,491.0	3.0		21
65	1/7/2024	Perforated	11,470.0	11,471.0	3.0		21
65	1/7/2024	Perforated	11,449.0	11,450.0	3.0		21
65	1/7/2024	Perforated	11,430.0	11,431.0	3.0		21
65	1/7/2024	Perforated	11,410.0	11,411.0	3.0		21
65	1/7/2024	Perforated	11,390.0	11,391.0	3.0		21
65	1/7/2024	Perforated	11,372.0	11,373.0	3.0		21
66	1/7/2024	Perforated	11,350.0	11,351.0	3.0		21



Regulatory- Perforations

Well Name: Wild 62-3328-22F

Well Name Wild 62-3328-22F	Lease Multiple Leases	API/UWI 43013543080000	Government Authority BLM/UTERO
Original KB Elevation (ft) 5,409.00	KB-Mud Line Distance (ft)		KB-Wellhead (ft)

Perforations

Int #	Date	Type	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Shots Plan	Entered Shot Total
66	1/7/2024	Perforated	11,330.0	11,331.0	3.0		21
66	1/7/2024	Perforated	11,310.0	11,311.0	3.0		21
66	1/7/2024	Perforated	11,290.0	11,291.0	3.0		21
66	1/7/2024	Perforated	11,272.0	11,273.0	3.0		21
66	1/7/2024	Perforated	11,250.0	11,251.0	3.0		21
66	1/7/2024	Perforated	11,230.0	11,231.0	3.0		21
67	1/7/2024	Perforated	11,210.0	11,211.0	3.0		21
67	1/7/2024	Perforated	11,190.0	11,191.0	3.0		21
67	1/7/2024	Perforated	11,170.0	11,171.0	3.0		21
67	1/7/2024	Perforated	11,148.0	11,149.0	3.0		21
67	1/7/2024	Perforated	11,130.0	11,131.0	3.0		21
67	1/7/2024	Perforated	11,110.0	11,111.0	3.0		21
67	1/7/2024	Perforated	11,090.0	11,091.0	3.0		21
68	1/8/2024	Perforated	11,070.0	11,071.0	3.0		21
68	1/8/2024	Perforated	11,050.0	11,051.0	3.0		21
68	1/8/2024	Perforated	11,030.0	11,031.0	3.0		21
68	1/8/2024	Perforated	11,010.0	11,011.0	3.0		21
68	1/8/2024	Perforated	10,990.0	10,991.0	3.0		21
68	1/8/2024	Perforated	10,970.0	10,971.0	3.0		21
68	1/8/2024	Perforated	10,950.0	10,951.0	3.0		21
69	1/8/2024	Perforated	10,930.0	10,931.0	3.0		21
69	1/8/2024	Perforated	10,910.0	10,911.0	3.0		21
69	1/8/2024	Perforated	10,890.0	10,891.0	3.0		21
69	1/8/2024	Perforated	10,870.0	10,871.0	3.0		21
69	1/8/2024	Perforated	10,850.0	10,851.0	3.0		21
69	1/8/2024	Perforated	10,832.0	10,833.0	3.0		21
69	1/8/2024	Perforated	10,810.0	10,811.0	3.0		21
70	1/8/2024	Perforated	10,790.0	10,791.0	3.0		21
70	1/8/2024	Perforated	10,770.0	10,771.0	3.0		21
70	1/8/2024	Perforated	10,750.0	10,751.0	3.0		21
70	1/8/2024	Perforated	10,730.0	10,731.0	3.0		21
70	1/8/2024	Perforated	10,710.0	10,711.0	3.0		21
70	1/8/2024	Perforated	10,693.0	10,694.0	3.0		21
70	1/8/2024	Perforated	10,670.0	10,671.0	3.0		21
71	1/8/2024	Perforated	10,650.0	10,651.0	3.0		21
71	1/8/2024	Perforated	10,630.0	10,631.0	3.0		21
71	1/8/2024	Perforated	10,610.0	10,611.0	3.0		21
71	1/8/2024	Perforated	10,590.0	10,591.0	3.0		21
71	1/8/2024	Perforated	10,570.0	10,571.0	3.0		21
71	1/8/2024	Perforated	10,548.0	10,549.0	3.0		21
71	1/8/2024	Perforated	10,530.0	10,531.0	3.0		21
72	1/9/2024	Perforated	10,510.0	10,511.0	3.0		21
72	1/9/2024	Perforated	10,490.0	10,491.0	3.0		21
72	1/9/2024	Perforated	10,470.0	10,471.0	3.0		21
72	1/9/2024	Perforated	10,450.0	10,451.0	3.0		21
72	1/9/2024	Perforated	10,430.0	10,431.0	3.0		21
72	1/9/2024	Perforated	10,413.0	10,414.0	3.0		21
72	1/9/2024	Perforated	10,390.0	10,391.0	3.0		21
73	1/9/2024	Perforated	10,370.0	10,371.0	3.0		21
73	1/9/2024	Perforated	10,350.0	10,351.0	3.0		21
73	1/9/2024	Perforated	10,330.0	10,331.0	3.0		21
73	1/9/2024	Perforated	10,310.0	10,311.0	3.0		21
73	1/9/2024	Perforated	10,290.0	10,291.0	3.0		21
73	1/9/2024	Perforated	10,270.0	10,271.0	3.0		21
73	1/9/2024	Perforated	10,250.0	10,251.0	3.0		21

Total

Wild 62-3328-22F

Stimulations Summary

Type Sand Frac	Stim/Treat Company PROFRAC	Start Date 12/8/2023	End Date
-------------------	-------------------------------	-------------------------	----------

Stimulation Intervals

Interval Number	Vol Clean Total (bbl)	Vol Slurry Total (bbl)	Proppant Total (lb)
1	4,727.80	4,900.09	141,800.0
2	6,315.60	6,694.88	315,320.0
3	6,328.60	6,706.27	315,300.0
4	6,226.20	6,597.86	315,380.0
5	6,251.70	6,627.56	315,400.0
6	6,137.20	6,513.97	315,630.0
7	6,315.80	6,692.88	315,560.0
8	6,354.20	6,731.16	315,400.0
9	6,223.40	6,604.11	315,640.0
10	6,327.30	6,708.26	315,550.0
11	6,324.50	6,703.48	316,000.0
12	6,235.30	6,601.03	315,500.0
13	6,406.10	6,786.37	315,280.0
14	6,307.70	6,683.03	315,220.0
15	8,313.40	8,651.08	278,700.0
16	6,293.10	6,673.27	315,180.0
17	6,196.10	6,573.08	315,287.0
18	6,127.40	6,505.39	315,872.0
19	6,267.90	6,651.68	316,617.0
20	6,281.60	6,656.33	314,900.0
21	5,059.60	5,396.67	295,469.0
22	6,330.00	6,709.16	315,100.0
23	6,488.30	6,880.05	328,100.0
24	6,373.40	6,754.89	315,168.0
25	7,323.60	8,460.35	189,509.0
26	6,213.40	6,592.64	315,785.0
27	6,387.40	6,772.15	315,572.0
28	6,702.50	7,088.52	315,600.0
29	6,408.20	6,793.68	315,929.0
30	8,826.90	10,076.77	245,900.0
31	5,163.50	5,395.09	192,815.0
32	6,362.10	6,747.41	315,172.0
33	6,339.20	7,612.14	310,350.0
34	6,284.10	6,664.99	315,930.0
35	6,320.80	6,702.59	315,091.0
36	6,251.00	6,629.40	315,200.0
37	6,498.90	6,877.33	314,042.0
38	6,272.40	6,653.14	315,300.0
39	6,323.00	6,710.08	315,200.0
40	5,876.50	7,119.90	315,338.0
41	6,263.20	6,638.76	315,200.0
42	6,319.20	6,704.35	315,100.0
43	6,367.20	6,749.37	315,807.0
44	6,411.00	6,811.64	316,100.0
45	6,289.20	6,674.27	315,422.0
46	6,758.90	8,144.99	315,800.0
47	6,303.70	6,687.72	315,720.0
48	6,307.70	6,695.47	315,260.0
49	7,130.50	7,488.05	286,400.0
50	6,302.20	6,690.59	316,859.0
51	6,267.00	6,650.00	316,115.0
52	6,418.10	6,799.33	315,300.0
53	6,744.50	7,132.25	318,960.0
54	6,061.00	6,419.55	315,603.0
55	6,259.70	6,643.01	315,300.0
56	6,255.10	6,638.02	315,300.0
57	6,247.50	6,627.43	315,140.0

Wild 62-3328-22F

Stimulation Intervals				
Interval Number	Vol Clean Total (bbl)		Vol Slurry Total (bbl)	Proppant Total (lb)
58	6,285.20		6,676.63	315,840.0
59	6,234.40		6,616.19	315,220.0
60	6,275.10		6,658.19	315,560.0
61	6,251.60		6,632.47	315,120.0
62	6,196.30		6,574.18	315,460.0
63	6,210.90		6,591.10	315,400.0
64	6,433.60		6,796.04	315,460.0
65	6,445.50		6,828.98	314,720.0
66	6,229.20		6,608.93	315,480.0
67	6,166.10		6,546.08	315,460.0
68	6,065.90		6,444.79	314,610.0
69	6,277.10		6,653.43	314,710.0
70	6,023.00		6,381.55	315,400.0
71	6,343.60		6,734.05	315,400.0
72	6,414.20		6,789.63	314,510.0
73	6,164.30		6,535.31	303,160.0



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00		Accounting ID 60061.01

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
7/12/2023 17:00	7/12/2023 18:00			RTBG	Run Tubing	1.00	Well Prep	TRIP IN HOLE WITH 2 7/8" TUBING FROM 17,873' TO 19,517'
7/12/2023 18:00	7/12/2023 19:30			General Ops	Downhole issues	1.50	Well Prep	CIRCULATE HOLE CLEAN. 2 BPM, 1,100 PSI
7/13/2023 06:00	7/13/2023 06:30			General Ops	Safety Stand-down	0.50	Well Prep	HELD SAFETY MEETING.
7/13/2023 06:30	7/13/2023 07:30			General Ops	Downhole issues	1.00	Well Prep	CIRCULATE HOLE CLEAN.
7/13/2023 07:30	7/13/2023 09:00			RTBG	Run Tubing	1.50	Well Prep	RUN IN HOLE WITH CLEAN OUT ASSEMBLY FROM 19,517' TO 20,403', NO DRAG THE WHOLE TRIP IN LATERAL SECTION.
7/13/2023 09:00	7/13/2023 12:00			General Ops	Downhole issues	3.00	Well Prep	RIG UP SWIVEL, CIRCULATE HOLE CLEAN, NO CEMENT OR DEBRIS AT SHAKERS, SPOT CORRISION INHIBITOR IN PIPE 1%, RIG DOWN SWIVEL
7/13/2023 12:00	7/13/2023 19:00			PTBG	Pull Tubing	7.00	Well Prep	PULL OUT OF HOLE WITH CLEAN OUT ASSEMBLY LAYING DOWN PIPE FROM 20,403' TO 12,900'.
7/13/2023 19:00	7/14/2023 06:00			General Ops	Standby	11.00	Well Prep	WELL SHUT IN, WAIT ON DAYLIGHT.
7/14/2023 06:00	7/14/2023 06:30			General Ops	Safety Stand-down	0.50	Well Prep	HELD SAFETY MEETING, OPEN WELL.
7/14/2023 06:30	7/14/2023 17:30			PTBG	Pull Tubing	11.00	Well Prep	PULL OUT OF HOLE LAYING DOWN PIPE FROM 12,900' TO 0', LAY DOWN CLEAN OUT ASSEMBLY
7/14/2023 17:30	7/15/2023 06:00			General Ops	Standby	12.50	Well Prep	PREP FOR RIG MOVE, WELL SHUT IN.
7/15/2023 06:00	7/15/2023 18:00			General Ops	Rigging Out	12.00	Well Prep	HELD SAFETY MEETING, MOVE STONE 8 WORKOVER RIG OFF WELL,
11/2/2023 06:00	11/2/2023 07:45			General Ops	Rigging In	1.75	Well Prep	ND TA CAP, INSTALL & NU B-SECTION, TEST VOID TO 5,000 PSI, TEST SEALS TO 10,000 PSI, NU STRONG HOLD FRAC VALVE FOR CSG TEST
11/2/2023 07:45	11/2/2023 10:45			Wireline	Logging	3.00	Well Prep	MIRU TWG PULL 60 ARM CALIPER 9,050 TO 2,200 & RCBL LOGS 9,942 TO SURF
11/2/2023 10:45	11/3/2023 06:00			Standby	Well Shut In	19.25	Well Prep	WSI, PREP FOR CASING TEST.
11/3/2023 06:00	11/3/2023 07:00			General Ops	Standby	1.00	Well Prep	WO MAX TO ARRIVE ON LOCATION
11/3/2023 07:00	11/3/2023 12:45			General Ops	Rigging In	5.75	Well Prep	MIRU EQUIPMENT. RU IRON.
11/3/2023 12:45	11/3/2023 13:15			Frac	Pressure Test	0.50	Well Prep	PRIME UP/PRESSURE TEST
11/3/2023 13:15	11/3/2023 13:45			General Ops	Standby	0.50	Well Prep	WAIT ON PRESSURE CABLE TO MONITOR BACK SIDE
11/3/2023 13:45	11/3/2023 15:45			Frac	Injection Test	2.00	Well Prep	OPEN WELL. IWP - 0, PUMP 555 BBL (17 BBL TO LOAD CASING) WATER FLUSH, 400 GA 15%, 50 BBL WATER SPACER, 300 GA. 15%, 538 BBL WATER FLUSH.
11/3/2023 15:45	11/3/2023 16:30			General Ops	Standby	0.75	Well Prep	DROP BALL.
11/3/2023 16:30	11/3/2023 17:22			Frac	Injection Test	0.87	Well Prep	PUM BALL DOWN - 19 BBLS TO LOAD CASING, PUMPED 219 BBLS SAW BALL ACTION, PUMPED A TOTAL OF 1380 BBLS.
11/3/2023 17:22	11/3/2023 17:52			Frac	Pressure Test	0.50	Well Prep	BEGIN STATE PRESSURE TEST - 10,011 PSI END STATE PRESSURE TEST - 10,102 PSI GOOD TEST - WELL READY FOR P&P STAGE 1.
11/3/2023 17:52	11/4/2023 06:00			Frac	Pressure Test	12.13		STANDBY FOR WIRELINE
11/16/2023 06:00	11/16/2023 10:00			General Ops	Rigging Out	4.00	Well Prep	WSI
11/16/2023 10:00	11/16/2023 10:30			General Ops	Rigging In	0.50	Well Prep	RU PRO FRAC PUMP DOWN, PRESSURE TEST 10,000 PSI
11/16/2023 10:30	11/16/2023 11:00			Pump Down	High Rate Flush	0.50	Well Prep	ESTABLISH INJECTION RATE OF 15.4 BPM @ 7,778 PSI WITH 62 BBLS PUMPED
11/16/2023 11:00	11/16/2023 11:15			General Ops	Rigging In	0.25	Well Prep	RU TWG
11/16/2023 11:15	11/16/2023 13:45			General Ops	Rigging Out	2.50	Well Prep	WAIT FOR WATER
11/16/2023 13:45	11/16/2023 15:45			Wireline	Plug & Perf	2.00	Well Prep	RIH, PERF STAGE 1, POOH
11/16/2023 15:45	11/16/2023 16:00			General Ops	Rigging Out	0.25	Well Prep	RDMO TWG
11/16/2023 16:00	11/17/2023 06:00			Standby	Well Shut In	14.00	Well Prep	WSI READY FOR FRAC TREE
11/26/2023 06:00	11/27/2023 06:00			General Ops	Standby	24.00		WSI WAITING FOR FRAC
11/27/2023 06:00	11/28/2023 06:00			General Ops	Standby	24.00		WSI WAITING FOR FRAC
11/28/2023 06:00	11/29/2023 06:00			General Ops	Standby	24.00		WSI WAITING FOR FRAC
11/29/2023 06:00	11/30/2023 06:00			General Ops	Standby	24.00		WSI WAITING FOR FRAC
11/30/2023 06:00	12/1/2023 06:00			General Ops	Standby	24.00		WSI WAITING FOR FRAC
12/1/2023 06:00	12/2/2023 06:00			General Ops	Standby	24.00		WSI WAITING FOR FRAC
12/2/2023 06:00	12/3/2023 06:00			General Ops	Standby	24.00		WSI WAITING FOR FRAC



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00		Accounting ID 60061.01

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
12/3/2023 06:00	12/4/2023 06:00			General Ops	Standby	24.00		WSI WAITING FOR FRAC
12/4/2023 06:00	12/5/2023 06:00			General Ops	Standby	24.00		WSI WAITING FOR FRAC
12/6/2023 06:00	12/7/2023 01:02			General Operations	Rigging In	19.04		Stage 1 - Rigging In
12/7/2023 06:00	12/7/2023 18:55			General Operations	Rigging In	12.92		Stage 1 - Rigging In
12/7/2023 18:55	12/8/2023 06:00			Standby	Well Shut In	11.08		Stage 1 - Well shut in. Ready for frac ops
12/8/2023 06:00	12/8/2023 10:39			Standby	Well Shut In	4.65	Stimulation	Stage 1 - Well shut in. Ready for frac ops
12/8/2023 10:39	12/8/2023 10:41			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 1 - Switching for Frac
12/8/2023 10:41	12/8/2023 10:58			Frac	Frac Pumps	0.28	Stimulation	Stage 1 - Frac pump maintenance. Exceeded 30 min well switch
12/8/2023 10:58	12/8/2023 11:06			Frac	Waiting on Services	0.14	Stimulation	Stage 1 - Frac waiting on PD to spot acid
12/8/2023 11:06	12/8/2023 12:40			Frac	Fracturing	1.57	Stimulation	Stage 1 - Frac operations Stage 1 IWHP: 4,668/ SICP: 5,540 Dropped FracBall for toe isolation to begin stage Start Stage: 10/12 fluid ends End Stage: 8/12 fluid ends
12/8/2023 12:40	12/8/2023 12:49			Frac Tree	Well Switch Wellhead	0.15	Stimulation	Stage 1 - Shutting in and bleeding off well
12/8/2023 12:49	12/8/2023 15:40			Standby	Well Shut In	2.84	Stimulation	Stage 1 - Well shut in. Ready for Wireline
12/8/2023 15:40	12/8/2023 15:41			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 1 - Switching for Wireline
12/8/2023 15:41	12/8/2023 15:43			Wireline	Equalizing	0.04	Stimulation	Stage 1 - Wireline stabbed on and equalizing pressure
12/8/2023 15:43	12/8/2023 17:46			Wireline	WL Run	2.05	Stimulation	Stage 2 - Wireline operations Stage 2
12/8/2023 17:46	12/8/2023 17:48			Frac Tree	Well Switch Wellhead	0.04	Stimulation	Stage 2 - Shutting in and bleeding off well
12/8/2023 17:48	12/8/2023 19:58			Standby	Well Shut In	2.16	Stimulation	Stage 2 - Well shut in. Ready for Frac
12/8/2023 19:58	12/8/2023 20:00			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 2 - Switching for Frac
12/8/2023 20:00	12/8/2023 20:19			Frac	Preventive Maintenance	0.32	Stimulation	Stage 2 - Frac pump maintenance
12/8/2023 20:19	12/8/2023 20:27			Frac	Pressure Test	0.14	Stimulation	Stage 2 - Frac pressure testing and equalizing to well
12/8/2023 20:27	12/8/2023 20:32			Frac	Pressure Test	0.07	Stimulation	Stage 2 - Frac pressure testing and equalizing to well. Exceeded 30 min well switch Profrac slow automated bleed off system
12/8/2023 20:32	12/8/2023 22:19			Frac	Fracturing	1.79	Stimulation	Stage 2 - Frac operations Stage 2 Start Stage: 11/12 IWHP: 4,990/ SICP: 5,760 End Stage: 9/12
12/8/2023 22:19	12/8/2023 22:23			Frac Tree	Well Switch Wellhead	0.06	Stimulation	Stage 2 - Shutting in and bleeding off well
12/8/2023 22:23	12/8/2023 22:25			Frac Tree	Well Switch Wireline	0.04	Stimulation	Stage 2 - Switching for Wireline
12/8/2023 22:25	12/8/2023 22:31			Wireline	Equalizing	0.10	Stimulation	Stage 2 - Wireline stabbed on and equalizing pressure
12/8/2023 22:31	12/8/2023 22:31			Frac Tree	Well Switch Wireline	0.00		Stage 2 - null
12/8/2023 22:31	12/9/2023 00:44			Wireline	WL Run	2.22	Stimulation	Stage 3 - Wireline operations Stage 3
12/9/2023 00:44	12/9/2023 00:53			Frac Tree	Well Switch Wellhead	0.15	Stimulation	Stage 3 - Shutting in and bleeding off well
12/9/2023 00:53	12/9/2023 06:00			Standby	Well Shut In	5.11	Stimulation	Stage 3 - Well shut in. Ready for Frac
12/9/2023 06:00	12/9/2023 06:00			Frac Tree	Well Switch Frac	0.00		Stage 3 - Switching for Frac
12/9/2023 06:00	12/9/2023 06:00			Frac	Preventive Maintenance	0.00		Stage 3 - Frac pump maintenance
12/9/2023 06:00	12/9/2023 06:00			Frac	Blender	0.00		Stage 3 - Frac issue with discharge manifold on blender
12/9/2023 06:00	12/9/2023 06:33			Standby	Well Shut In	0.55	Stimulation	Stage 3 - Well shut in. Ready for Frac



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00	Accounting ID 60061.01	

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
12/9/2023 06:33	12/9/2023 06:35			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 3 - Switching for Frac
12/9/2023 06:35	12/9/2023 07:03			Frac	Preventive Maintenanc e	0.47	Stimulation	Stage 3 - Frac pump maintenance
12/9/2023 07:03	12/9/2023 07:07			Frac	Equalizing	0.08	Stimulation	Stage 3 - Frac equalizing to well. Exceeded 30 min well switch
12/9/2023 07:07	12/9/2023 07:15			Frac	Waiting on Services	0.13	Stimulation	Stage 3 - Frac waiting on PD to spot acid
12/9/2023 07:15	12/9/2023 09:04			Frac	Fracturing	1.82	Stimulation	Stage 3 - Frac operations Stage 3 IWHP: 4,952/ SICP: 5,117 Start Stage: 12/12 FLUID ENDS End Stage: 11/12 FLUID ENDS
12/9/2023 09:04	12/9/2023 09:11			Frac Tree	Well Switch Wellhead	0.11	Stimulation	Stage 3 - Shutting in and bleeding off well
12/9/2023 09:11	12/9/2023 09:48			Standby	Well Shut In	0.61	Stimulation	Stage 3 - Well shut in. Ready for Frac
12/9/2023 09:48	12/9/2023 09:49			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 3 - Switching for Wireline
12/9/2023 09:49	12/9/2023 09:52			Wireline	Equalizing	0.05	Stimulation	Stage 3 - Wireline stabbed on and equalizing pressure
12/9/2023 09:52	12/9/2023 13:08			Wireline	WL Run	3.26	Stimulation	Stage 4 - Wireline operations Stage 4
12/9/2023 13:08	12/9/2023 13:14			Frac Tree	Well Switch Wellhead	0.10	Stimulation	Stage 4 - Shutting in and bleeding off well
12/9/2023 13:14	12/10/2023 00:03			Standby	Well Shut In	10.82	Stimulation	Stage 4 - Well shut in. Ready for Frac
12/10/2023 00:03	12/10/2023 00:05			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 4 - Switching for Frac
12/10/2023 00:05	12/10/2023 00:28			Frac	Preventive Maintenanc e	0.39	Stimulation	Stage 4 - Frac pump maintenance
12/10/2023 00:28	12/10/2023 00:33			Frac	Equalizing	0.08	Stimulation	Stage 4 - Frac equalizing to well
12/10/2023 00:33	12/10/2023 00:41			Frac	Equalizing	0.13	Stimulation	Stage 4 - Frac equalizing to well. Exceeded 30 min well switch Profrac rig in pump, rig off pump
12/10/2023 00:41	12/10/2023 02:41			Frac	Fracturing	2.00	Stimulation	Stage 4 - Frac operations Stage 4 Start Stage: 11/12 IWHP: 4,820/ SICP: 5,340 End Stage: 9/12
12/10/2023 02:41	12/10/2023 02:54			Frac Tree	Well Switch Wellhead	0.21	Stimulation	Stage 4 - Shutting in and bleeding off well
12/10/2023 02:54	12/10/2023 03:38			Standby	Well Shut In	0.75	Stimulation	Stage 4 - Well shut in. Ready for Wireline
12/10/2023 03:38	12/10/2023 03:43			Frac Tree	Well Switch Wireline	0.08	Stimulation	Stage 4 - Switching for Wireline
12/10/2023 03:43	12/10/2023 03:45			Wireline	Equalizing	0.03	Stimulation	Stage 4 - Wireline stabbed on and equalizing pressure
12/10/2023 03:45	12/10/2023 05:30			Wireline	WL Run	1.75	Stimulation	Stage 5 - Wireline operations Stage 5
12/10/2023 05:30	12/10/2023 05:37			Frac Tree	Well Switch Wellhead	0.12	Stimulation	Stage 5 - Shutting in and bleeding off well
12/10/2023 05:37	12/10/2023 06:00			Standby	Well Shut In	0.37	Stimulation	Stage 5 - Well shut in. Ready for Frac
12/10/2023 06:00	12/10/2023 09:27			Standby	Well Shut In	3.46	Stimulation	Stage 5 - Well shut in. Ready for Frac
12/10/2023 09:27	12/10/2023 09:29			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 5 - Switching for Frac
12/10/2023 09:29	12/10/2023 09:49			Frac	Preventive Maintenanc e	0.33	Stimulation	Stage 5 - Frac pump maintenance
12/10/2023 09:49	12/10/2023 09:55			Frac	Equalizing	0.10	Stimulation	Stage 5 - Frac equalizing to well
12/10/2023 09:55	12/10/2023 10:00			Frac	Waiting on Services	0.09	Stimulation	Stage 5 - Frac waiting on PD to spot acid
12/10/2023 10:00	12/10/2023 11:57			Frac	Fracturing	1.95	Stimulation	Stage 5 - Frac operations Stage 5 IWHP: 4,893/ SICP: 5,173 Start Stage: 11/12 FLUID ENDS End Stage: 11/12 FLUID ENDS
12/10/2023 11:57	12/10/2023 12:01			Frac Tree	Well Switch Wellhead	0.06	Stimulation	Stage 5 - Shutting in and bleeding off well
12/10/2023 12:01	12/10/2023 12:03			Standby	Well Shut In	0.04	Stimulation	Stage 5 - Well shut in. Ready for Wireline



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00	Accounting ID 60061.01	

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
12/11/2023 10:18	12/11/2023 12:23			Frac	Fracturing	2.09	Stimulation	Stage 8 - Frac operations Stage 8 IWHP: 4,907/ SICP: 5,222 Start Stage: 10/12 FLUID ENDS End Stage: 8/12 FLUID ENDS
12/11/2023 12:23	12/11/2023 12:29			Frac Tree	Well Switch Wellhead	0.11	Stimulation	Stage 8 - Shutting in and bleeding off well
12/11/2023 12:29	12/11/2023 12:48			Standby	Well Shut In	0.31	Stimulation	Stage 8 - Well shut in. Ready for Wireline
12/11/2023 12:48	12/11/2023 12:49			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 8 - Switching for Wireline
12/11/2023 12:49	12/11/2023 12:51			Wireline	Equalizing	0.04	Stimulation	Stage 8 - Wireline stabbed on and equalizing pressure
12/11/2023 12:51	12/11/2023 14:23			Wireline	WL Run	1.54	Stimulation	Stage 9 - Wireline operations Stage 9
12/11/2023 14:23	12/11/2023 14:28			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 9 - Shutting in and bleeding off well
12/11/2023 14:28	12/11/2023 17:58			Standby	Well Shut In	3.50	Stimulation	Stage 9 - Well shut in. Ready for Frac
12/11/2023 17:58	12/11/2023 18:00			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 9 - Switching for Frac
12/11/2023 18:00	12/11/2023 18:15			Frac	Preventive Maintenance	0.25	Stimulation	Stage 9 - Frac pump maintenance
12/11/2023 18:15	12/11/2023 18:26			Frac	Equalizing	0.19	Stimulation	Stage 9 - Frac equalizing to well
12/11/2023 18:26	12/11/2023 20:23			Frac	Fracturing	1.96	Stimulation	Stage 9 - Frac operations Stage 9 Start Stage: 9/12 IWHP: 4,840/ SICP: 5,240 End Stage: 8/12
12/11/2023 20:23	12/11/2023 20:28			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 9 - Shutting in and bleeding off well
12/11/2023 20:28	12/11/2023 20:39			Standby	Well Shut In	0.19	Stimulation	Stage 9 - Well shut in. Ready for Wireline
12/11/2023 20:39	12/11/2023 20:41			Frac Tree	Well Switch Wireline	0.04	Stimulation	Stage 9 - Switching for Wireline
12/11/2023 20:41	12/11/2023 20:43			Wireline	Equalizing	0.03	Stimulation	Stage 9 - Wireline stabbed on and equalizing pressure
12/11/2023 20:43	12/11/2023 22:05			Wireline	WL Run	1.36	Stimulation	Stage 10 - Wireline operations Stage 10
12/11/2023 22:05	12/11/2023 22:11			Frac Tree	Well Switch Wellhead	0.11	Stimulation	Stage 10 - Shutting in and bleeding off well
12/11/2023 22:11	12/12/2023 02:29			Standby	Well Shut In	4.29	Stimulation	Stage 10 - Well shut in. Ready for Frac
12/12/2023 02:29	12/12/2023 02:31			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 10 - Switching for Frac
12/12/2023 02:31	12/12/2023 02:53			Frac	Preventive Maintenance	0.37	Stimulation	Stage 10 - Frac pump maintenance
12/12/2023 02:53	12/12/2023 02:59			Frac	Equalizing	0.11	Stimulation	Stage 10 - Frac equalizing to well
12/12/2023 02:59	12/12/2023 02:59			Frac	Equalizing	0.00		Stage 10 - Frac equalizing to well. Exceeded 30 min well switch
12/12/2023 02:59	12/12/2023 04:51			Frac	Fracturing	1.86	Stimulation	Stage 10 - Frac operations Stage 10 IWHP: 5,790/ SICP: 5,310 Start Stage: 11/12 FLUID ENDS End Stage: 11/12 FLUID ENDS ISIP: 6081
12/12/2023 04:51	12/12/2023 04:53			Frac Tree	Well Switch Wellhead	0.04	Stimulation	Stage 10 - Shutting in and bleeding off well
12/12/2023 04:53	12/12/2023 04:56			Standby	Well Shut In	0.04	Stimulation	Stage 10 - Well shut in. Ready for Wireline
12/12/2023 04:56	12/12/2023 04:57			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 10 - Switching for Wireline
12/12/2023 04:57	12/12/2023 04:59			Wireline	Equalizing	0.03	Stimulation	Stage 10 - Wireline stabbed on and equalizing pressure
12/12/2023 04:59	12/12/2023 06:00			Wireline	WL Run	1.00	Stimulation	Stage 11 - Wireline operations Stage 11
12/12/2023 06:00	12/12/2023 06:36			Wireline	WL Run	0.61	Stimulation	Stage 11 - Wireline operations Stage 11
12/12/2023 06:36	12/12/2023 06:41			Frac Tree	Well Switch Wellhead	0.09	Stimulation	Stage 11 - Shutting in and bleeding off well
12/12/2023 06:41	12/12/2023 06:55			Standby	Well Shut In	0.23	Stimulation	Stage 11 - Well shut in. Ready for Frac



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00	Accounting ID 60061.01	

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
12/12/2023 06:55	12/12/2023 06:57			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 11 - Switching for Frac
12/12/2023 06:57	12/12/2023 07:25			Frac	Preventive Maintenance	0.47	Stimulation	Stage 11 - Frac pump maintenance
12/12/2023 07:25	12/12/2023 07:38			Frac	Frac Pumps	0.22	Stimulation	Stage 11 - Comms cable pump 4, rigged in 2 A, 6A hole 2
12/12/2023 07:38	12/12/2023 07:52			Frac	Pressure Test	0.23	Stimulation	Stage 11 - Comms cable pump 4, rigged in 2 A, 6A hole 2
12/12/2023 07:52	12/12/2023 09:38			Frac	Fracturing	1.77	Stimulation	Stage 11 - Frac operations Stage 11 IWHP: 4,878/ SICP: 5,313 Start Stage: 12/12 FLUID ENDS End Stage: 12/12 FLUID ENDS
12/12/2023 09:38	12/12/2023 09:44			Frac Tree	Well Switch Wellhead	0.10	Stimulation	Stage 11 - Shutting in and bleeding off well
12/12/2023 09:44	12/12/2023 11:01			Standby	Well Shut In	1.27	Stimulation	Stage 11 - Well shut in. Ready for Wireline
12/12/2023 11:01	12/12/2023 11:02			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 11 - Switching for Wireline
12/12/2023 11:02	12/12/2023 11:04			Wireline	Equalizing	0.05	Stimulation	Stage 11 - Wireline stabbed on and equalizing pressure
12/12/2023 11:04	12/12/2023 12:33			Wireline	WL Run	1.47	Stimulation	Stage 12 - Wireline operations Stage 12
12/12/2023 12:33	12/12/2023 12:38			Frac Tree	Well Switch Wellhead	0.08	Stimulation	Stage 12 - Shutting in and bleeding off well
12/12/2023 12:38	12/13/2023 06:00			Standby	Well Shut In	17.36	Special Services	Stage 12 - Well shut in. Ready for Frac
12/13/2023 06:00	12/14/2023 06:00			Standby	Well Shut In	24.00	Special Services	Stage 12 - Well shut in. Ready for Frac
12/14/2023 06:00	12/15/2023 06:00			Standby	Well Shut In	24.00	Special Services	Stage 12 - Well shut in. Ready for Frac
12/15/2023 06:00	12/16/2023 05:59			Standby	Well Shut In	24.00	Special Services	Stage 12 - Well shut in. Ready for Frac
12/16/2023 06:00	12/17/2023 05:59			Standby	Well Shut In	24.00	Special Services	Stage 12 - Well shut in. Ready for Frac
12/17/2023 06:00	12/18/2023 05:59			Standby	Well Shut In	24.00	Special Services	Stage 12 - Well shut in. Ready for Frac
12/18/2023 06:00	12/18/2023 06:23			Standby	Well Shut In	0.39	Special Services	Stage 12 - Well shut in. Ready for Frac
12/18/2023 06:23	12/18/2023 06:25			Frac Tree	Well Switch Pump Down	0.03	Special Services	Stage 12 - Switching for PD
12/18/2023 06:25	12/18/2023 06:35			Pump Down	Acid Pump Down	0.17	Special Services	Stage 12 - PD spotting acid Stage: 12 acid Open: 06:25 OWP: 3900 Close: 06:35 SICP: 5050 750 gals 15% HCL
12/18/2023 06:35	12/18/2023 06:40			Frac Tree	Well Switch Wellhead	0.07	Special Services	Stage 12 - Shutting in and bleeding off well
12/18/2023 06:40	12/18/2023 06:41			Frac Tree	Well Switch Frac	0.02	Special Services	Stage 12 - Switching for Frac
12/18/2023 06:41	12/18/2023 06:44			Frac	Equalizing	0.07	Special Services	Stage 12 - Frac equalizing to well
12/18/2023 06:44	12/18/2023 08:29			Frac	Fracturing	1.74	Stimulation	Stage 12 - Frac operations Stage 12 IWHP: 4,688/ SICP: 5,555 Start Stage: 11/12 FLUID ENDS End Stage: 11/12 FLUID ENDS
12/18/2023 08:29	12/18/2023 08:31			Frac Tree	Well Switch Wellhead	0.03	Stimulation	Stage 12 - Shutting in and bleeding off well
12/18/2023 08:31	12/18/2023 08:59			Frac	Preventive Maintenance	0.47	Stimulation	Stage 12 - Frac pump maintenance
12/18/2023 08:59	12/18/2023 09:52			Frac	Waiting on Services	0.88	Stimulation	Stage 12 - Frac waiting on PD to spot acid in WILD 51 Waiting on acid to be spotted with PD. They were tied up with a casing test on the wild 54
12/18/2023 09:52	12/18/2023 09:53			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 12 - Switching for Wireline
12/18/2023 09:53	12/18/2023 09:55			Wireline	Equalizing	0.03	Stimulation	Stage 12 - Wireline stabbed on and equalizing pressure - Mon Dec 18 2023 09:56:32 GMT-0700 (Jeremy Ho): Done by WL B -side
12/18/2023 09:55	12/18/2023 11:43			Wireline	WL Run	1.80	Stimulation	Stage 13 - Wireline operations Stage 13 - Mon Dec 18 2023 09:57:17 GMT-0700 (Jeremy Ho): Done by WIL B-side
12/18/2023 11:43	12/18/2023 11:49			Frac Tree	Well Switch Wellhead	0.10	Stimulation	Stage 13 - Shutting in and bleeding off well



Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
12/20/2023 07:14	12/20/2023 07:17			Wireline	Equalizing	0.05	Stimulation	Stage 17 - Wireline stabbed on and equalizing pressure
12/20/2023 07:17	12/20/2023 08:49			Wireline	WL Run	1.53	Stimulation	Stage 18 - Wireline operations Stage 18
12/20/2023 08:49	12/20/2023 08:53			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 18 - Shutting in and bleeding off well
12/20/2023 08:53	12/20/2023 10:14			Standby	Well Shut In	1.34	Stimulation	Stage 18 - Well shut in. Ready for Frac
12/20/2023 10:14	12/20/2023 10:16			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 18 - Switching for Frac
12/20/2023 10:16	12/20/2023 10:44			Frac	Preventive Maintenance	0.47	Stimulation	Stage 18 - Frac pump maintenance
12/20/2023 10:44	12/20/2023 10:53			Frac	Pressure Test	0.16	Stimulation	Stage 18 - ProFrac pump maintenance
12/20/2023 10:53	12/20/2023 12:43			Frac	Fracturing	1.83	Stimulation	Stage 18 - Frac operations Stage 18 IWHP: 4,797/ SICP: 5,181 Start Stage: 11/12 FLUID ENDS End Stage: 11/12 FLUID ENDS ISIP: 5,784
12/20/2023 12:43	12/20/2023 12:47			Frac Tree	Well Switch Wellhead	0.06	Stimulation	Stage 18 - Shutting in and bleeding off well
12/20/2023 12:47	12/20/2023 13:11			Standby	Well Shut In	0.41	Stimulation	Stage 18 - Well shut in. Ready for Wireline
12/20/2023 13:11	12/20/2023 13:12			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 18 - Switching for Wireline
12/20/2023 13:12	12/20/2023 13:14			Wireline	Equalizing	0.03	Stimulation	Stage 18 - Wireline stabbed on and equalizing pressure
12/20/2023 13:14	12/20/2023 14:39			Wireline	WL Run	1.42	Stimulation	Stage 19 - Wireline operations Stage 19
12/20/2023 14:39	12/20/2023 14:44			Frac Tree	Well Switch Wellhead	0.08	Stimulation	Stage 19 - Shutting in and bleeding off well
12/20/2023 14:44	12/20/2023 15:03			Standby	Well Shut In	0.32	Stimulation	Stage 19 - Well shut in. Ready for Frac
12/20/2023 15:03	12/20/2023 15:05			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 19 - Switching for Frac
12/20/2023 15:05	12/20/2023 15:21			Frac	Equalizing	0.26	Stimulation	Stage 19 - Frac pressure testing and equalizing to well
12/20/2023 15:21	12/20/2023 17:10			Frac	Fracturing	1.82	Stimulation	Stage 19 - Frac operations Stage 19 IWHP: 4,862 / SICP: 4509 START 11/12 FLUID ENDS END 11/12 FLUID ENDS
12/20/2023 17:10	12/20/2023 17:14			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 19 - Shutting in and bleeding off well
12/20/2023 17:14	12/20/2023 17:20			Standby	Well Shut In	0.10	Stimulation	Stage 19 - Well shut in. Ready for Wireline
12/20/2023 17:20	12/20/2023 17:21			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 19 - Switching for Wireline
12/20/2023 17:21	12/20/2023 17:24			Wireline	Equalizing	0.04	Stimulation	Stage 19 - Wireline stabbed on and equalizing pressure
12/20/2023 17:24	12/20/2023 18:47			Wireline	WL Run	1.38	Stimulation	Stage 20 - Wireline operations Stage 20
12/20/2023 18:47	12/20/2023 18:50			Frac Tree	Well Switch Wellhead	0.06	Stimulation	Stage 20 - Shutting in and bleeding off well
12/20/2023 18:50	12/20/2023 20:18			Standby	Well Shut In	1.45	Stimulation	Stage 20 - Well shut in. Ready for Frac
12/20/2023 20:18	12/20/2023 20:20			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 20 - Switching for Frac
12/20/2023 20:20	12/20/2023 20:48			Frac	Preventive Maintenance	0.47	Stimulation	Stage 20 - Frac pump maintenance
12/20/2023 20:48	12/20/2023 21:24			Frac	Frac Pumps	0.61	Stimulation	Stage 20 - Frac pump maintenance. Exceeded 30 min well switch working on pump
12/20/2023 21:24	12/20/2023 21:31			Frac	Equalizing	0.11	Stimulation	Stage 20 - Frac equalizing to well. Exceeded 30 min well switch
12/20/2023 21:31	12/20/2023 23:33			Frac	Fracturing	2.04	Stimulation	Stage 20 - Frac operations Stage 20 IWHP: 4700 / SICP: 5548 START 11/12 FLUID ENDS END 11/12 FLUID ENDS
12/20/2023 23:33	12/20/2023 23:38			Frac Tree	Well Switch Wellhead	0.09	Stimulation	Stage 20 - Shutting in and bleeding off well
12/20/2023 23:38	12/20/2023 23:40			Frac Tree	Well Switch Wireline	0.03	Stimulation	Stage 20 - Switching for Wireline



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00		Accounting ID 60061.01

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
12/20/2023 23:40	12/20/2023 23:40			Standby	Well Shut In	0.00		Stage 20 - null
12/20/2023 23:40	12/20/2023 23:42			Wireline	Equalizing	0.04	Stimulation	Stage 20 - Wireline stabbed on and equalizing pressure
12/20/2023 23:42	12/21/2023 01:05			Wireline	WL Run	1.38	Stimulation	Stage 21 - Wireline operations Stage 21
12/21/2023 01:05	12/21/2023 01:09			Frac Tree	Well Switch Wellhead	0.06	Stimulation	Stage 21 - Shutting in and bleeding off well
12/21/2023 01:09	12/21/2023 03:08			Standby	Well Shut In	1.98	Stimulation	Stage 21 - Well shut in. Ready for Frac
12/21/2023 03:08	12/21/2023 03:10			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 21 - Switching for Frac
12/21/2023 03:10	12/21/2023 03:33			Frac	Preventive Maintenance	0.38	Stimulation	Stage 21 - Frac pump maintenance
12/21/2023 03:33	12/21/2023 03:38			Frac	Pressure Test	0.09	Stimulation	Stage 21 - Frac pressure testing and equalizing to well
12/21/2023 03:38	12/21/2023 03:43			Frac	Pressure Test	0.09	Stimulation	Stage 21 - Frac pressure testing and equalizing to well. Exceeded 30 min well switch RU pump
12/21/2023 03:43	12/21/2023 05:25			Frac	Fracturing	1.69	Stimulation	Stage 21 - Frac operations Stage 21 IWHP: 4784 / SICP:4,392 Start Stage: 11/12 FLUID ENDS End Stage: 11/12 FLUID ENDS Frac washed bleeds on remote pad, 94% sand placed. Called stg
12/21/2023 05:25	12/21/2023 05:26			Frac Tree	Well Switch Wellhead	0.02	Stimulation	Stage 21 - Shutting in and bleeding off well
12/21/2023 05:26	12/21/2023 05:59			Pump Down	High Rate Flush	0.56	Stimulation	Stage 21 - PD flushing well OP: 4600
12/21/2023 06:00	12/21/2023 06:09			Pump Down	High Rate Flush	0.15	Stimulation	Stage 21 - PD flushing well CP: 8,300 At 170 bbls pressure spiked. Pumped a total of 215 bbls. Last injection rate 1.9 bpm, 9,600 psi. Line up well to flow back.
12/21/2023 06:09	12/21/2023 06:10			Frac Tree	Well Switch Wellhead	0.02	Stimulation	Stage 21 - Shutting in and bleeding off well
12/21/2023 06:10	12/21/2023 06:47			Standby	Well Shut In	0.63	Stimulation	Stage 21 - Well shut in. Ready for Wireline
12/21/2023 06:47	12/21/2023 08:28			General Operations	Flowback	1.68	Stimulation	Stage 21 - Flowback well OP: 4,800 CP: 3,500 Flowed 440 bbls total
12/21/2023 08:28	12/21/2023 08:45			Frac	Pressure Test	0.28	Stimulation	Stage 21 - Frac pressure testing and equalizing to well. Exceeded 30 min well switch
12/21/2023 08:45	12/21/2023 10:22			Frac	High Rate Flush	1.62	Stimulation	Stage 21 - Frac flushing well. Multiple attempts to flush 62/Blue Pumped wellbore plus 100 rate lined out at 5bpm. Made it twice to 20bpm pressured out 100bbls later each time
12/21/2023 10:22	12/21/2023 10:29			Frac Tree	Well Switch Wellhead	0.11	Stimulation	Stage 21 - Shutting in and bleeding off well
12/21/2023 10:29	12/21/2023 10:54			Standby	Well Shut In	0.41	Stimulation	Stage 21 - Well shut in. Ready for Wireline
12/21/2023 10:54	12/21/2023 14:10			General Operations	Flowback	3.28	Stimulation	Stage 21 - Flowback well
12/21/2023 14:10	12/21/2023 14:37			Frac	High Rate Flush	0.44	Stimulation	Stage 21 - High rate flush Owp 4,944 CP 3,800 Flowed ~ 850 bbls.
12/21/2023 14:37	12/21/2023 14:41			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 21 - Shutting in and bleeding off well
12/21/2023 14:41	12/21/2023 15:15			Standby	Well Shut In	0.56	Stimulation	Stage 21 - Well shut in. Ready for Wireline
12/21/2023 15:15	12/21/2023 15:16			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 21 - Switching for Wireline
12/21/2023 15:16	12/21/2023 15:17			Wireline	Equalizing	0.02	Stimulation	Stage 21 - Wireline stabbed on and equalizing pressure
12/21/2023 15:17	12/21/2023 16:45			Wireline	WL Run	1.45	Stimulation	Stage 22 - Wireline operations Stage 22
12/21/2023 16:45	12/21/2023 16:49			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 22 - Shutting in and bleeding off well
12/21/2023 16:49	12/21/2023 19:29			Standby	Well Shut In	2.66	Stimulation	Stage 22 - Well shut in. Ready for Frac
12/21/2023 19:29	12/21/2023 19:31			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 22 - Switching for Frac
12/21/2023 19:31	12/21/2023 19:56			Frac	Preventive Maintenance	0.41	Stimulation	Stage 22 - Frac pump maintenance
12/21/2023 19:56	12/21/2023 19:59			Frac	Equalizing	0.06	Stimulation	Stage 22 - Frac equalizing to well



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00	Accounting ID 60061.01	

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
12/21/2023 19:59	12/21/2023 21:50			Frac	Fracturing	1.84	Stimulation	Stage 22 - Frac operations Stage 22 IWHP: 4560 / SICP: 5036 START 12/12 FLUID ENDS END 12/12 FLUID ENDS
12/21/2023 21:50	12/21/2023 21:56			Frac Tree	Well Switch Wellhead	0.11	Stimulation	Stage 22 - Shutting in and bleeding off well
12/21/2023 21:56	12/21/2023 21:58			Frac Tree	Well Switch Wireline	0.03	Stimulation	Stage 22 - Switching for Wireline
12/21/2023 21:58	12/21/2023 22:01			Wireline	Equalizing	0.06	Stimulation	Stage 22 - Wireline stabbed on and equalizing pressure
12/21/2023 22:01	12/21/2023 23:19			Wireline	WL Run	1.30	Stimulation	Stage 23 - Wireline operations Stage 23
12/21/2023 23:19	12/21/2023 23:23			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 23 - Shutting in and bleeding off well
12/21/2023 23:23	12/22/2023 00:05			Standby	Well Shut In	0.69	Stimulation	Stage 23 - Well shut in. Ready for Frac
12/22/2023 00:05	12/22/2023 00:07			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 23 - Switching for Frac
12/22/2023 00:07	12/22/2023 00:34			Frac	Preventive Maintenance	0.45	Stimulation	Stage 23 - Frac pump maintenance
12/22/2023 00:34	12/22/2023 00:35			Frac	Equalizing	0.02	Stimulation	Stage 23 - Frac equalizing to well
12/22/2023 00:35	12/22/2023 00:37			Frac	Equalizing	0.03	Stimulation	Stage 23 - Frac equalizing to well. Exceeded 30 min well switch blender sensor
12/22/2023 00:37	12/22/2023 02:40			Frac	Fracturing	2.05	Stimulation	Stage 23 - Frac operations Stage 23 IWHP: 5000 / SICP: 5347 START 12/12 FLUID ENDS END 12/12 FLUID ENDS
12/22/2023 02:40	12/22/2023 02:45			Frac Tree	Well Switch Wellhead	0.08	Stimulation	Stage 23 - Shutting in and bleeding off well
12/22/2023 02:45	12/22/2023 02:45			Standby	Well Shut In	0.00		Stage 23 - null
12/22/2023 02:45	12/22/2023 02:47			Frac Tree	Well Switch Wireline	0.04	Stimulation	Stage 23 - Switching for Wireline
12/22/2023 02:47	12/22/2023 02:50			Wireline	Equalizing	0.05	Stimulation	Stage 23 - Wireline stabbed on and equalizing pressure
12/22/2023 02:50	12/22/2023 04:06			Wireline	WL Run	1.27	Stimulation	Stage 24 - Wireline operations Stage 24
12/22/2023 04:06	12/22/2023 04:09			Frac Tree	Well Switch Wellhead	0.05	Stimulation	Stage 24 - Shutting in and bleeding off well
12/22/2023 04:09	12/22/2023 04:52			Standby	Well Shut In	0.72	Stimulation	Stage 24 - Well shut in. Ready for Frac
12/22/2023 04:52	12/22/2023 04:54			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 24 - Switching for Frac
12/22/2023 04:54	12/22/2023 05:22			Frac	Preventive Maintenance	0.47	Stimulation	Stage 24 - Frac pump maintenance
12/22/2023 05:22	12/22/2023 05:37			Frac	Frac Pumps	0.25	Stimulation	Stage 24 - ProFrac pump 5A greaser
12/22/2023 05:37	12/22/2023 05:40			Frac	Equalizing	0.05	Stimulation	Stage 24 - Frac equalizing to well. Exceeded 30 min well switch
12/22/2023 05:40	12/22/2023 06:00			Frac	Fracturing	0.32	Stimulation	Stage 24 - Frac operations Stage 24 IWHP: 4,677 Start Stage: 12/12 FLUID ENDS
12/22/2023 06:00	12/22/2023 07:31			Frac	Fracturing	1.53	Stimulation	Stage 24 - Frac operations Stage 24 IWHP: 4,677 / SICP: 5,384 Start Stage: 12/12 FLUID ENDS End Stage: 11/12 FLUID ENDS
12/22/2023 07:31	12/22/2023 07:40			Frac Tree	Well Switch Wellhead	0.14	Stimulation	Stage 24 - Shutting in and bleeding off well
12/22/2023 07:40	12/22/2023 07:47			Standby	Well Shut In	0.11	Stimulation	Stage 24 - Well shut in. Ready for Wireline
12/22/2023 07:47	12/22/2023 07:48			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 24 - Switching for Wireline
12/22/2023 07:48	12/22/2023 07:49			Wireline	Equalizing	0.03	Stimulation	Stage 24 - Wireline stabbed on and equalizing pressure
12/22/2023 07:49	12/22/2023 08:58			Wireline	WL Run	1.15	Stimulation	Stage 25 - Wireline operations Stage 25
12/22/2023 08:58	12/22/2023 09:04			Frac Tree	Well Switch Wellhead	0.10	Stimulation	Stage 25 - Shutting in and bleeding off well
12/22/2023 09:04	12/22/2023 10:13			Standby	Well Shut In	1.15	Stimulation	Stage 25 - Well shut in. Ready for Frac
12/22/2023 10:13	12/22/2023 10:15			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 25 - Switching for Frac

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00	Accounting ID 60061.01	

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
12/24/2023 09:31	12/24/2023 09:32			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 29 - Switching for Wireline
12/24/2023 09:32	12/24/2023 09:34			Wireline	Equalizing	0.04	Stimulation	Stage 29 - Wireline stabbed on and equalizing pressure
12/24/2023 09:34	12/24/2023 10:47			Wireline	WL Run	1.22	Stimulation	Stage 30 - Wireline operations Stage 30
12/24/2023 10:47	12/24/2023 10:54			Frac Tree	Well Switch Wellhead	0.12	Stimulation	Stage 30 - Shutting in and bleeding off well
12/24/2023 10:54	12/24/2023 14:20			Standby	Well Shut In	3.43	Stimulation	Stage 30 - Well shut in. Ready for Frac
12/24/2023 14:20	12/24/2023 14:22			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 30 - Switching for Frac
12/24/2023 14:22	12/24/2023 14:50			Frac	Preventive Maintenance	0.47	Stimulation	Stage 30 - Frac pump maintenance
12/24/2023 14:50	12/24/2023 14:56			Frac	Pressure Test	0.11	Stimulation	Stage 30 - Frac pressure testing and equalizing to well. Exceeded 30 min well switch
12/24/2023 14:56	12/24/2023 16:16			Frac	Fracturing	1.32	Stimulation	Stage 30 - Frac operations Stage 30
12/24/2023 16:16	12/24/2023 19:48			Frac	Frac Iron	3.54	Stimulation	Stage 30 - Leak in the Mono line. Leak on monoline 2" line, blender suction and breakers
12/24/2023 19:48	12/24/2023 19:52			Frac	Equalizing	0.06	Stimulation	Stage 30 - Frac equalizing to well
12/24/2023 19:52	12/24/2023 19:53			Frac	Fracturing	0.02	Stimulation	Stage 30 - Frac operations Stage 30 Resume.
12/24/2023 19:53	12/24/2023 21:10			Frac	Blender	1.29	Stimulation	Stage 30 - Frac working on blender.
12/24/2023 21:10	12/24/2023 23:18			Frac	Fracturing	2.12	Stimulation	Stage 30 - Frac operations Stage 30 Resume IWHP: 4,820 / SICP: 6389 START 11/12 FLUID ENDS END 11/12 FLUID ENDS
12/24/2023 23:18	12/24/2023 23:23			Frac Tree	Well Switch Wellhead	0.08	Stimulation	Stage 30 - Shutting in and bleeding off well
12/24/2023 23:23	12/24/2023 23:36			Standby	Well Shut In	0.23	Stimulation	Stage 30 - Well shut in. Ready for Wireline
12/24/2023 23:36	12/24/2023 23:38			Frac Tree	Well Switch Wireline	0.03	Stimulation	Stage 30 - Switching for Wireline
12/24/2023 23:38	12/24/2023 23:40			Wireline	Equalizing	0.04	Stimulation	Stage 30 - Wireline stabbed on and equalizing pressure
12/24/2023 23:40	12/25/2023 00:56			Wireline	WL Run	1.25	Stimulation	Stage 31 - Wireline operations Stage 31
12/25/2023 00:56	12/25/2023 01:19			Frac Tree	Well Switch Wellhead	0.39	Stimulation	Stage 31 - Shutting in and bleeding off well
12/25/2023 01:19	12/25/2023 04:42			Standby	Well Shut In	3.39	Stimulation	Stage 31 - Well shut in. Ready for Frac
12/25/2023 04:42	12/25/2023 04:44			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 31 - Switching for Frac
12/25/2023 04:44	12/25/2023 05:12			Frac	Preventive Maintenance	0.47	Stimulation	Stage 31 - Frac pump maintenance
12/25/2023 05:12	12/25/2023 05:18			Frac	Frac Pumps	0.10	Stimulation	Stage 31 - Frac pump maintenance. Exceeded 30 min well switch Profrac- pump packing/ clear codes on blender
12/25/2023 05:18	12/25/2023 05:23			Frac	Pressure Test	0.08	Stimulation	Stage 31 - Frac pressure testing and equalizing to well. Exceeded 30 min well switch
12/25/2023 05:23	12/25/2023 06:00			Frac	Fracturing	0.61	Stimulation	Stage 31 - Frac operations Stage 31
12/25/2023 06:00	12/25/2023 07:46			Frac	Fracturing	1.78	Stimulation	Stage 31 - Frac operations Stage 31 Start Stage: 11/12 IWHP: 5,059 / SICP: 5,413 End Stage: 11/12 Rapid pressure increase with 1.75# on bottom/2# in wellbore. Forced rate drop down to 20bpm while attempting to flush well. 23bpm max rate after flushing wellbore.
12/25/2023 07:46	12/25/2023 07:50			Frac Tree	Well Switch Wellhead	0.06	Stimulation	Stage 31 - Shutting in and bleeding off well
12/25/2023 07:50	12/25/2023 08:20			Standby	Well Shut In	0.50	Stimulation	Stage 31 - Well shut in. Ready for Wireline
12/25/2023 08:20	12/25/2023 08:21			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 31 - Switching for Wireline
12/25/2023 08:21	12/25/2023 08:23			Wireline	Equalizing	0.04	Stimulation	Stage 31 - Wireline stabbed on and equalizing pressure
12/25/2023 08:23	12/25/2023 09:34			Wireline	WL Run	1.19	Stimulation	Stage 32 - Wireline operations Stage 32



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00	Accounting ID 60061.01	

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
12/25/2023 09:34	12/25/2023 09:39			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 32 - Shutting in and bleeding off well
12/25/2023 09:39	12/25/2023 12:41			Standby	Well Shut In	3.04	Stimulation	Stage 32 - Well shut in. Ready for Frac
12/25/2023 12:41	12/25/2023 12:43			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 32 - Switching for Frac
12/25/2023 12:43	12/25/2023 12:59			Frac	Preventive Maintenance	0.26	Stimulation	Stage 32 - Frac pump maintenance
12/25/2023 12:59	12/25/2023 13:03			Frac	Equalizing	0.08	Stimulation	Stage 32 - Frac equalizing to well
12/25/2023 13:03	12/25/2023 14:55			Frac	Fracturing	1.87	Stimulation	Stage 32 - Frac operations Stage 32 Start Stage: 11/12 IWHP: 4,872 / SICP:5,314 End Stage: 11/12
12/25/2023 14:55	12/25/2023 14:59			Frac Tree	Well Switch Wellhead	0.06	Stimulation	Stage 32 - Shutting in and bleeding off well
12/25/2023 14:59	12/25/2023 15:03			Standby	Well Shut In	0.06	Stimulation	Stage 32 - Well shut in. Ready for Wireline
12/25/2023 15:03	12/25/2023 15:04			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 32 - Switching for Wireline
12/25/2023 15:04	12/25/2023 15:06			Wireline	Equalizing	0.04	Stimulation	Stage 32 - Wireline stabbed on and equalizing pressure
12/25/2023 15:06	12/25/2023 16:37			Wireline	WL Run	1.52	Stimulation	Stage 33 - Wireline operations Stage 33
12/25/2023 16:37	12/25/2023 16:48			Frac Tree	Well Switch Wellhead	0.18	Stimulation	Stage 33 - Shutting in and bleeding off well
12/25/2023 16:48	12/25/2023 21:01			Standby	Well Shut In	4.22	Stimulation	Stage 33 - Well shut in. Ready for Wireline
12/25/2023 21:01	12/25/2023 21:03			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 33 - Switching for Frac
12/25/2023 21:03	12/25/2023 21:14			Frac	Preventive Maintenance	0.18	Stimulation	Stage 33 - Frac pump maintenance
12/25/2023 21:14	12/25/2023 21:14			Frac	Priming Pumps	0.00		Stage 33 - null
12/25/2023 21:14	12/25/2023 21:16			Frac	Equalizing	0.05	Stimulation	Stage 33 - Frac equalizing to well
12/25/2023 21:16	12/25/2023 22:09			Frac	Fracturing	0.88	Stimulation	Stage 33 - Frac operations Stage 33
12/25/2023 22:09	12/25/2023 22:11			Frac	Blender	0.03	Stimulation	Stage 33 - Frac issues with blender Blender suction issues thru out frac
12/25/2023 22:11	12/25/2023 23:36			Frac	Fracturing	1.42	Stimulation	Stage 33 - Frac operations Stage 33 Resume. IWHP: 4850 / SICP: 5567 START 11/12 FLUID ENDS END 11/12 FLUID ENDS
12/25/2023 23:36	12/25/2023 23:40			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 33 - Shutting in and bleeding off well
12/25/2023 23:40	12/25/2023 23:47			Standby	Well Shut In	0.11	Stimulation	Stage 33 - Well shut in. Ready for Wireline
12/25/2023 23:47	12/25/2023 23:48			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 33 - Switching for Wireline
12/25/2023 23:48	12/25/2023 23:51			Wireline	Equalizing	0.04	Stimulation	Stage 33 - Wireline stabbed on and equalizing pressure
12/26/2023 01:00	12/26/2023 01:04			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 34 - Shutting in and bleeding off well
12/26/2023 01:04	12/26/2023 04:59			Standby	Well Shut In	3.93	Stimulation	Stage 34 - Well shut in. Ready for Frac
12/26/2023 04:59	12/26/2023 05:01			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 34 - Switching for Frac
12/26/2023 05:01	12/26/2023 05:25			Frac	Preventive Maintenance	0.39	Stimulation	Stage 34 - Frac pump maintenance
12/26/2023 05:25	12/26/2023 05:29			Frac	Pressure Test	0.07	Stimulation	Stage 34 - Frac pressure testing and equalizing to well
12/26/2023 05:29	12/26/2023 05:33			Frac	Pressure Test	0.06	Stimulation	Stage 34 - Exceeded 30 min well switch
12/26/2023 05:33	12/26/2023 05:59			Frac	Fracturing	0.45	Stimulation	Stage 34 - Frac operations Stage 34

[illegible]



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00	Accounting ID 60061.01	

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
1/1/2024 20:49	1/1/2024 21:17			Frac	Preventive Maintenanc e	0.47	Stimulation	Stage 52 - Frac pump maintenance
1/1/2024 21:17	1/1/2024 21:19			Frac	Frac Pumps	0.04	Stimulation	Stage 52 - Frac pump maintenance. Exceeded 30 min well switch Pro Frac - Pump Maintenance
1/1/2024 21:19	1/1/2024 21:28			Frac	Pressure Test	0.14	Stimulation	Stage 52 - Frac pressure testing and equalizing to well. Exceeded 30 min well switch
1/1/2024 21:28	1/1/2024 23:22			Frac	Fracturing	1.90	Stimulation	Stage 52 - Frac operations Stage 52 IWHP: 4,518 / SICP: 5,457 START 11/12 FLUID ENDS END 8/12 FLUID ENDS
1/1/2024 23:22	1/1/2024 23:26			Frac Tree	Well Switch Wellhead	0.08	Stimulation	Stage 52 - Shutting in and bleeding off well
1/1/2024 23:26	1/1/2024 23:28			Standby	Well Shut In	0.03	Stimulation	Stage 52 - Well shut in. Ready for Wireline
1/1/2024 23:28	1/1/2024 23:29			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 52 - Switching for Wireline
1/1/2024 23:29	1/1/2024 23:32			Wireline	Equalizing	0.04	Stimulation	Stage 52 - Wireline stabbed on and equalizing pressure
1/1/2024 23:32	1/2/2024 00:35			Wireline	WL Run	1.05	Stimulation	Stage 53 - Wireline operations Stage 53
1/2/2024 00:35	1/2/2024 00:39			Frac Tree	Well Switch Wellhead	0.08	Stimulation	Stage 53 - Shutting in and bleeding off well
1/2/2024 00:39	1/2/2024 05:03			Standby	Well Shut In	4.40	Stimulation	Stage 53 - Well shut in. Ready for Frac
1/2/2024 05:03	1/2/2024 05:05			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 53 - Switching for Frac
1/2/2024 05:05	1/2/2024 05:33			Frac	Preventive Maintenanc e	0.47	Stimulation	Stage 53 - Frac pump maintenance
1/2/2024 05:33	1/2/2024 05:53			Frac	Frac Pumps	0.32	Stimulation	Stage 53 - Frac pump maintenance. Exceeded 30 min well switch Working on greasers, Pump maintenanc
1/2/2024 05:53	1/2/2024 05:59			Frac	Pressure Test	0.12	Stimulation	Stage 53 - Frac pressure testing and equalizing to well. Exceeded 30 min well switch Working on greasers, Pump maintenanc
1/2/2024 06:00	1/2/2024 07:36			Frac	Fracturing	1.61	Stimulation	Stage 53 - Frac operations Stage 53 Start Stage: 10/12 IWHP: 4,675/ SICP: 5,025 End Stage: 10/12
1/2/2024 07:36	1/2/2024 07:40			Frac Tree	Well Switch Wellhead	0.06	Stimulation	Stage 53 - Shutting in and bleeding off well
1/2/2024 07:40	1/2/2024 07:41			Standby	Well Shut In	0.02	Stimulation	Stage 53 - Well shut in. Ready for Wireline
1/2/2024 07:41	1/2/2024 07:42			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 53 - Switching for Wireline
1/2/2024 07:42	1/2/2024 07:44			Wireline	Equalizing	0.03	Stimulation	Stage 53 - Wireline stabbed on and equalizing pressure
1/2/2024 07:44	1/2/2024 08:59			Wireline	WL Run	1.25	Stimulation	Stage 54 - Wireline operations Stage 54
1/2/2024 08:59	1/2/2024 09:02			Frac Tree	Well Switch Wellhead	0.05	Stimulation	Stage 54 - Shutting in and bleeding off well
1/2/2024 09:02	1/2/2024 12:08			Standby	Well Shut In	3.09	Stimulation	Stage 54 - Well shut in. Ready for Frac
1/2/2024 12:08	1/2/2024 12:10			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 54 - Switching for Frac
1/2/2024 12:10	1/2/2024 12:30			Frac	Preventive Maintenanc e	0.33	Stimulation	Stage 54 - Frac pump maintenance
1/2/2024 12:30	1/2/2024 12:38			Frac	Equalizing	0.13	Stimulation	Stage 54 - Frac equalizing to well
1/2/2024 12:38	1/2/2024 14:17			Frac	Fracturing	1.65	Stimulation	Stage 54 - Frac operations Stage 54 Start Stage: 11/12 IWHP: 4633 / SICP: 5084 End Stage: 11/12
1/2/2024 14:17	1/2/2024 14:20			Frac Tree	Well Switch Wellhead	0.05	Stimulation	Stage 54 - Shutting in and bleeding off well
1/2/2024 14:20	1/2/2024 14:28			Standby	Well Shut In	0.14	Stimulation	Stage 54 - Well shut in. Ready for Wireline
1/2/2024 14:28	1/2/2024 14:29			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 54 - Switching for Wireline
1/2/2024 14:29	1/2/2024 14:31			Wireline	Equalizing	0.03	Stimulation	Stage 54 - Wireline stabbed on and equalizing pressure



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00		Accounting ID 60061.01

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
1/4/2024 20:49	1/4/2024 20:51			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 60 - Switching for Frac
1/4/2024 20:51	1/4/2024 20:59			Frac	Preventive Maintenance	0.13	Stimulation	Stage 60 - Frac pump maintenance
1/4/2024 20:59	1/4/2024 21:02			Frac	Equalizing	0.05	Stimulation	Stage 60 - Frac equalizing to well
1/4/2024 21:02	1/4/2024 22:40			Frac	Fracturing	1.64	Stimulation	Stage 60 - Frac operations Stage 60 IWHP: 4,412/ SICP: 5,375 Start Stage: 11/12 FLUID ENDS End Stage: 11/12 FLUID ENDS ISIP: 5,874
1/4/2024 22:40	1/4/2024 22:44			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 60 - Shutting in and bleeding off well
1/4/2024 22:44	1/4/2024 22:49			Standby	Well Shut In	0.08	Stimulation	Stage 60 - Well shut in. Ready for Wireline
1/4/2024 22:49	1/4/2024 22:51			Frac Tree	Well Switch Wireline	0.03	Stimulation	Stage 60 - Switching for Wireline
1/4/2024 22:51	1/4/2024 22:54			Wireline	Equalizing	0.05	Stimulation	Stage 60 - Wireline stabbed on and equalizing pressure
1/4/2024 22:54	1/4/2024 23:53			Wireline	WL Run	0.99	Stimulation	Stage 61 - Wireline operations Stage 61
1/4/2024 23:53	1/4/2024 23:56			Frac Tree	Well Switch Wellhead	0.05	Stimulation	Stage 61 - Shutting in and bleeding off well
1/4/2024 23:56	1/5/2024 03:18			Standby	Well Shut In	3.37	Stimulation	Stage 61 - Well shut in. Ready for Frac
1/5/2024 03:18	1/5/2024 05:19			Frac	Frac Pumps	2.02	Stimulation	Stage 61 - BALANCE BLOCK: A side to frac Tan well. - Fri Jan 05 2024 03:25:08 GMT-0700 (Jeremy Ho): A side to frac Tan well.
1/5/2024 05:19	1/5/2024 06:00			Standby	Well Shut In	0.67	Stimulation	Stage 61 - Well shut in. Ready for Frac
1/5/2024 06:00	1/5/2024 10:17			Standby	Well Shut In	4.30	Stimulation	Stage 61 - Well shut in. Ready for Frac
1/5/2024 10:17	1/5/2024 10:19			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 61 - Switching for Frac
1/5/2024 10:19	1/5/2024 10:47			Frac	Preventive Maintenance	0.47	Stimulation	Stage 61 - Frac pump maintenance
1/5/2024 10:47	1/5/2024 10:56			Frac	Equalizing	0.14	Stimulation	Stage 61 - Profrac pump maint
1/5/2024 10:56	1/5/2024 12:43			Frac	Fracturing	1.79	Stimulation	Stage 61 - Frac operations Stage 61 IWHP: 4,460/ SICP: 5,510 Start Stage: 11/12 FLUID ENDS End Stage: 10/12 FLUID ENDS
1/5/2024 12:43	1/5/2024 12:47			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 61 - Shutting in and bleeding off well
1/5/2024 12:47	1/5/2024 12:49			Standby	Well Shut In	0.03	Stimulation	Stage 61 - Well shut in. Ready for Wireline
1/5/2024 12:49	1/5/2024 12:50			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 61 - Switching for Wireline
1/5/2024 12:50	1/5/2024 12:53			Wireline	Equalizing	0.04	Stimulation	Stage 61 - Wireline stabbed on and equalizing pressure
1/5/2024 12:53	1/5/2024 13:47			Wireline	WL Run	0.90	Stimulation	Stage 62 - Wireline operations Stage 62
1/5/2024 13:47	1/5/2024 13:51			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 62 - Shutting in and bleeding off well
1/5/2024 13:51	1/5/2024 17:39			Standby	Well Shut In	3.81	Stimulation	Stage 62 - Well shut in. Ready for Frac
1/5/2024 17:39	1/5/2024 20:03			Frac	Frac Pumps	2.40	Stimulation	Stage 62 - Balanced Block A side to Frac TAN well.
1/5/2024 20:03	1/6/2024 00:24			Standby	Well Shut In	4.34	Stimulation	Stage 62 - Well shut in. Ready for Frac
1/6/2024 00:24	1/6/2024 00:26			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 62 - Switching for Frac
1/6/2024 00:26	1/6/2024 00:30			Frac	Preventive Maintenance	0.06	Stimulation	Stage 62 - Frac pump maintenance
1/6/2024 00:30	1/6/2024 00:34			Frac	Equalizing	0.07	Stimulation	Stage 62 - Frac equalizing to well
1/6/2024 00:34	1/6/2024 02:10			Frac	Fracturing	1.61	Stimulation	Stage 62 - Frac operations Stage 62 IWHP: 4,374/ SICP: 5,102 Start Stage: 11/12 FLUID ENDS End Stage: 11/12 FLUID ENDS
1/6/2024 02:10	1/6/2024 02:14			Frac Tree	Well Switch Wellhead	0.06	Stimulation	Stage 62 - Shutting in and bleeding off well
1/6/2024 02:14	1/6/2024 02:23			Standby	Well Shut In	0.16	Stimulation	Stage 62 - Well shut in. Ready for Wireline



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00		Accounting ID 60061.01

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
1/7/2024 07:55	1/7/2024 07:57			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 65 - Switching for Frac
1/7/2024 07:57	1/7/2024 08:12			Frac	Preventive Maintenance	0.26	Stimulation	Stage 65 - Frac pump maintenance
1/7/2024 08:12	1/7/2024 08:25			Frac	Equalizing	0.21	Stimulation	Stage 65 - Frac pressure testing and equalizing to well
1/7/2024 08:25	1/7/2024 08:32			Frac	Equalizing	0.12	Stimulation	Stage 65 - Frac pressure testing and equalizing to well. Exceeded 30 min well switch
1/7/2024 08:32	1/7/2024 10:52			Frac	Fracturing	2.34	Stimulation	Stage 65 - Frac operations Stage 65 Start Stage: 10/12 IWHP: 4,590/ SICP: 6,260 End Stage: 10/12 ISIP: 6,150
1/7/2024 10:52	1/7/2024 10:57			Frac Tree	Well Switch Wellhead	0.08	Stimulation	Stage 65 - Shutting in and bleeding off well
1/7/2024 10:57	1/7/2024 11:00			Standby	Well Shut In	0.05	Stimulation	Stage 65 - Well shut in. Ready for Wireline
1/7/2024 11:00	1/7/2024 11:01			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 65 - Switching for Wireline
1/7/2024 11:01	1/7/2024 11:03			Wireline	Equalizing	0.04	Stimulation	Stage 65 - Wireline stabbed on and equalizing pressure
1/7/2024 11:03	1/7/2024 12:26			Wireline	WL Run	1.38	Stimulation	Stage 66 - Wireline operations Stage 66
1/7/2024 12:26	1/7/2024 12:30			Frac Tree	Well Switch Wellhead	0.07	Stimulation	Stage 66 - Shutting in and bleeding off well
1/7/2024 12:30	1/7/2024 15:27			Standby	Well Shut In	2.95	Stimulation	Stage 66 - Well shut in. Ready for Frac
1/7/2024 15:27	1/7/2024 15:29			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 66 - Switching for Frac
1/7/2024 15:29	1/7/2024 15:47			Frac	Preventive Maintenance	0.30	Stimulation	Stage 66 - Frac pump maintenance
1/7/2024 15:47	1/7/2024 15:57			Frac	Pressure Test	0.17	Stimulation	Stage 66 - Frac pressure testing and equalizing to well
1/7/2024 15:57	1/7/2024 16:04			Frac	Pressure Test	0.12	Stimulation	Stage 66 - Profrac welding on missile
1/7/2024 16:04	1/7/2024 18:00			Frac	Fracturing	1.93	Stimulation	Stage 66 - Frac operations Stage 66 IWHP: 4,950/ SICP: 5,258 Start Stage: 12/12 FLUID ENDS End Stage: 12/12 FLUID ENDS
1/7/2024 18:00	1/7/2024 18:02			Frac Tree	Well Switch Wellhead	0.04	Stimulation	Stage 66 - Shutting in and bleeding off well
1/7/2024 18:02	1/7/2024 18:03			Standby	Well Shut In	0.02	Stimulation	Stage 66 - Well shut in. Ready for Wireline
1/7/2024 18:03	1/7/2024 18:04			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 66 - Switching for Wireline
1/7/2024 18:04	1/7/2024 18:07			Wireline	Equalizing	0.04	Stimulation	Stage 66 - Wireline stabbed on and equalizing pressure
1/7/2024 18:07	1/7/2024 19:07			Wireline	WL Run	1.00	Stimulation	Stage 67 - Wireline operations Stage 67
1/7/2024 19:07	1/7/2024 19:13			Frac Tree	Well Switch Wellhead	0.10	Stimulation	Stage 67 - Shutting in and bleeding off well
1/7/2024 19:13	1/7/2024 22:37			Standby	Well Shut In	3.39	Stimulation	Stage 67 - Well shut in. Ready for Frac
1/7/2024 22:37	1/7/2024 22:39			Frac Tree	Well Switch Frac	0.03	Stimulation	Stage 67 - Switching for Frac
1/7/2024 22:39	1/7/2024 22:43			Frac	Equalizing	0.08	Stimulation	Stage 67 - Frac equalizing to well
1/7/2024 22:43	1/8/2024 00:22			Frac	Fracturing	1.64	Stimulation	Stage 67 - Frac operations Stage 67 IWHP: 4,375/ SICP: 5,600 Start Stage: 11/12 FLUID ENDS End Stage: 11/12 FLUID ENDS
1/8/2024 00:22	1/8/2024 00:25			Frac Tree	Well Switch Wellhead	0.06	Stimulation	Stage 67 - Shutting in and bleeding off well
1/8/2024 00:25	1/8/2024 00:46			Standby	Well Shut In	0.35	Stimulation	Stage 67 - Well shut in. Ready for Wireline
1/8/2024 00:46	1/8/2024 00:47			Frac Tree	Well Switch Wireline	0.02	Stimulation	Stage 67 - Switching for Wireline
1/8/2024 00:47	1/8/2024 00:50			Wireline	Equalizing	0.04	Stimulation	Stage 67 - Wireline stabbed on and equalizing pressure
1/8/2024 00:50	1/8/2024 01:38			Wireline	WL Run	0.80	Stimulation	Stage 68 - Wireline operations Stage 68
1/8/2024 01:38	1/8/2024 01:47			Frac Tree	Well Switch Wellhead	0.15	Stimulation	Stage 68 - Shutting in and bleeding off well



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00		Accounting ID 60061.01

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
2/13/2024 04:30	2/13/2024 06:00			Coil Tubing	Milling	1.50	Drill Out	DRILL PLUGS 21 - 30 OF 72 AVG. DT - 0 MIN. AVG. PT - 6 MIN AVG. CIRC - 6,267 PSI AVG. WHP - 3,258 PSI AVG RATE- 4.2/4.0 IN/OUT AVG SAND CONC - 6% SEND 10/10/10 BBL FW SWEEP AFTER PLUG 25 SEND 10/10/10 BBL FW SWEEP AFTER PLUG 30
2/13/2024 06:00	2/13/2024 07:00			Coil Tubing	Milling	1.00	Drill Out	DRILL PLUGS 31 - 40 OF 72 AVG. DT - 0 MIN. AVG. PT - 8.1 MIN AVG. CIRC - 6,298 PSI AVG. WHP - 3,270 PSI AVG RATE- 4.6/4.5 IN/OUT AVG SAND CONC - 5% SEND 10/10/10 BBL FW SWEEP AFTER PLUG 35 SEND 10/10/10 BBL FW SWEEP AFTER PLUG 40
2/13/2024 07:00	2/13/2024 09:30			Coil Tubing	Milling	2.50	Drill Out	DRILL PLUGS 41 - 50 OF 72 AVG. DT - 0 MIN. AVG. PT - 15.2 MIN AVG. CIRC - 6,530 PSI AVG. WHP - 3,501 PSI AVG RATE- 4.6/4.5 IN/OUT AVG SAND CONC - 6% SEND 10/10/10 BBL FW SWEEP AFTER PLUG 45 SEND 10/10/10 BBL FW SWEEP AFTER PLUG 50
2/13/2024 09:30	2/13/2024 13:45			Coil Tubing	Milling	4.25	Drill Out	DRILL PLUGS 51 - 60 OF 72 AVG. DT - 0 MIN. AVG. PT - 25.0 MIN AVG. CIRC - 6,188 PSI AVG. WHP - 3,637 PSI AVG RATE- 4.2/4.0 IN/OUT AVG SAND CONC - 3% SEND 10/10/10 BBL FW SWEEP AFTER PLUG 55 SEND 10/10/10 BBL FW SWEEP AFTER PLUG 60
2/13/2024 13:45	2/13/2024 23:45			Coil Tubing	Milling	10.00	Drill Out	DRILL PLUGS 61 - 72 OF 72 AVG. DT - 0 MIN. AVG. PT - 44.8 MIN AVG. CIRC - 6,380 PSI AVG. WHP - 3,665 PSI AVG RATE- 4.2/4.0 IN/OUT AVG SAND CONC - 3% WASH TO TD @20,350' SEND 10 BBL FW SWEEP AFTER PLUG 65 SEND 10/10/10 BBL FW SWEEP, 90 BBL SPACER, FOLOWED BY SECOND 10/10/10 BBL SWEEP AFTER PLUG 72. ALLOW SWEEPS TO EXIT TUBING AND CIRCULATE UP HOLE 1,000'. PREPARE TO POOH.
2/13/2024 23:45	2/14/2024 06:00			Coil Tubing	Pull out of hole	6.25	Drill Out	POOH FROM TD @ 20,350' CHASING SWEEPS. PUMP 10/10/10 BBL FW SWEEP AT HALF LATERAL (16,000') AND 90 (11,000). PU WHT- 58k
2/14/2024 06:00	2/14/2024 08:45			Coil Tubing	Pull out of hole	2.75	Drill Out	CONTINUE POOH CHASING SWEEPS FROM 12,000'.
2/14/2024 08:45	2/14/2024 09:30			General Ops	Rigging Out	0.75	Drill Out	LD BHA, SLIP COIL RDMO TO WILD 74
2/14/2024 09:30	2/15/2024 06:00			Standby	Well Shut In	20.50		LD BHA. RDMO TO WILD 74
2/21/2024 06:00	2/21/2024 13:00			Standby	Well Shut In	7.00		WSI FOR PRODUCTION TREE INSTALL

--



Time & Activity Summary_WV10

Well Name Wild 62-3328-22F	Lease Multiple Leases	Government Authority BLM/UTERO	API/UWI 43013543080000	Pad Name Sprouse Pad
Original KB Elevation (ft) 5,409.00	Ground Elevation (ft) 5,379.00	KB-Ground Distance (ft) 30.00		Accounting ID 60061.01

Time Log								
Start Date	End Date	Start Depth (ftKB)	End Depth (ftKB)	Code 1	Code 2	Dur (hr)	Phase	Com
2/21/2024 13:00	2/21/2024 15:00			General Ops	Rigging In	2.00	Well Prep	MIRU BACKDRAFT HOT OILER. HEAT FLUID, SICP 3,900 PSI, PUMP 8 BBLs HOT WATER, PRESSURE UP TO 4,500 PSI, RU B&C TEST PUMP, PUMP 12 BBL HOT WATER, PRESSURE BROKE @ 4,550 PSI, MIRU CAMERON HYDRAULIC LUBRICATOR, MU TUBING HANGER ASSEMBLY WITH BPV INSTALLED IN HANGER, LUBRICATE IN HANGER ASSEMBLY AND RUN IN LOCK DOWN PINS, BLEED PRESSURE OFF, ND HYDRAULIC LUBRICATOR, HYDRAULIC & MANUAL MASTER VALVES. NIPPLE UP PRODUCTION TREE AND TEST VOID, TEST GOOD. DRY ROD BPV OUT OF HANGER. TBG HANGER DETAIL TUBING HANGER - 7 1/16 OD X 2.875" ID 0.95 EUE PIN X EUE PIN 2.875 (2.31) XN PROFILE NIPPLE 2.875" 2" EUE PUP BXP CERAMIC DISC -----CERAMIC DISC STILL IN PLACE--- -- MULE SHOE COLLAR ON BOTOM BURST DISK STILL IN PLACE, DID NOT ATTEMPT TO BURST.
2/21/2024 15:00	2/22/2024 06:00			Standby	Well Shut In	15.00	Well Prep	WSI TURNED OVER TO PRODUCTION W/CERAMIC DISK IN PLACE
